## This electronic collection of documents is provided for the convenience of the user and is Not a Certified Document –

The documents contained herein were originally issued and sealed by the individuals whose names and license numbers appear on each page, on the dates appearing with their signature on that page.


This file or an individual page shall not be considered a certified document.

PROJECT REFERENCE NO. SHEET NO.  $W-5601DU \qquad \qquad 5$ 

SITE 21

NOT TO SCALE



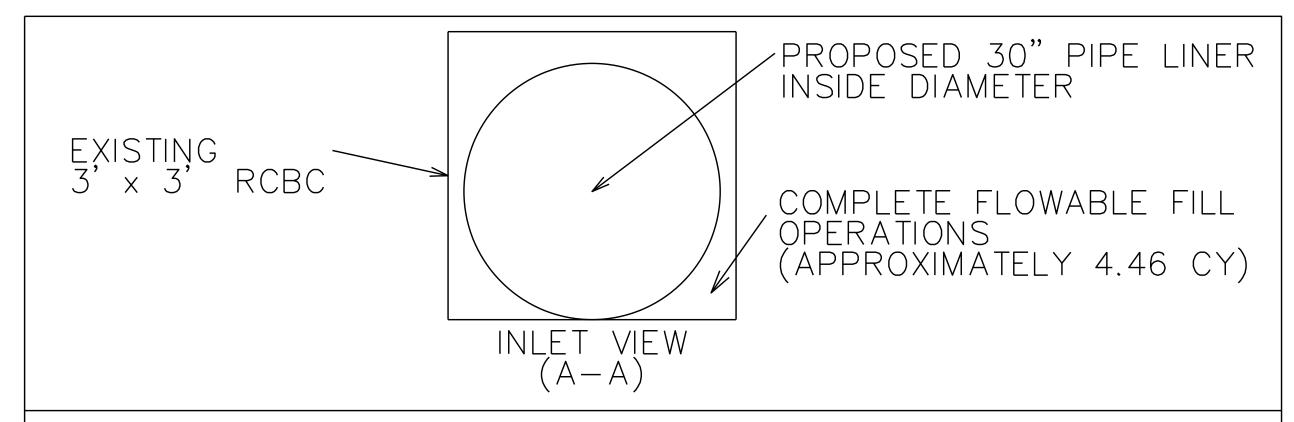

- 1) INSTALL AN IMPERVIOUS DIKE AT THE INLET END.
- 2) SEE SPECIAL PROVISION FOR PUMP AROUND OPERATIONS.
- 3)PUMP DIVERTED WATER THROUGH EXISTING RCBC MAKING SURE THE DIVERTER PIPE IS LONG ENOUGH TO BRING WATER AWAY FROM OUTLET END TO PREVENT WATER FROM BACKING UP INTO CONSTRUCTION AREA.
- 4) ALLOW INLET AND OUTLET ENDS OF RCBC TO DRY OUT.
- 5) THREAD THE WATER DIVERTER PIPE THROUGH THE LINER BEFORE INSTALLING THE LINER IN THE RCBC.

PROJECT BEGIN S21B STA 145+80 12" WATTLES W/PAM

PROJECT END S21E STA 144+53


NOTE: EXISTING PIPE TO BE EXTENDED 10', ALSO CONSTRUCT 8' SHOULDER SEE DETAIL SHEET 5-A.

LOW POINT AND OPEN END MEASURES

MUST BE INSTALLED IN ALL SILT FENCES

SEEDING AND MULCHING APPROXIMATELY .04 ACRES

EARTHWORK LOCATION	UNCLASSIFIED EXCAVATION	UNDERCUT	EMBT + %	BORROW	WASTE
SITE 21 (144+53 to 145+80) LEFT				232.23 C.Y.	

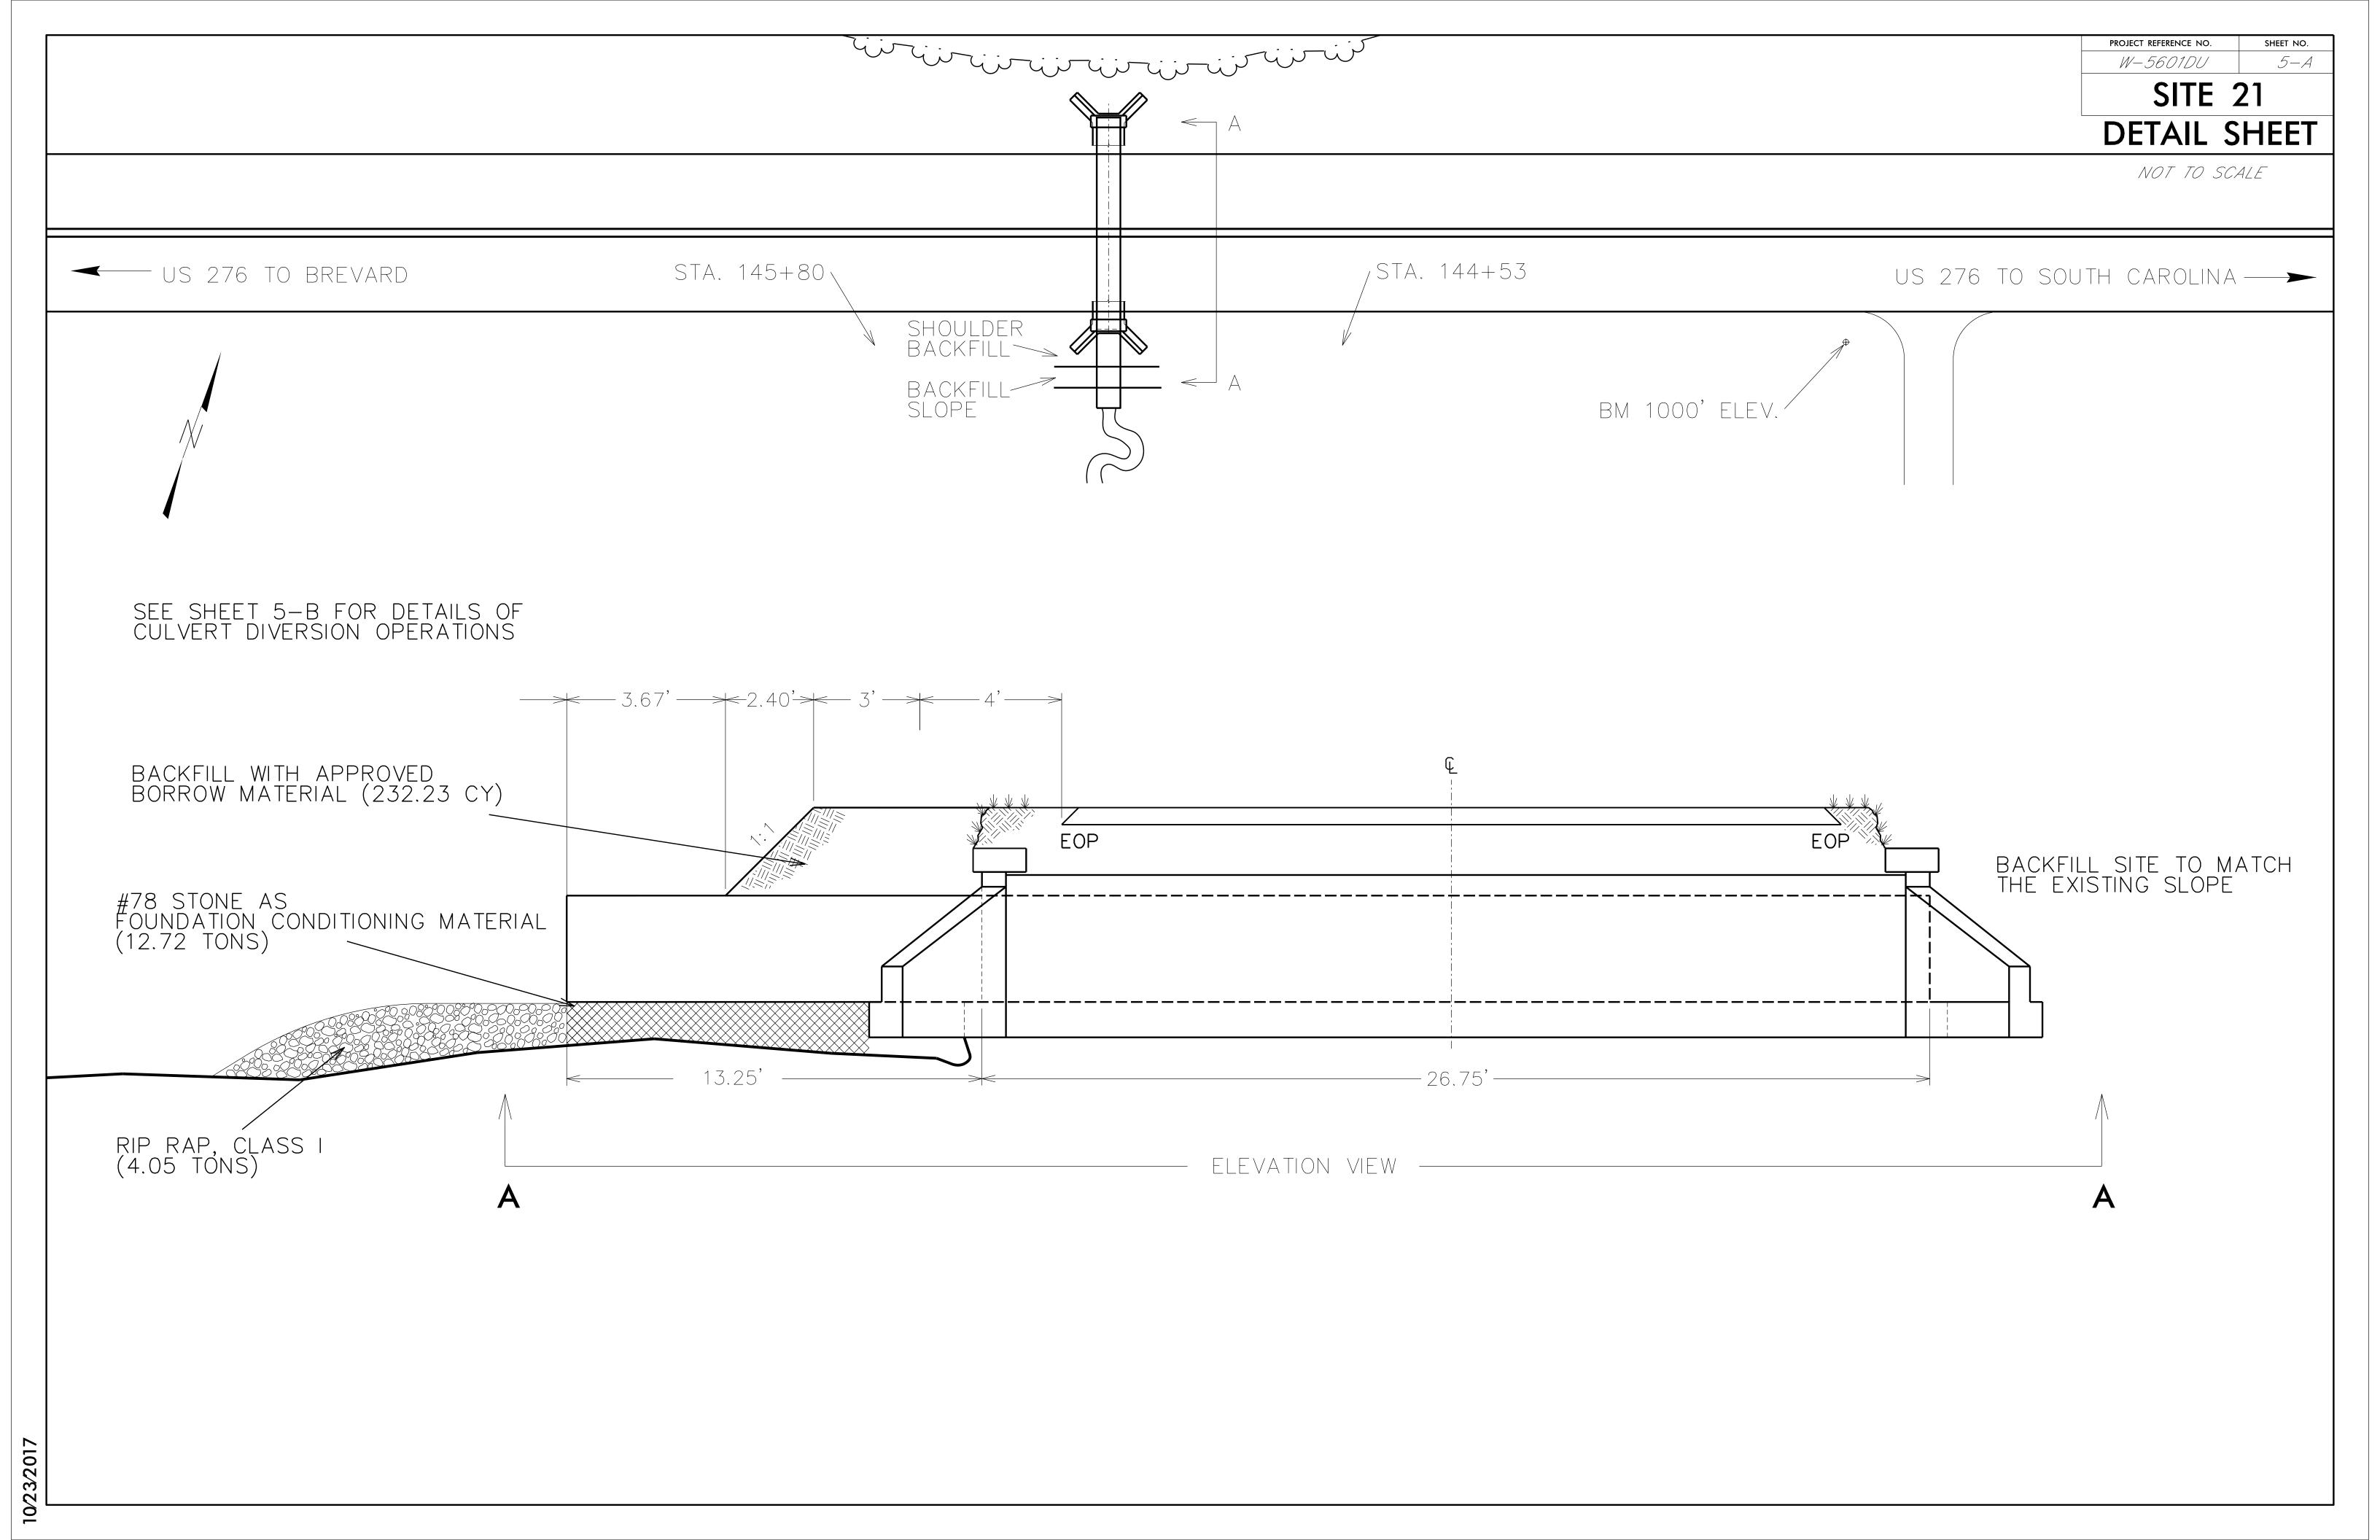


PROJECT REFERENCE NO. W-5601DU SITE 21 **DETAIL SHEET** TEMPORARY SILT FENCE \
APPROXIMATELY 300 LF 12" WATTLES W/PAM SHOULDER BACKFILL FILL SLOPE TOP OF BANK IMPERVIOUS DIKE SHOULDER BACKFILL TOP OF BANK **≫** 12" WATTLES W/PAM FILL SLOPE TYPICAL PLAN VIEW INSTALL 30" HDPE SLIP LINE PIPE TO THE FACE OF INLET FROM THE OUTLET END NOT TO SCALE OPEN END AND LOW POINT MEASURES MUST BE INSTALLED IN ALL SILT FENCES EXPOSED PIPE LINER TO BE COVERED WITH RIP RAP 10232017

PROJECT REFERENCE NO.

W-5601DU

SITE 21
DETAIL SHEET


SHEET NO.

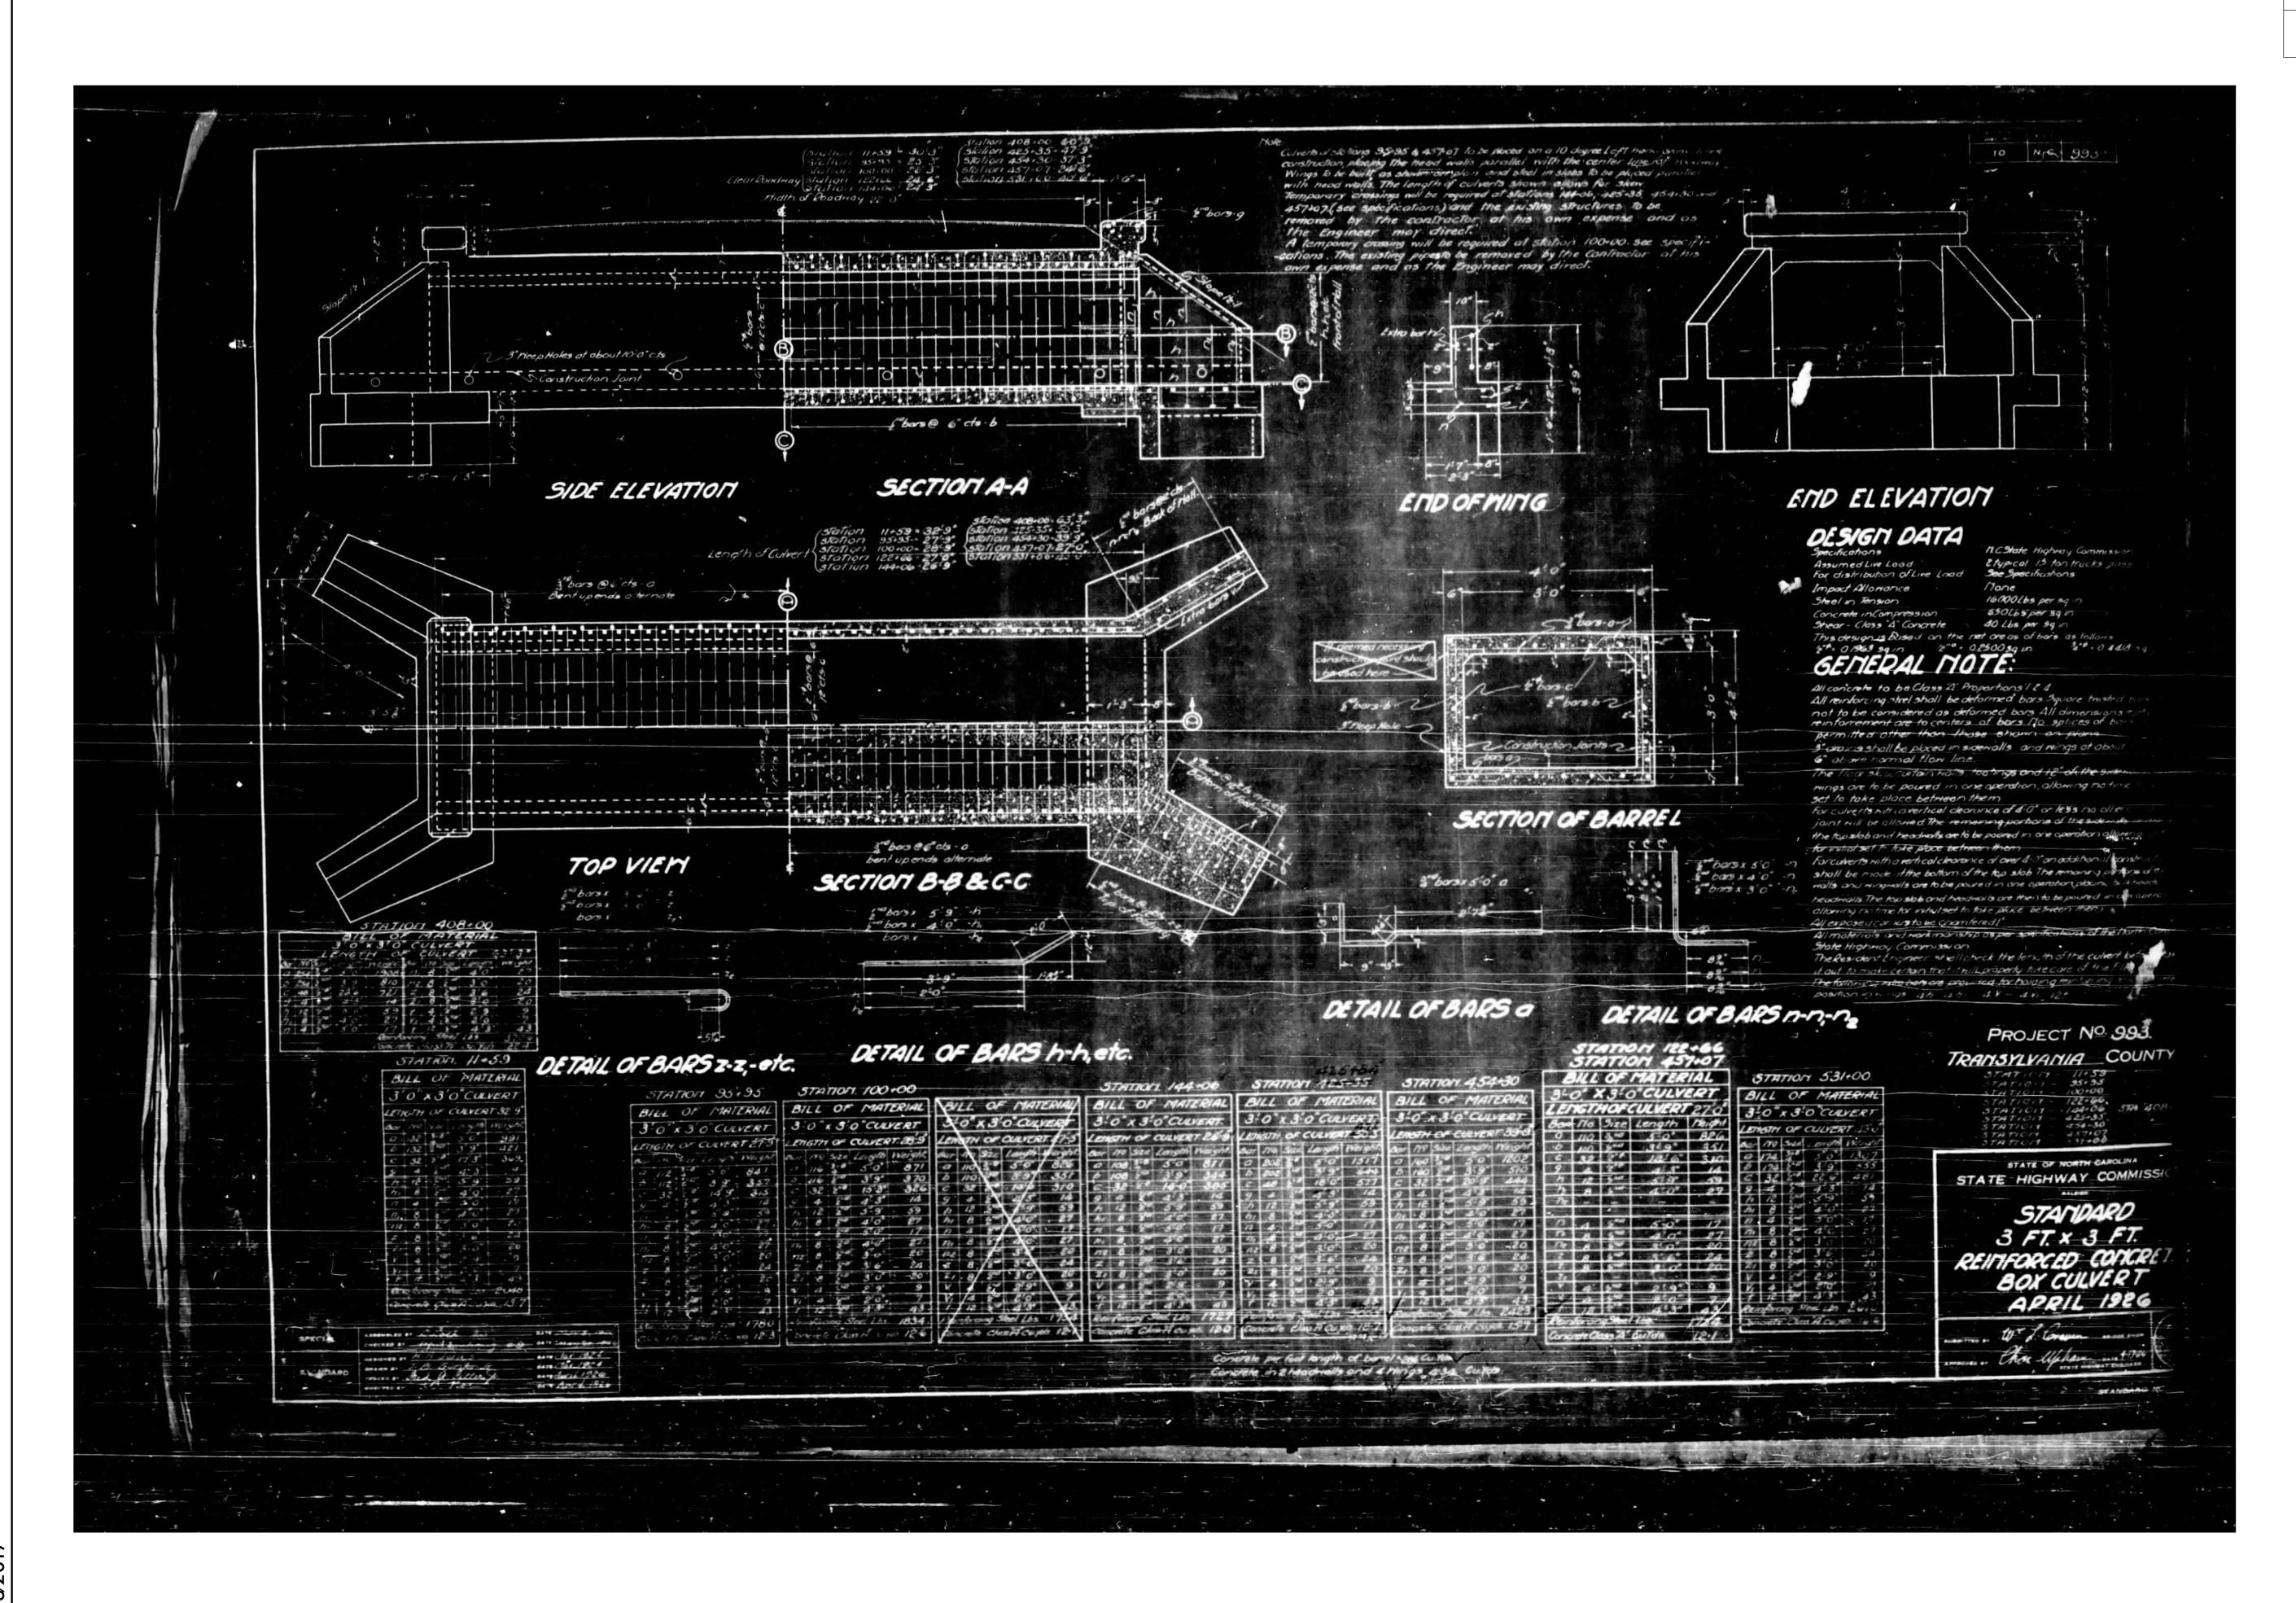

PROJECT REFERENCE NO. SHEET NO.

W-56010U 6

SITE 21B

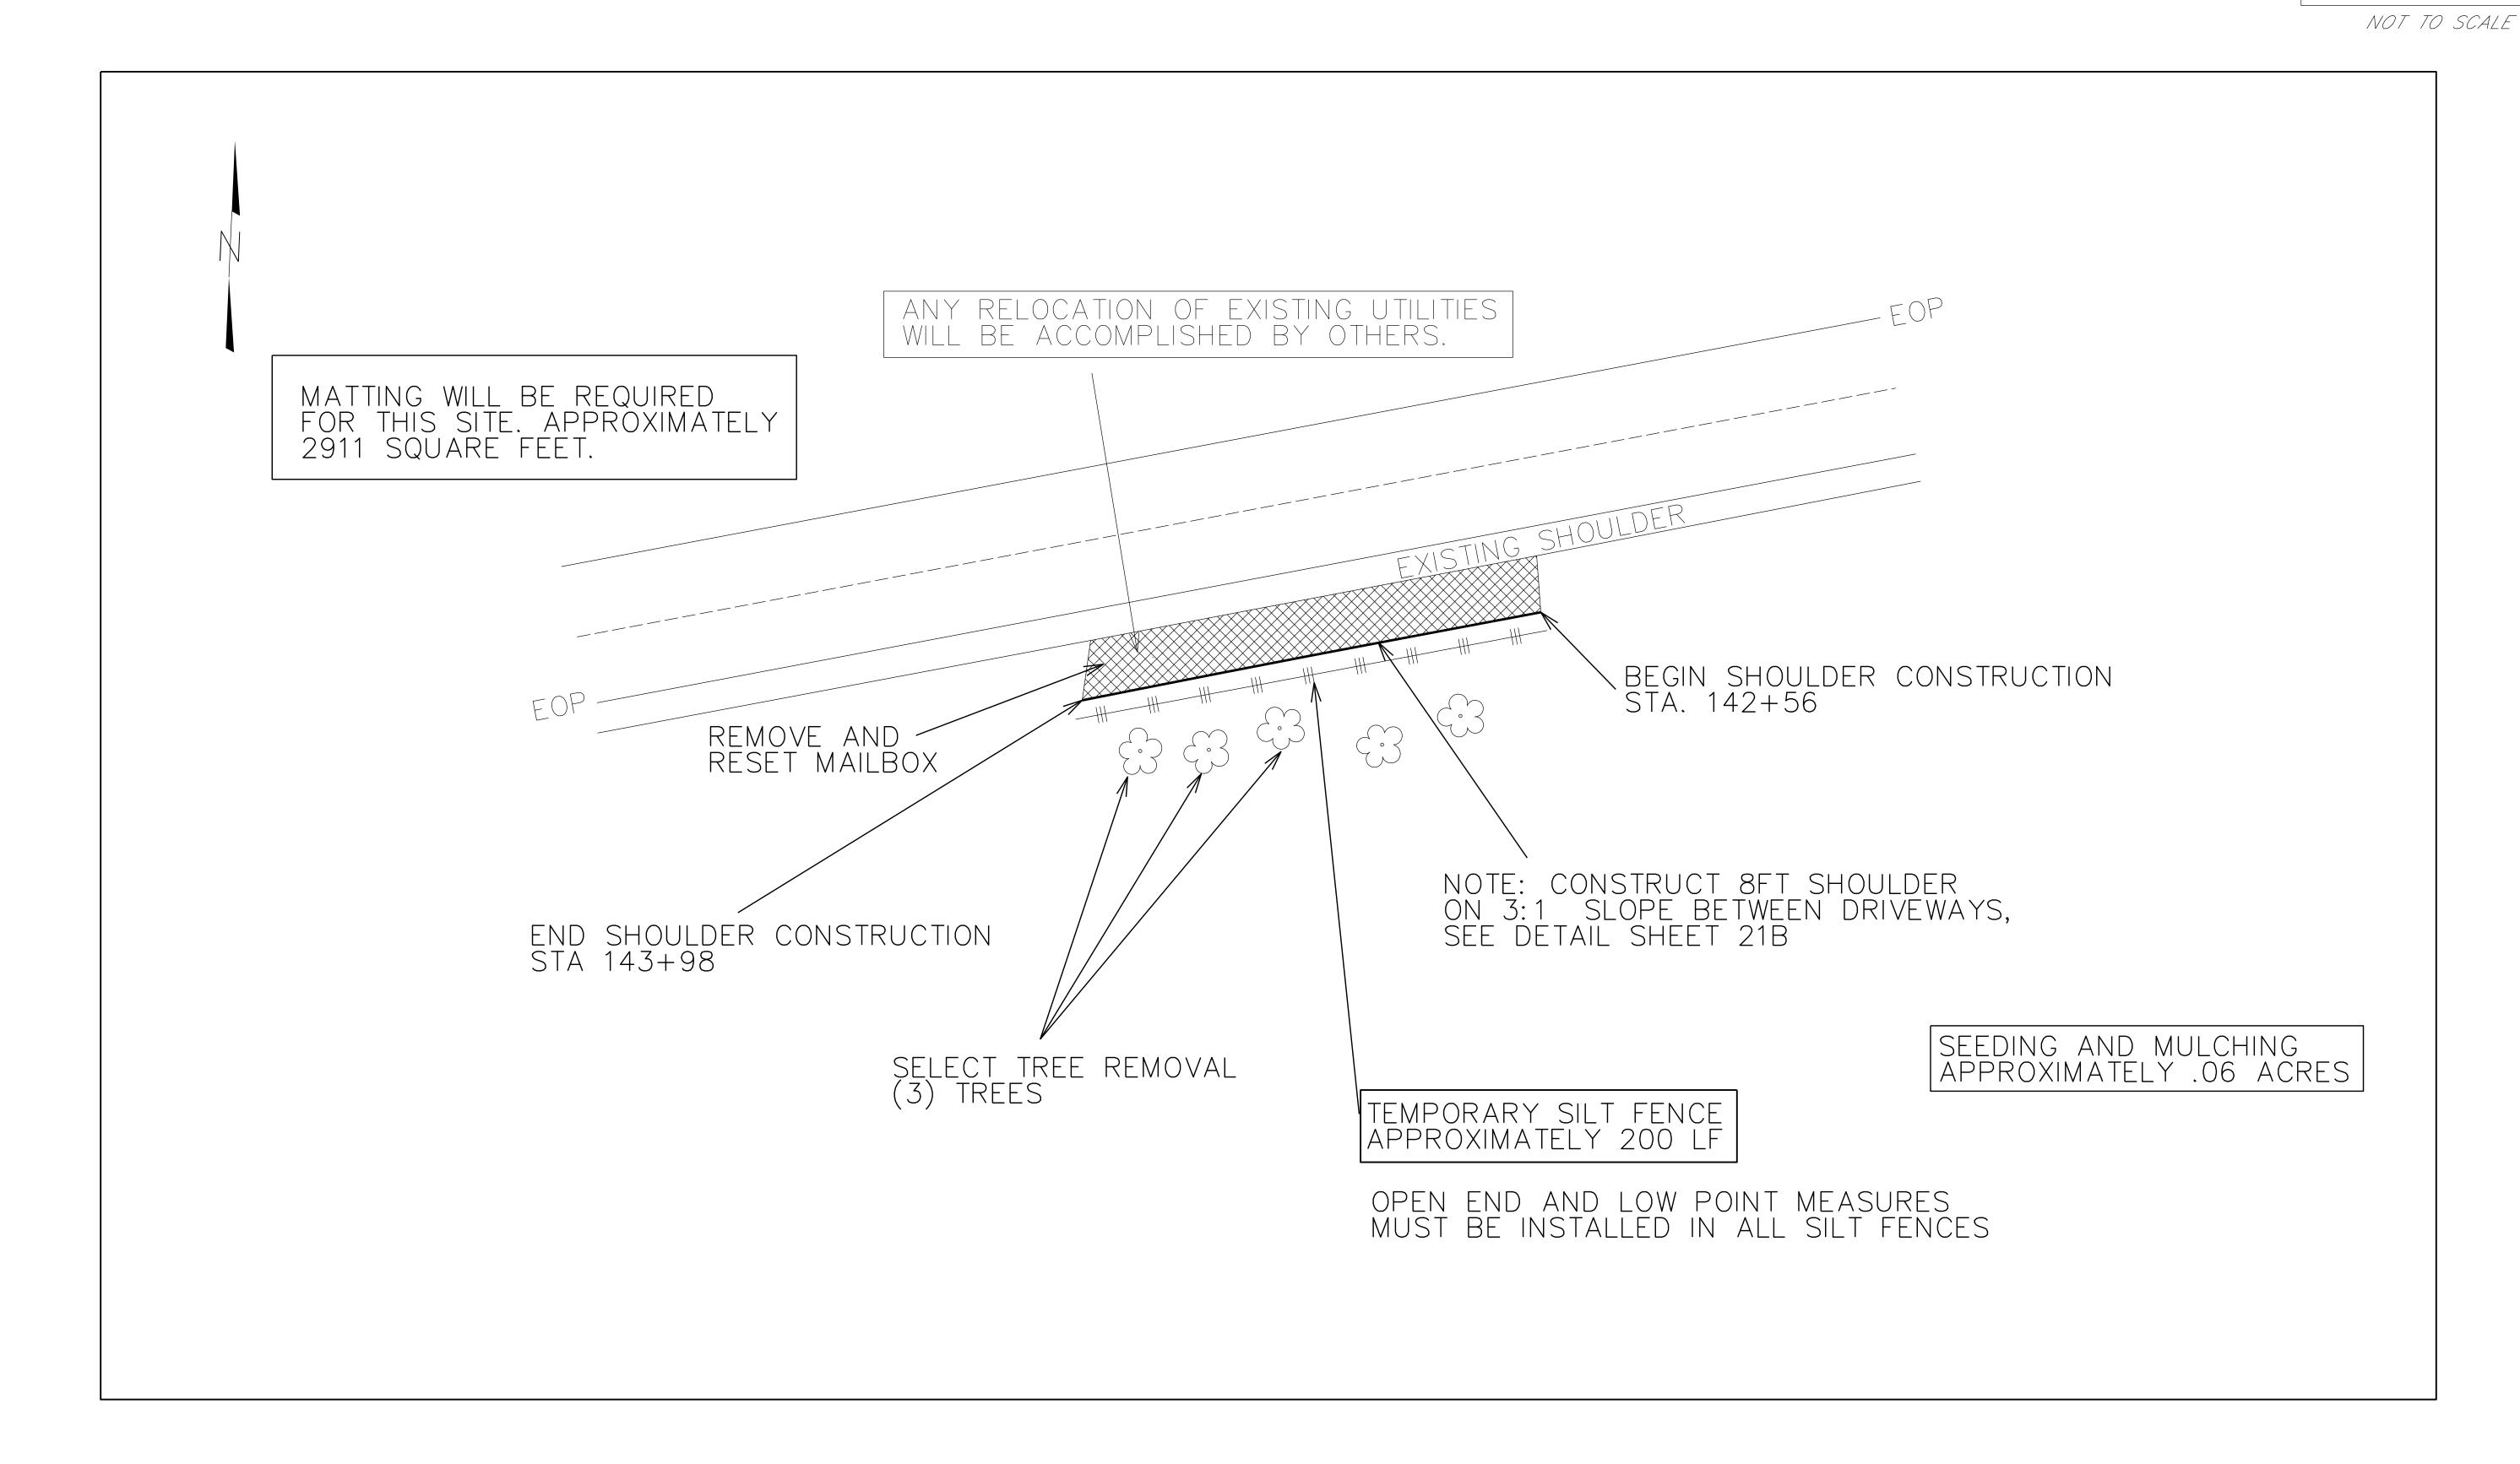


017	EARTHWORK LOCATION	UNCLASSIFIED EXCAVATION	UNDERCUT	EMBT + %	BORROW	WASTE
/23/2	SITE 21B (142+56 to 143+98) LEFT				238.30 C.Y.	

PROJECT REFERENCE NO. W-5601DU SITE 21B **DETAIL SHEET** NOT TO SCALE THIS SITE WILL REQUIRE APPROXIMATELY 3692 SQUARE FEET OF MATTING THIS SITE WILL REQUIRE APPROXIMATELY 200 LINEAR FEET OF SILT FENCE IMAGE VIEW NOT TO SCALE PLAN VIEW NOT TO SCALE ROAD BACKFILL WITH (238.30 CY) APPROVED BORROW MATERIAL SECTION A-A NOT TO SCALE 10/23/2017

PROJECT REFERENCE NO. SHOW—5601DU

SITE 29

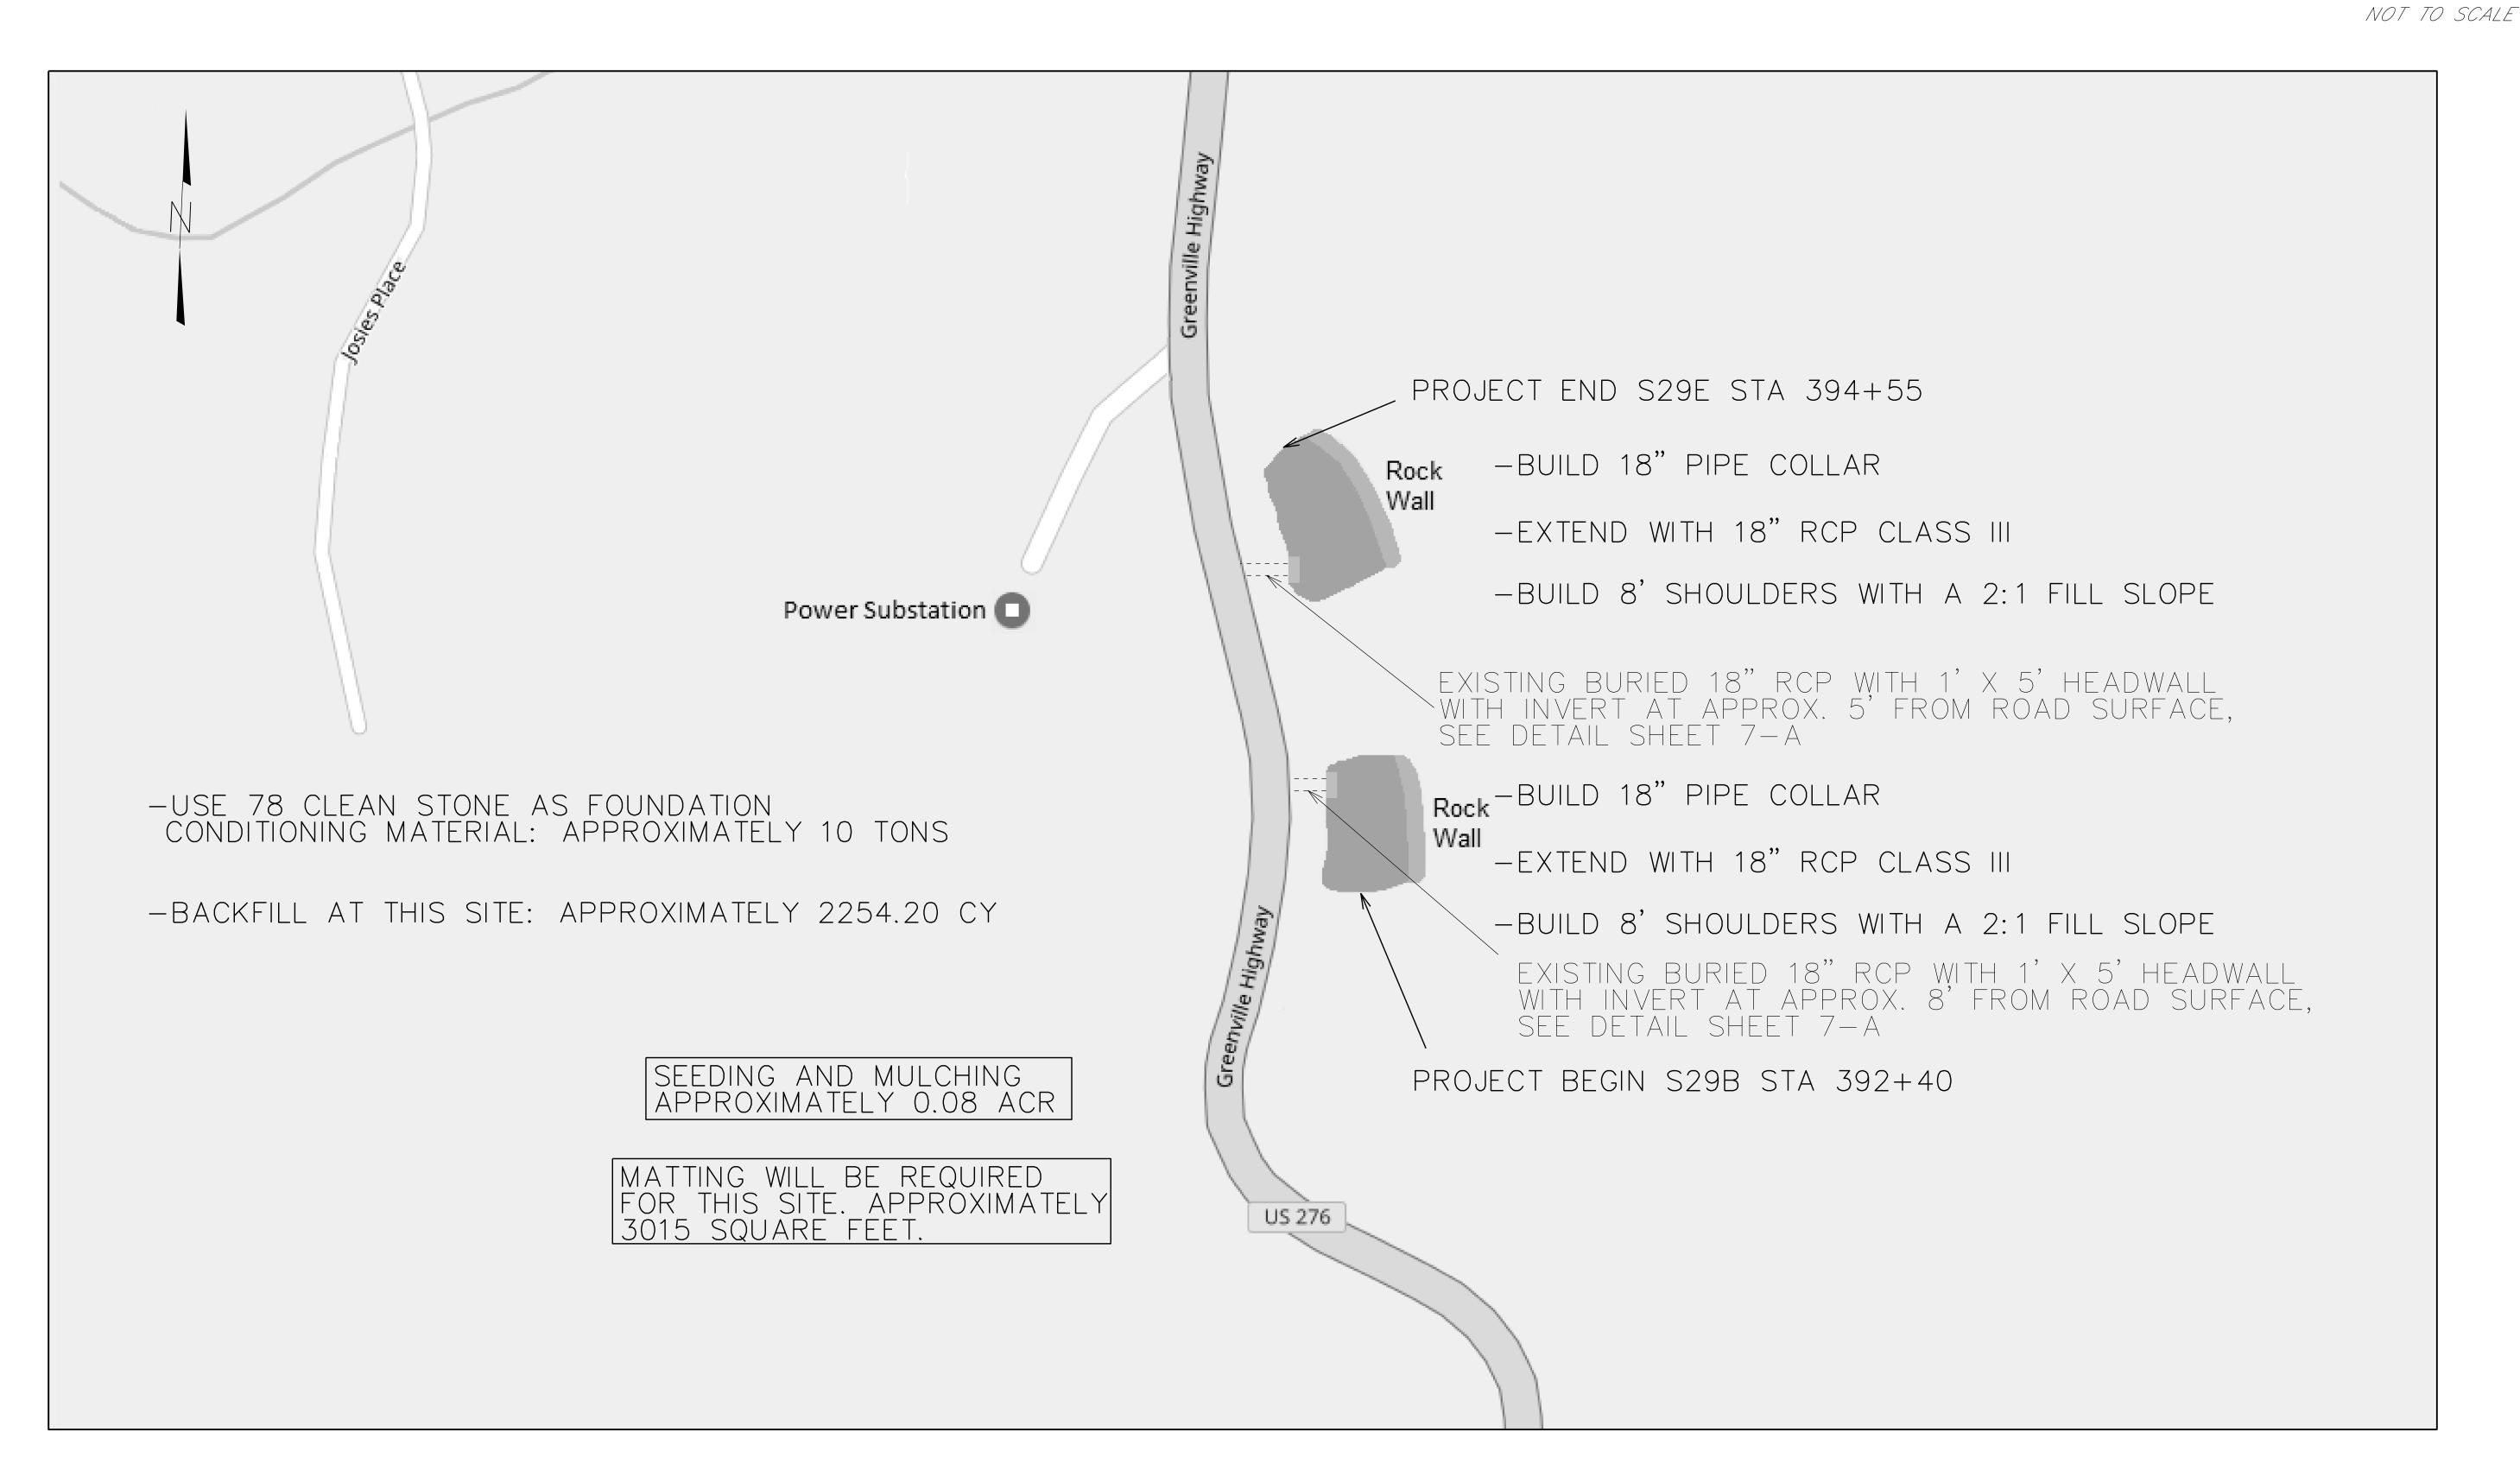

EARTHWORK LOCATION	UNCLASSIFIED EXCAVATION	UNDERCUT	EMBT + %	BORROW	WASTE	
SITE 29 (392+40 to 394+55) RIGHT				2254.20 C.Y.		

