


**PROJECT: 11C.014098**

15-JUN-2018 07:41 R:\Road Projects\Secondary\Caldwell\SR1958 Lacey Road\EC Plan Sheets\SR1958\_EC\_1.sh.dgn

VICINITY MAP

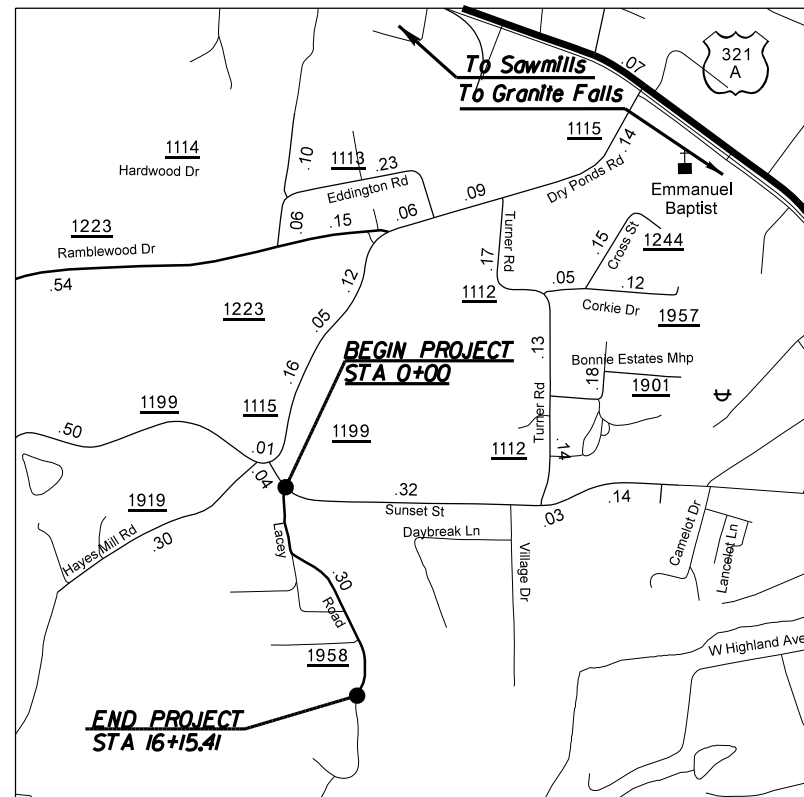

STATE OF NORTH CAROLINA  
DIVISION OF HIGHWAYS  
PLAN FOR PROPOSED  
HIGHWAY EROSION CONTROL  
**CALDWELL COUNTY**

**LOCATION: SR 1958 LACEY ROAD FROM  
SR 1199 SUNSET STREET TO E.O.P.  
STA 0+00 TO EOP STA 16+15.41  
TYPE OF WORK: GRADING, DRAINAGE, BASE  
AND PAVING - 0.31 MILES**

STATE	STATE PROJECT REFERENCE NO.	SHEET NO.	TOTAL SHEETS
N.C.	11C.014098	EC-1	13
STATE PROJ. NO.	F.A. PROJ. NO.	DESCRIPTION	

**EROSION AND SEDIMENT CONTROL MEASURES**

Std. #	Description	Symbol
1630.03	Temporary Silt Ditch	
1630.05	Temporary Diversion	
1605.01	Temporary Silt Fence	
1606.01	Special Sediment Control Fence	
1622.01	Temporary Berms and Slope Drains	
1630.02	Silt Basin Type B	
1633.01	Temporary Rock Silt Check Type-A	
	Temporary Rock Silt Check Type-A with Matting and Polyacrylamide (PAM)	
1633.02	Temporary Rock Silt Check Type-B	
	Wattle/Coir Fiber Wattle	
	Wattle/Coir Fiber Wattle with Polyacrylamide (PAM)	
1634.01	Temporary Rock Sediment Dam Type-A	
1634.02	Temporary Rock Sediment Dam Type-B	
1635.01	Rock Pipe Inlet Sediment Trap Type-A	
1635.02	Rock Pipe Inlet Sediment Trap Type-B	
1630.04	Stilling Basin	
1630.06	Special Stilling Basin	
	Rock Inlet Sediment Trap:	
1632.01	Type A	
1632.02	Type B	
1632.03	Type C	
	Skimmer Basin	
	Tiered Skimmer Basin	
	Infiltration Basin	


Porous Baffle Spacing  
\*Baffles in Silt Basins at drainage turnouts and all other temporary rock sediment dams-Type B:  
-If basin length=10' or less;1 baffle  
-If basin length=11' to 20';2 baffles  
-If basin length=20' or more;3 baffles equally spaced in basin

NOTE: PERIMETER EROSION CONTROL MEASURES SHALL BE INSTALLED DURING CLEARING AND GRUBBING PHASE.

THIS PROJECT CONTAINS  
EROSION CONTROL PLANS  
FOR CLEARING AND  
GRUBBING PHASE OF  
CONSTRUCTION.

Level III Cert # 3474

**GRAPHIC SCALE**



ROADSIDE ENVIRONMENTAL UNIT  
DIVISION OF HIGHWAYS  
STATE OF NORTH CAROLINA

THESE EROSION AND SEDIMENT CONTROL PLANS COMPLY  
WITH THE REGULATIONS SET FORTH BY THE  
NCG-010000 GENERAL CONSTRUCTION PERMIT EFFECTIVE AUGUST 3, 2011  
ISSUED BY THE NORTH CAROLINA DEPARTMENT OF ENVIRONMENT AND  
NATURAL RESOURCES DIVISION OF WATER QUALITY.

Prepared in the Office of:  
**DIVISION OF HIGHWAYS**  
DIVISION 11, DISTRICT 2 BOONE  
P.O. BOX 1460, BOONE, N.C. 28607  
**2018 STANDARD SPECIFICATIONS**

Roadway Standard Drawings

The following roadway english standards as appear in "Roadway Standard Drawings"- Roadway Design Unit - N. C. Department of Transportation - Raleigh, N. C., dated January 2012 and the latest revision thereto are applicable to this project and by reference hereby are considered a part of these plans.

1604.01 Railroad Erosion Control Detail	1632.01 Rock Inlet Sediment Trap Type A
1605.01 Temporary Silt Fence	1632.02 Rock Inlet Sediment Trap Type B
1606.01 Special Sediment Control Fence	1632.03 Rock Inlet Sediment Trap Type C
1607.01 Gravel Construction Entrance	1633.01 Temporary Rock Silt Check Type A
1622.01 Temporary Berms and Slope Drains	1633.02 Temporary Rock Silt Check Type B
1630.01 Riser Basin	1634.01 Temporary Rock Sediment Dam Type A
1630.02 Silt Basin Type B	1634.02 Temporary Rock Sediment Dam Type B
1630.03 Temporary Silt Ditch	1635.01 Rock Pipe Inlet Sediment Trap Type A
1630.04 Stilling Basin	1635.02 Rock Pipe Inlet Sediment Trap Type B
1630.05 Temporary Diversion	1640.01 Coir Fiber Baffle
1630.06 Special Stilling Basin	1645.01 Temporary Stream Crossing
1631.01 Matting Installation	

# EROSION CONTROL & PIPE INSTALLATION SCHEDULE

## TROUT BUFFER ZONE SEQUENCE

### GENERAL E&SC NOTES

### GROUND STABILIZATION CHART

#### Erosion Control Schedule and Notes

1. Generally, the order of installation of the erosion control measures will be as follows:
  - A. Temporary silt basins shall be installed before clearing and grubbing begins.
  - B. Silt fences and temporary silt ditches shall be installed after clearing and before grading.
  - C. Temporary stone ditch checks with PAM or wattles with PAM shall be installed in all disturbed areas as soon as the disturbance begins.
  - D. Final stone ditch checks or wattles shall be installed as soon as ditch line is established.
  - E. Pipe outlet and inlet protection will be done as soon as the pipe is installed.
  - F. Other permanent erosion control measures are to be implemented as soon as practical.
2. Temporary rock silt checks, type B will be spaced by percent grade as shown in the erosion control plan.
3. No. 5 stone, or equivalent, will be used in conjunction with the temporary rock silt checks in locations where water is leaving the project or entering a pipe.
4. All devices are to be cleaned out when half full.
5. Establish permanent vegetation per ground stabilization chart.

**Notes:**

For silt basin size see the attached erosion control plans.

PAM is to be placed on all Type A checks and wattles in the erosion control chain except for the final device in HWQ and Trout projects.

#### Wet Pipe Installation Schedule and Notes

1. Prior to installing any E&SC measures identify permit conditions and impact area limits.
2. Install erosion control devices.
3. Manage the water course. The pipe must be placed in the dry. Install dewatering measures.
4. Remove material and existing pipe while limiting material and sediment from entering stream and escaping the project.
5. Excavation of stream channel shall not exceed 10' on either side of new pipe or culvert unless indicated on permit.
6. Per permit conditions for Corps of Engineers and the Wildlife Resources Commission, all pipes in streams 48" or greater must be buried 12" below streambed elevation. Pipes less than 48" must be buried with 20% of the diameter below streambed elevation.
7. Place the new pipe and compact backfill.
8. Install slope protection on the outlet and inlet ends of the pipe. Also complete installation of erosion control measures and perform maintenance as needed on existing measures.
9. Establish permanent vegetation per ground stabilization chart.
10. More information on wet pipe installation can be found in the BMP manual section 4.2 "Pipe & Culvert installation"

#### General Erosion Control Sequence & Notes for NC DOT Projects in Trout Buffer Zones

1. Prior to installing any E&SC measures identify permit conditions and impact area limits. Review trout buffer variance approval conditions for any special provisions.
2. All materials should be on the hand before work is commenced.
3. Install EC devices
4. Work within the buffer zone should be sequenced to minimize the length of time that disturbed areas are exposed. Stream bank stabilization, which includes the area from the edge of water to the top of bank, should be phased so that each day's work is a completed work, including provision of adequate ground cover.
5. Graded slopes and fills within the trout buffer zone will within 7 calendar days of completion of any phase of grading be planted or otherwise provided with temporary or permanent ground cover, devices, or structures sufficient to restrain erosion.
6. Graded slopes and fills within the trout buffer zone (excluding road shoulders) shall be protected with rolled erosion control product, bonded fiber matrix, or flexible growth medium after seeding.

**Notes:**

Silt fence backed by woven wire, with a post spacing of 6 feet, shall be used instead of standard silt fence in trout buffer zone. Special sediment control fence shall be used in areas where bedrock is encountered which prohibits the proper anchoring of fabric, and in low points of the silt fence in 3-foot sections to allow for concentrated flows.

The disturbed areas within the stream buffer shall be restored to native vegetation characteristic of an undisturbed buffer to the extent practical upon completion of construction.

Flyrock protection such as blast mats should be provided for blasting in close proximity to streams.


PAM is to be placed on all Type A checks and wattles in the erosion control chain except for the final device in HWQ and Trout projects.

**GROUND STABILIZATION CHART**


Site Area Description	Stabilization Time Frame	Stabilization Time Frame Exceptions
Perimeter dikes, swales, ditches and slopes	7 days	None
High Quality Water Zones	7 days	None
Slopes steeper than 3:1	7 days	If slopes are 10 ft. or less in length and are not steeper than 2:1, 14 days are allowed
Slopes 3:1 or flatter	14 days	7 days for slopes greater than 50' in length
All other areas flatter than 4:1	14 days	None (except for perimeters and HQW zones)

6/2/99

PROJECT REFERENCE NO.	SHEET NO.
11C.014098	2
ROADWAY DESIGN ENGINEER	PAVEMENT DESIGN ENGINEER

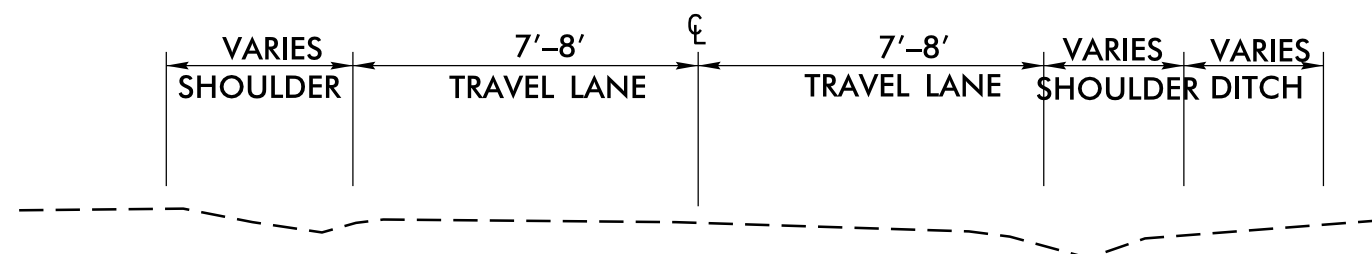


**14'-16' EXISTING TYPICAL SECTION**

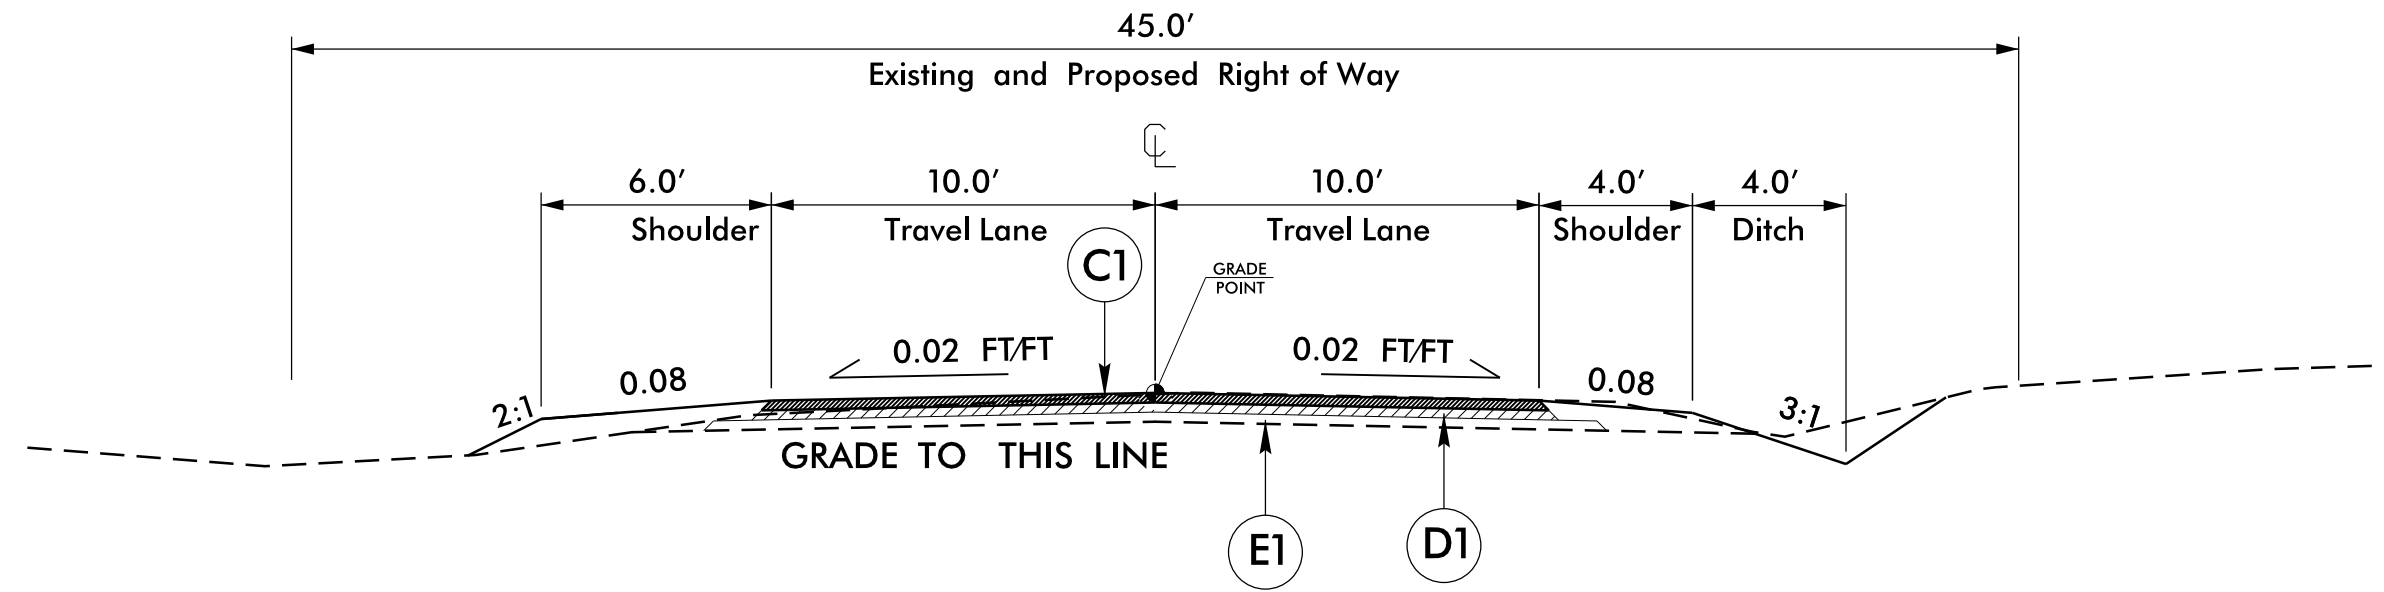

**TYPICAL SECTION NO. 1**

\*Sta. 0+00 to 15+17.34




<b>C1</b>	PROP. ASPHALT SURFACE TREATMENT (TRIPLE SEAL).
<b>D1</b>	PROP. APPROX. 3" ASPHALT CONCRETE INTERMEDIATE COURSE, TYPE I19.0C, AT AN AVERAGE RATE OF 342 LBS. PER SQ. YD.
<b>E1</b>	PROP. APPROX. 6" AGGREGATE BASE COURSE.

I:\JUN-2008\_07-41  
 R:\Road\Projects\Secondary\Caldwell\SR1958 Lacey Road\EC Plan Sheets\col1958\_typ\_2.dgn  
 \$\$\$\$USFHNSM\$\$\$


6/2/99  
 I:\JUN-2008\_07-41  
 R:\Road\Projects\Secondary\Caldwell\SR1958 Lacey Road\EC work\EC Plan Sheets\c01958\_typ\_2.dgn  
 \$\$\$\$USFENB\$\$\$\$

PROJECT REFERENCE NO.	SHEET NO.
11C.014098	2A
ROADWAY DESIGN ENGINEER	PAVEMENT DESIGN ENGINEER

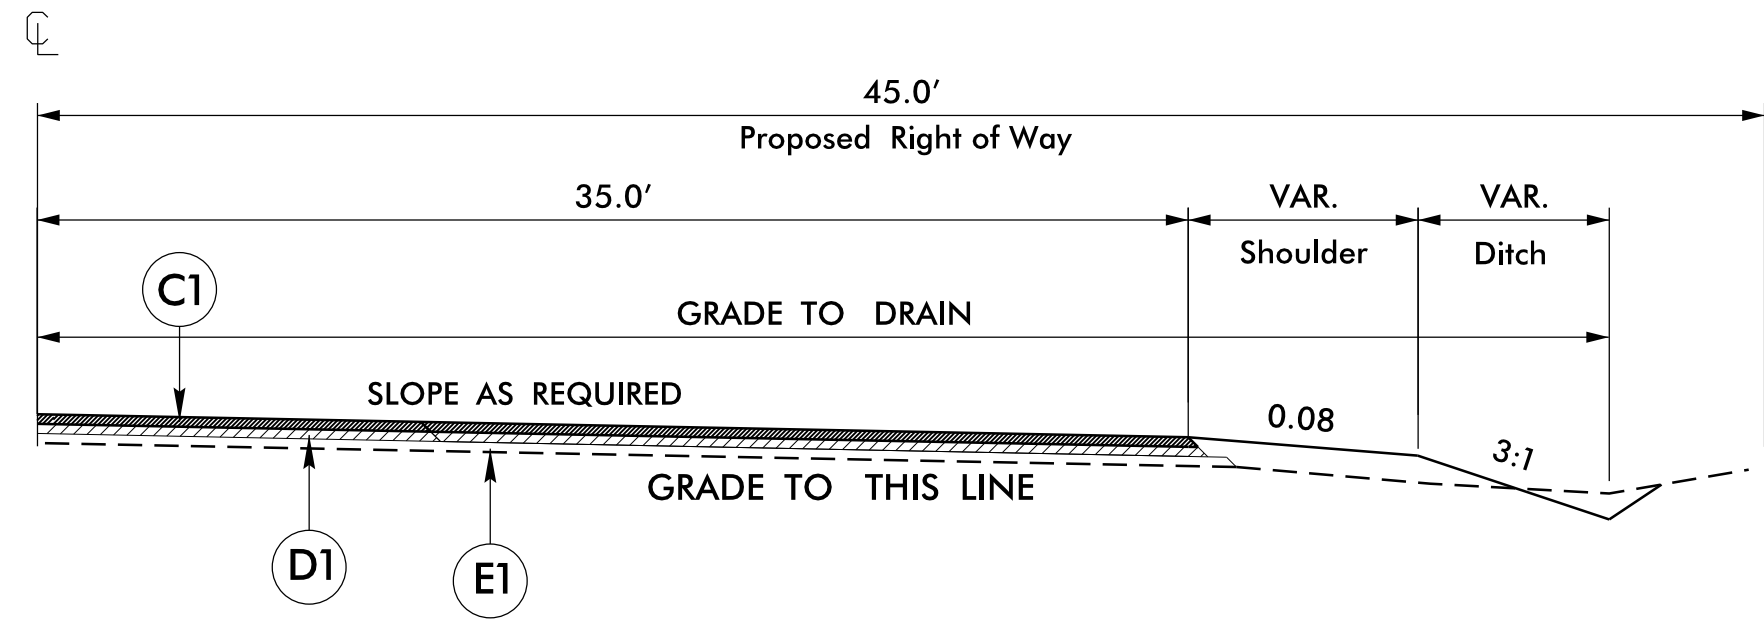

## TYPICAL SECTION NO. 2

CUL-DE-SAC TYPICAL  
 \*Sta. 15+17.34 to 16+13.75



<b>C1</b>	PROP. ASPHALT SURFACE TREATMENT (TRIPLE SEAL).
<b>D1</b>	PROP. APPROX. 3" ASPHALT CONCRETE INTERMEDIATE COURSE, TYPE I19.0C, AT AN AVERAGE RATE OF 342 LBS. PER SQ. YD.
<b>E1</b>	PROP. APPROX. 6" AGGREGATE BASE COURSE.



DIVISION OF HIGHWAYS  
STATE OF NORTH CAROLINA


PROJECT REFERENCE NO.	SHEET NO.
<i>11C.014098</i>	<i>EC-3B</i>
ROADWAY DESIGN ENGINEER	HYDRAULICS ENGINEER

# ***SOIL STABILIZATION TIMEFRAMES***

<i>SITE DESCRIPTION</i>	<i>STABILIZATION TIME</i>	<i>TIMEFRAME EXCEPTIONS</i>
PERIMETER DIKES, SWALES, DITCHES AND SLOPES	7 DAYS	NONE
HIGH QUALITY WATER (HOW) ZONES	7 DAYS	NONE
SLOPES STEEPER THAN 3:1	7 DAYS	IF SLOPES ARE 10' OR LESS IN LENGTH AND ARE NOT STEEPER THAN 2:1, 14 DAYS ARE ALLOWED.
SLOPES 3:1 OR FLATTER	14 DAYS	7 DAYS FOR SLOPES GREATER THAN 50' IN LENGTH.
ALL OTHER AREAS WITH SLOPES FLATTER THAN 4:1	14 DAYS	NONE, EXCEPT FOR PERIMETERS AND HOW ZONES.


PROJECT REFERENCE NO.	SHEET NO.
11C.014098	EC-4
RW SHEET NO.	
ROADWAY DESIGN ENGINEER	HYDRAULICS ENGINEER

8/17/99  
 REVISIONS  
 15-JUN-2018 07:41  
 R:\Roads\Projects\Secondary\Caldwell\SR1958 Lacey Road\EC work\EC Plan Sheets\EC-4.dgn  
 \$\$\$USE ENGLISH \$\$\$

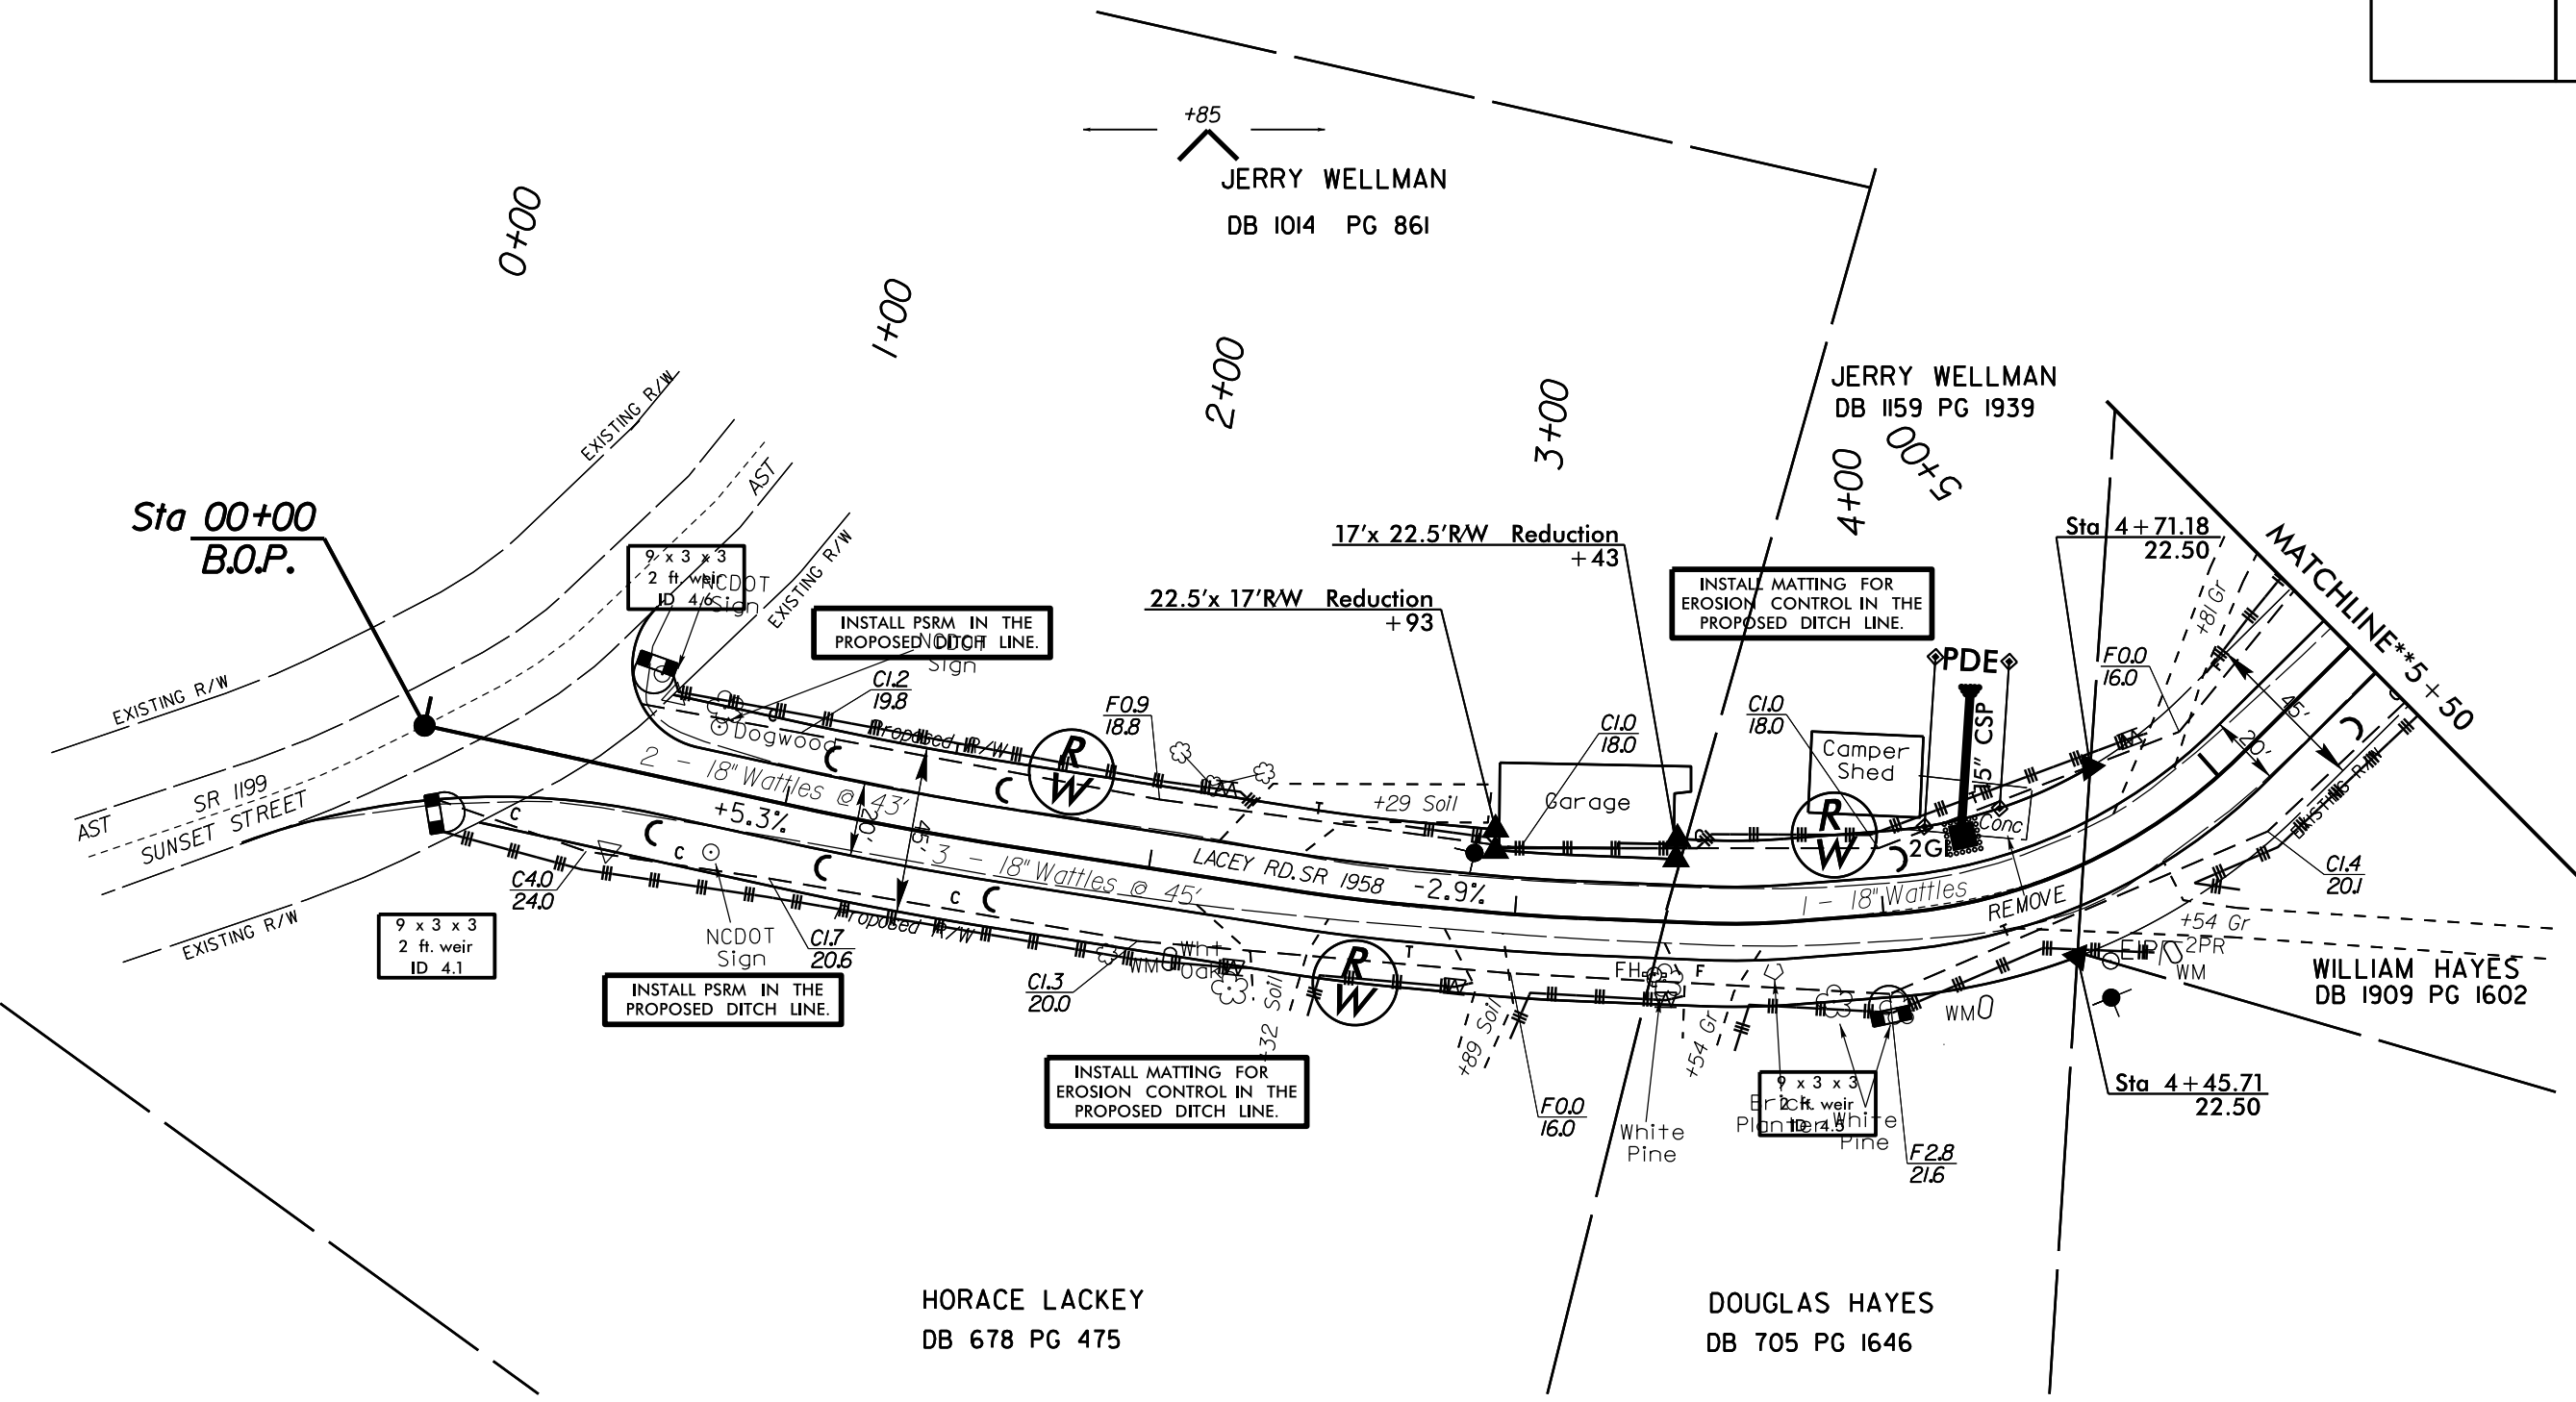

PROJECT REFERENCE NO.	SHEET NO.
11C.014098	EC-5
RW SHEET NO.	
ROADWAY DESIGN ENGINEER	HYDRAULICS ENGINEER

8/17/99  
 REVISIONS  
 15-JUN-2018 07:41  
 R:\Roads\Projects\Secondary\Caldwell11\SR1958\_Lacey Road\EC\_work\EC\_Plan\_Sheets\EC-5.dgn  
 \$\$\$USE ENVELOPE \$\$\$

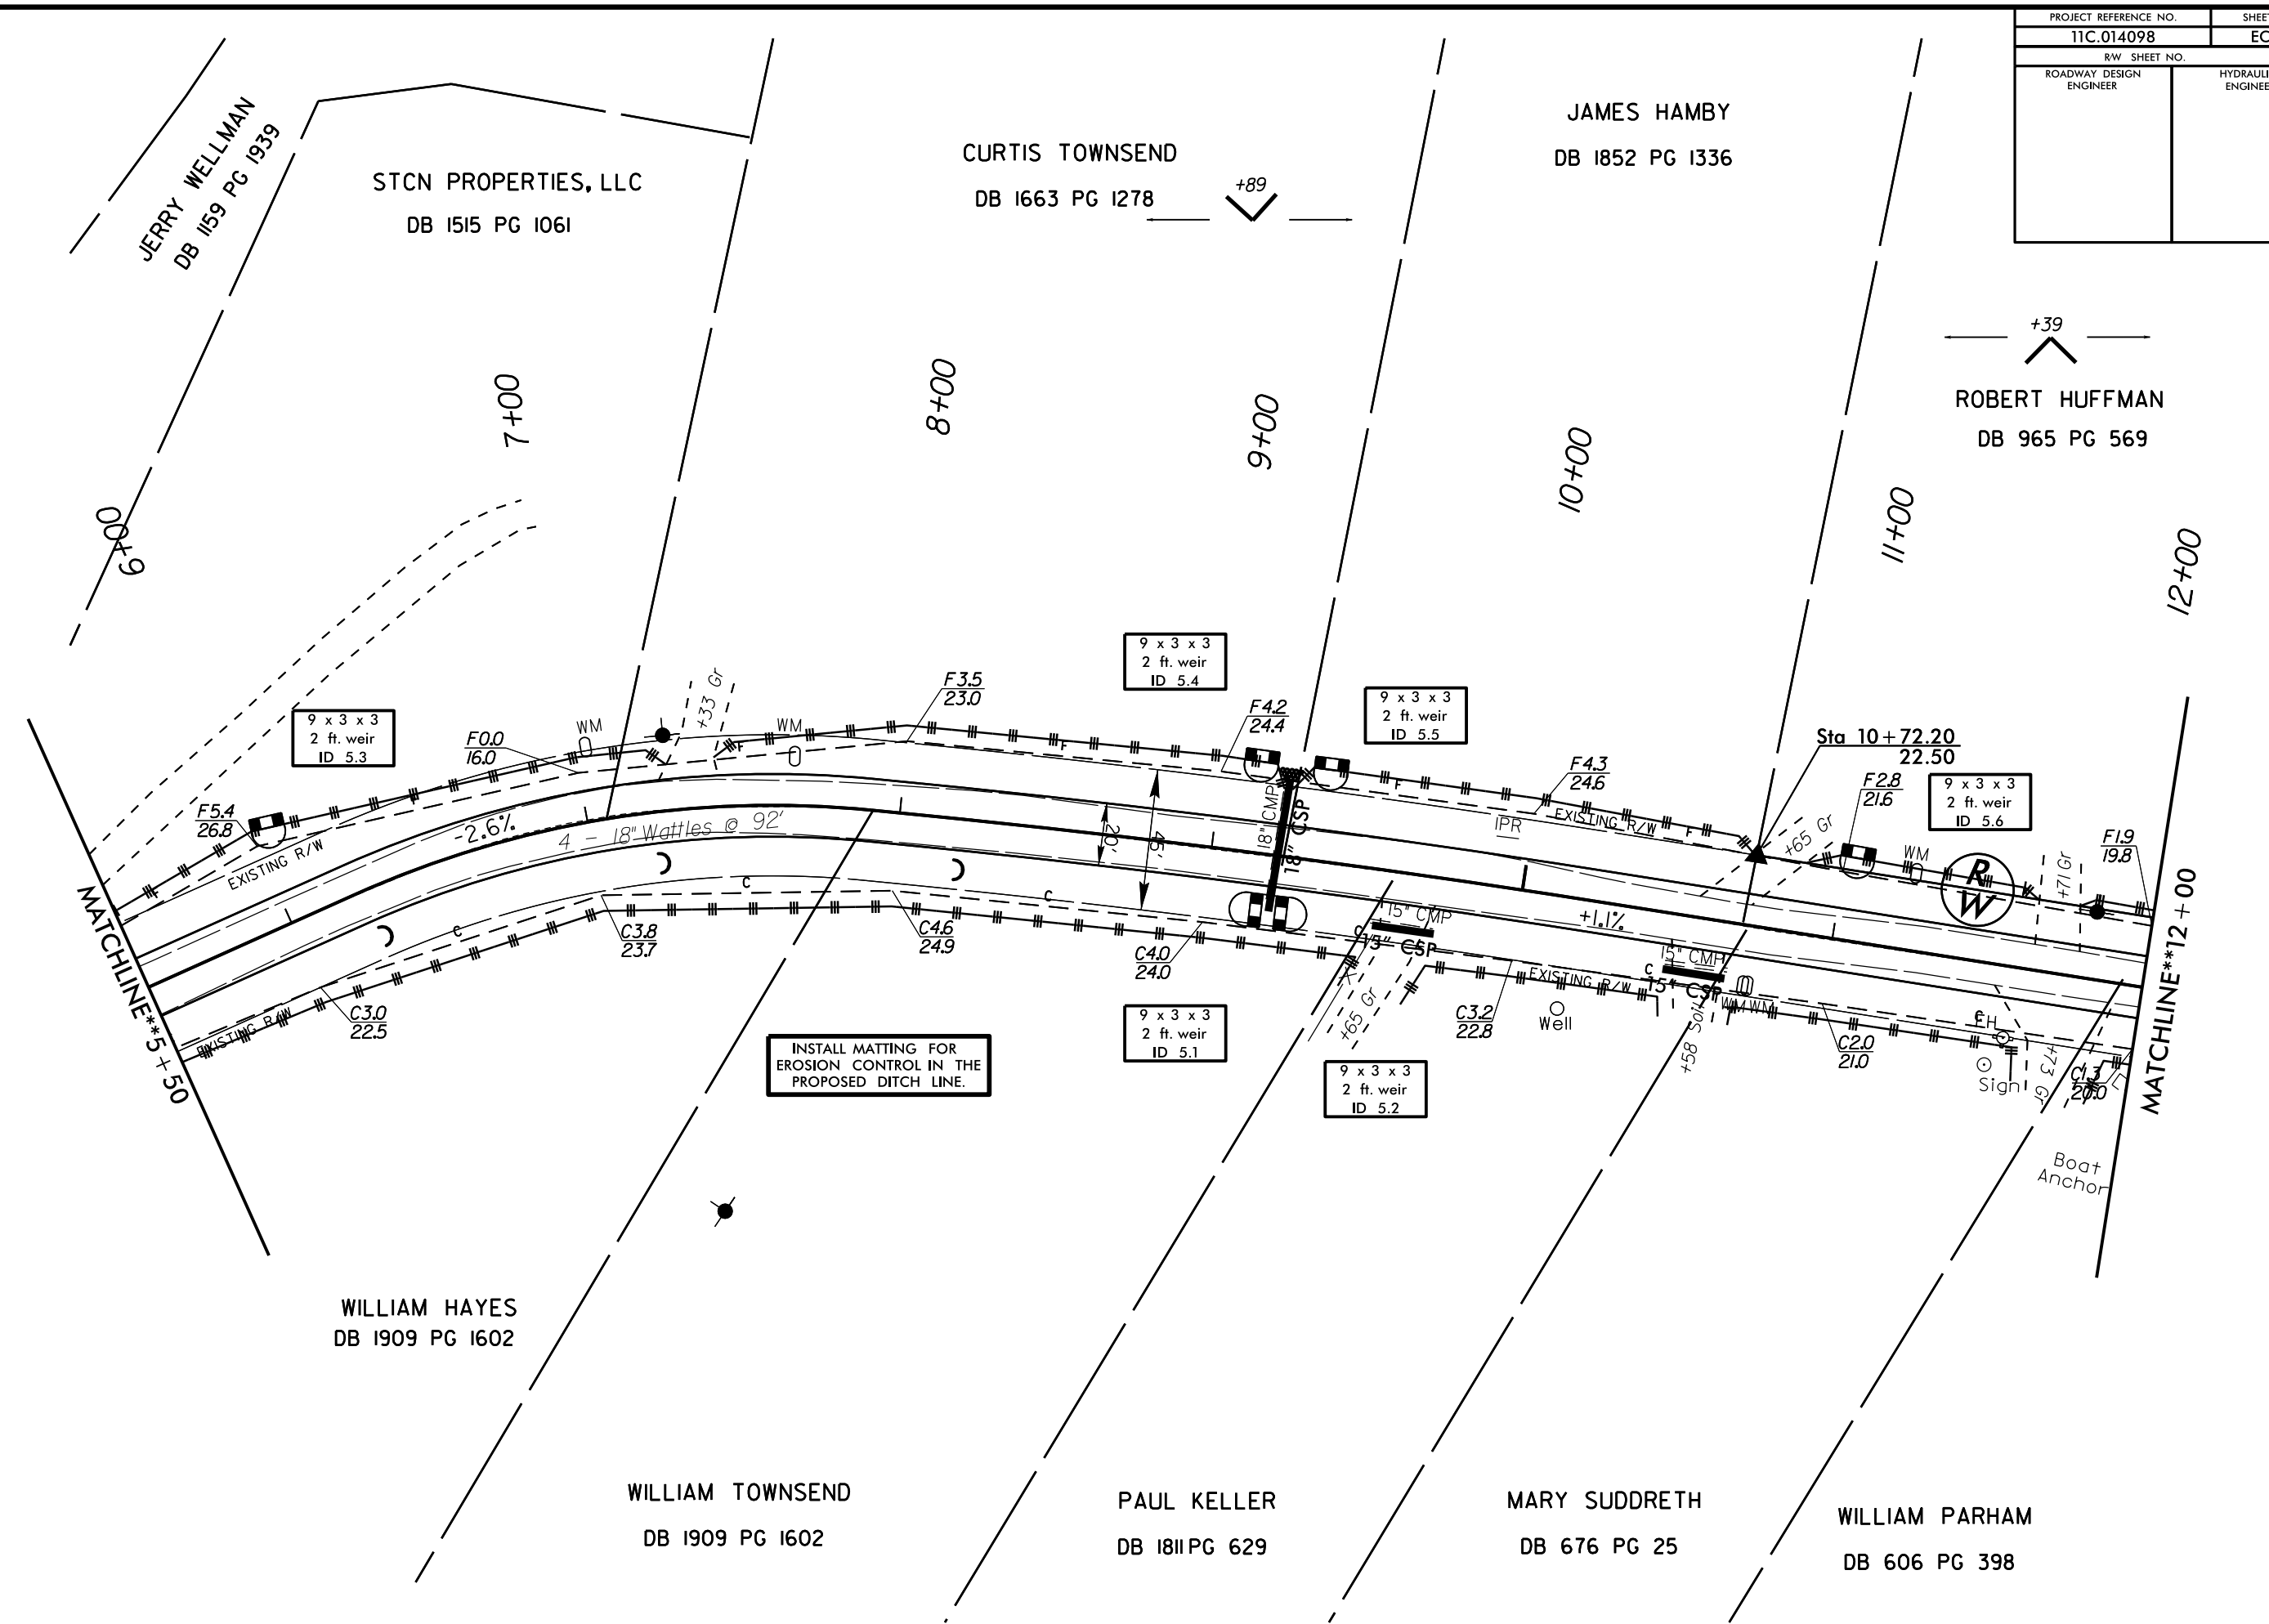





PROJECT REFERENCE NO.	SHEET NO.
11C.014098	EC-6
RW SHEET NO.	
ROADWAY DESIGN ENGINEER	HYDRAULICS ENGINEER

8/17/99

REVISIONS

15-JUN-2018 07:41  
 R:\Roads\Projects\Secondary\Caldwell\SR1958\_Lacey Road\EC\_Plan\_Sheets\EC-6.dgn  
 \$\$\$\$USE ENVELOPE\$\$\$\$

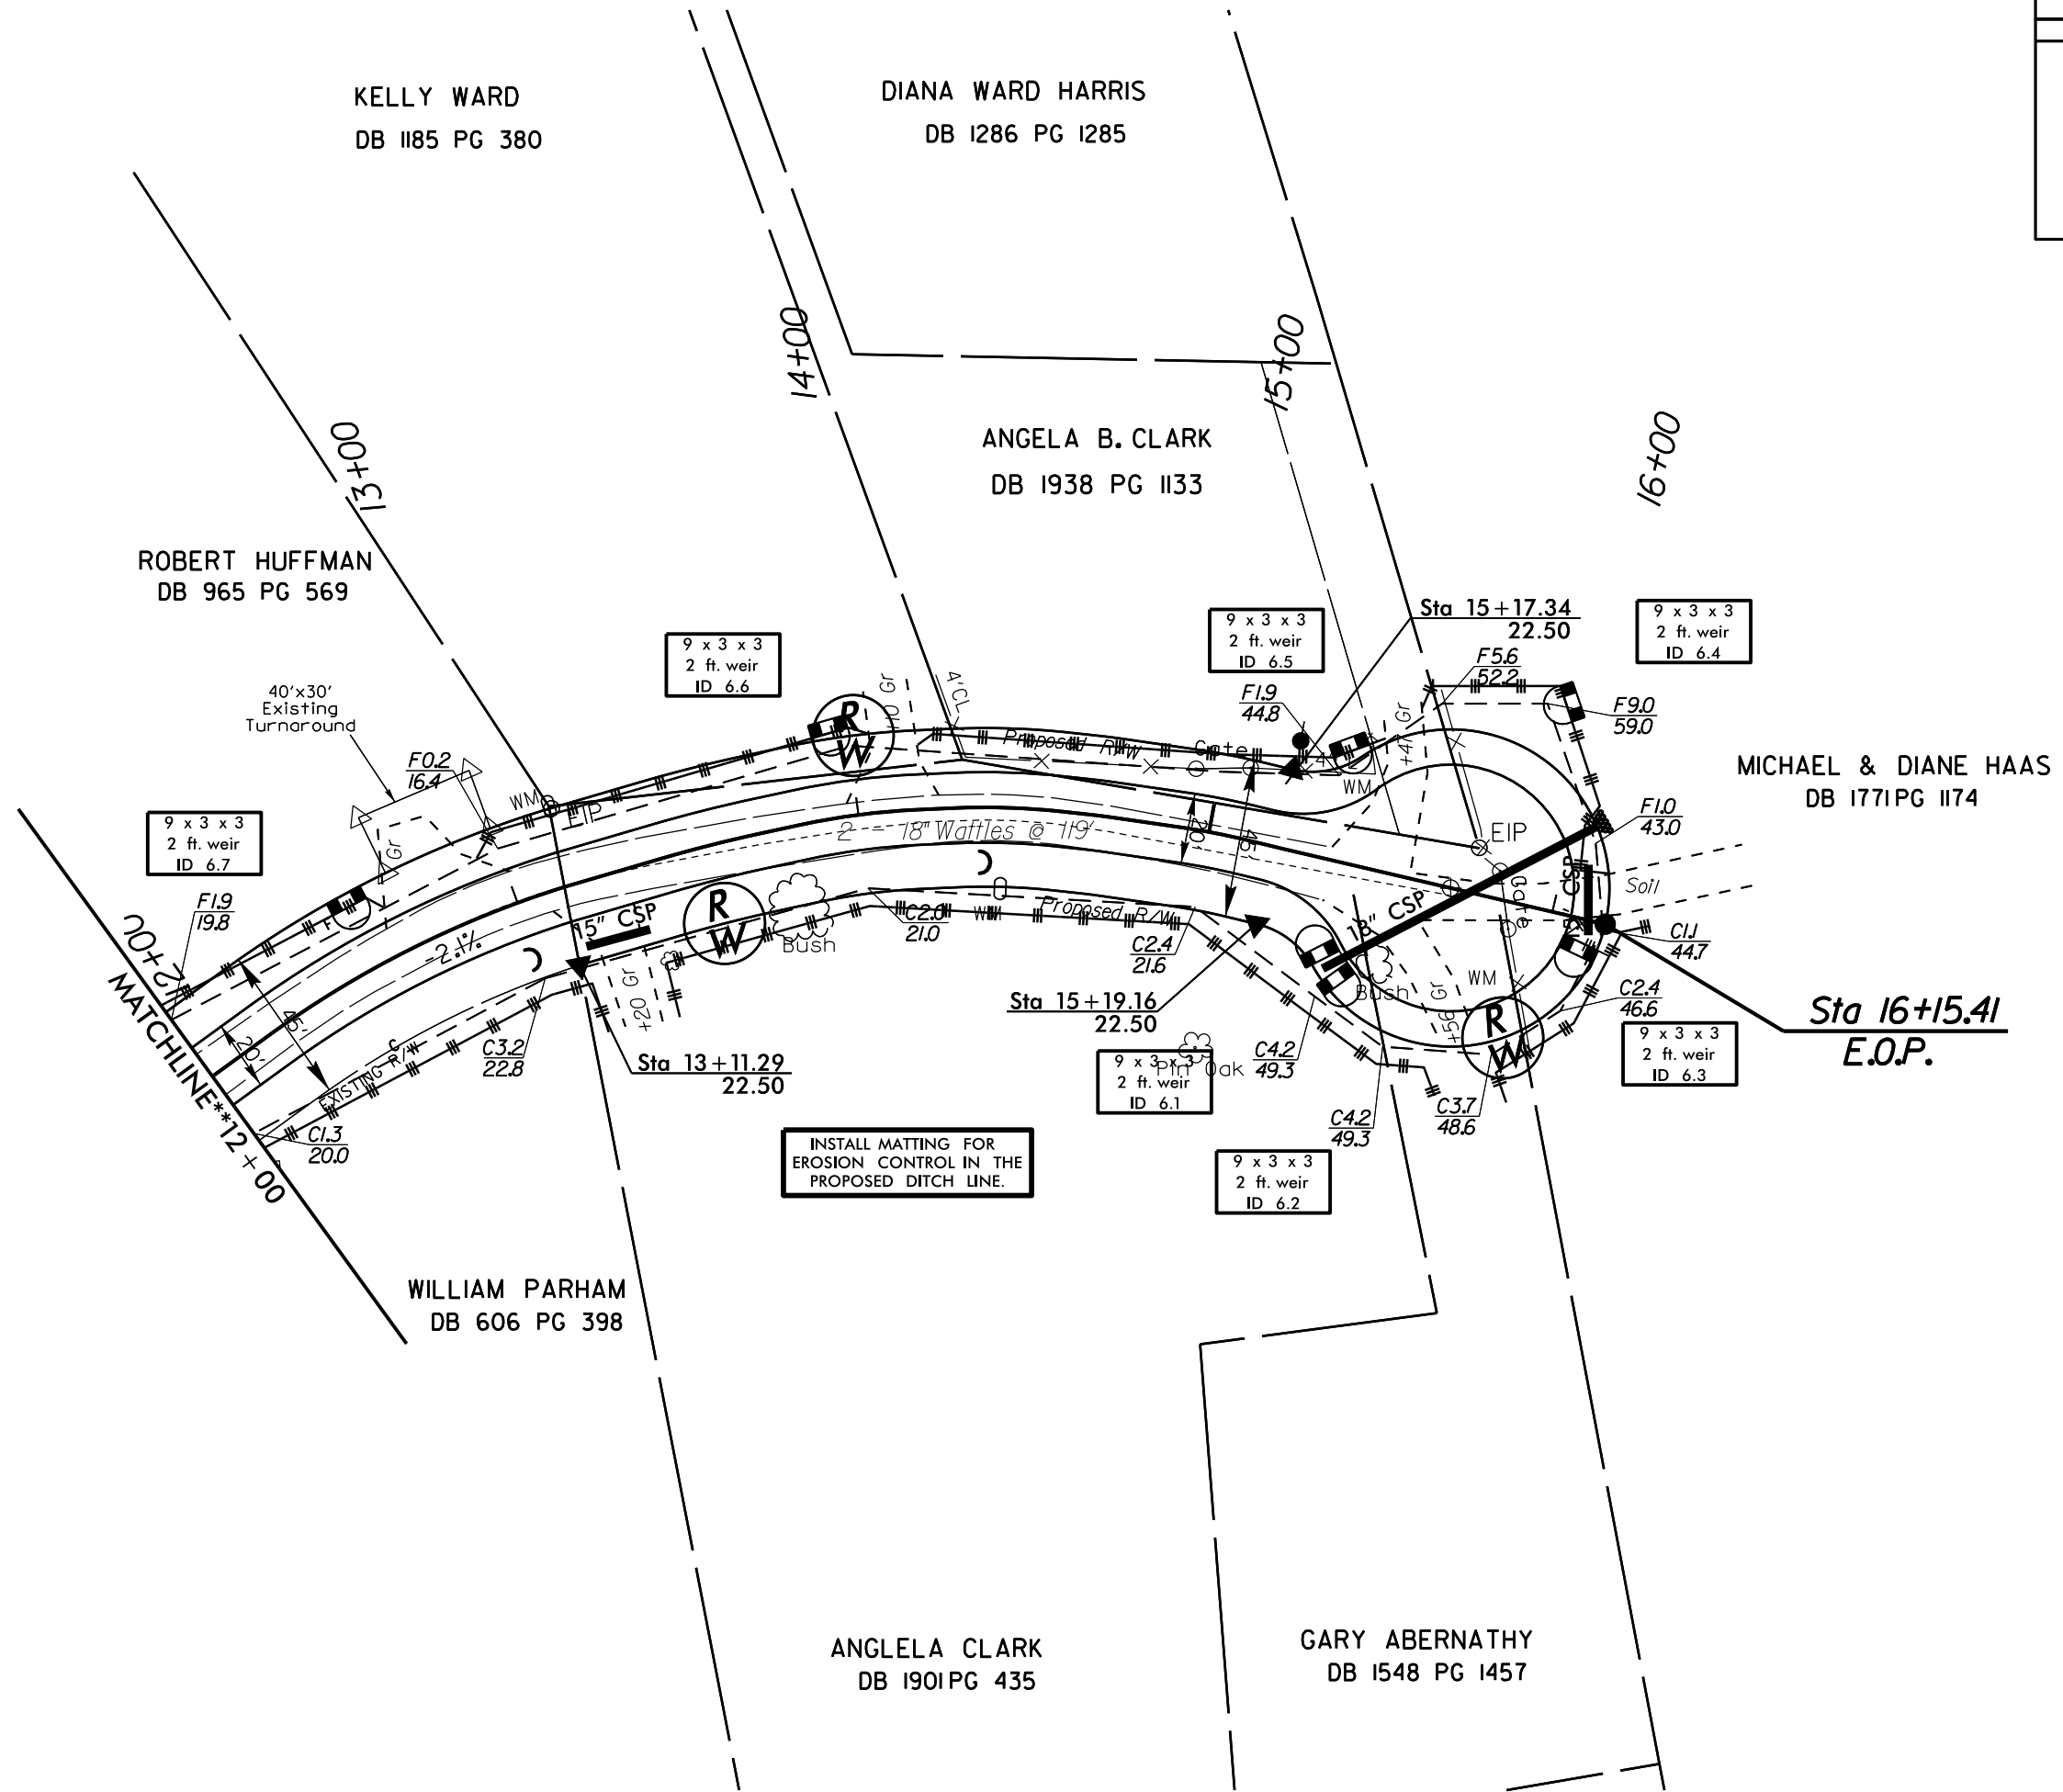

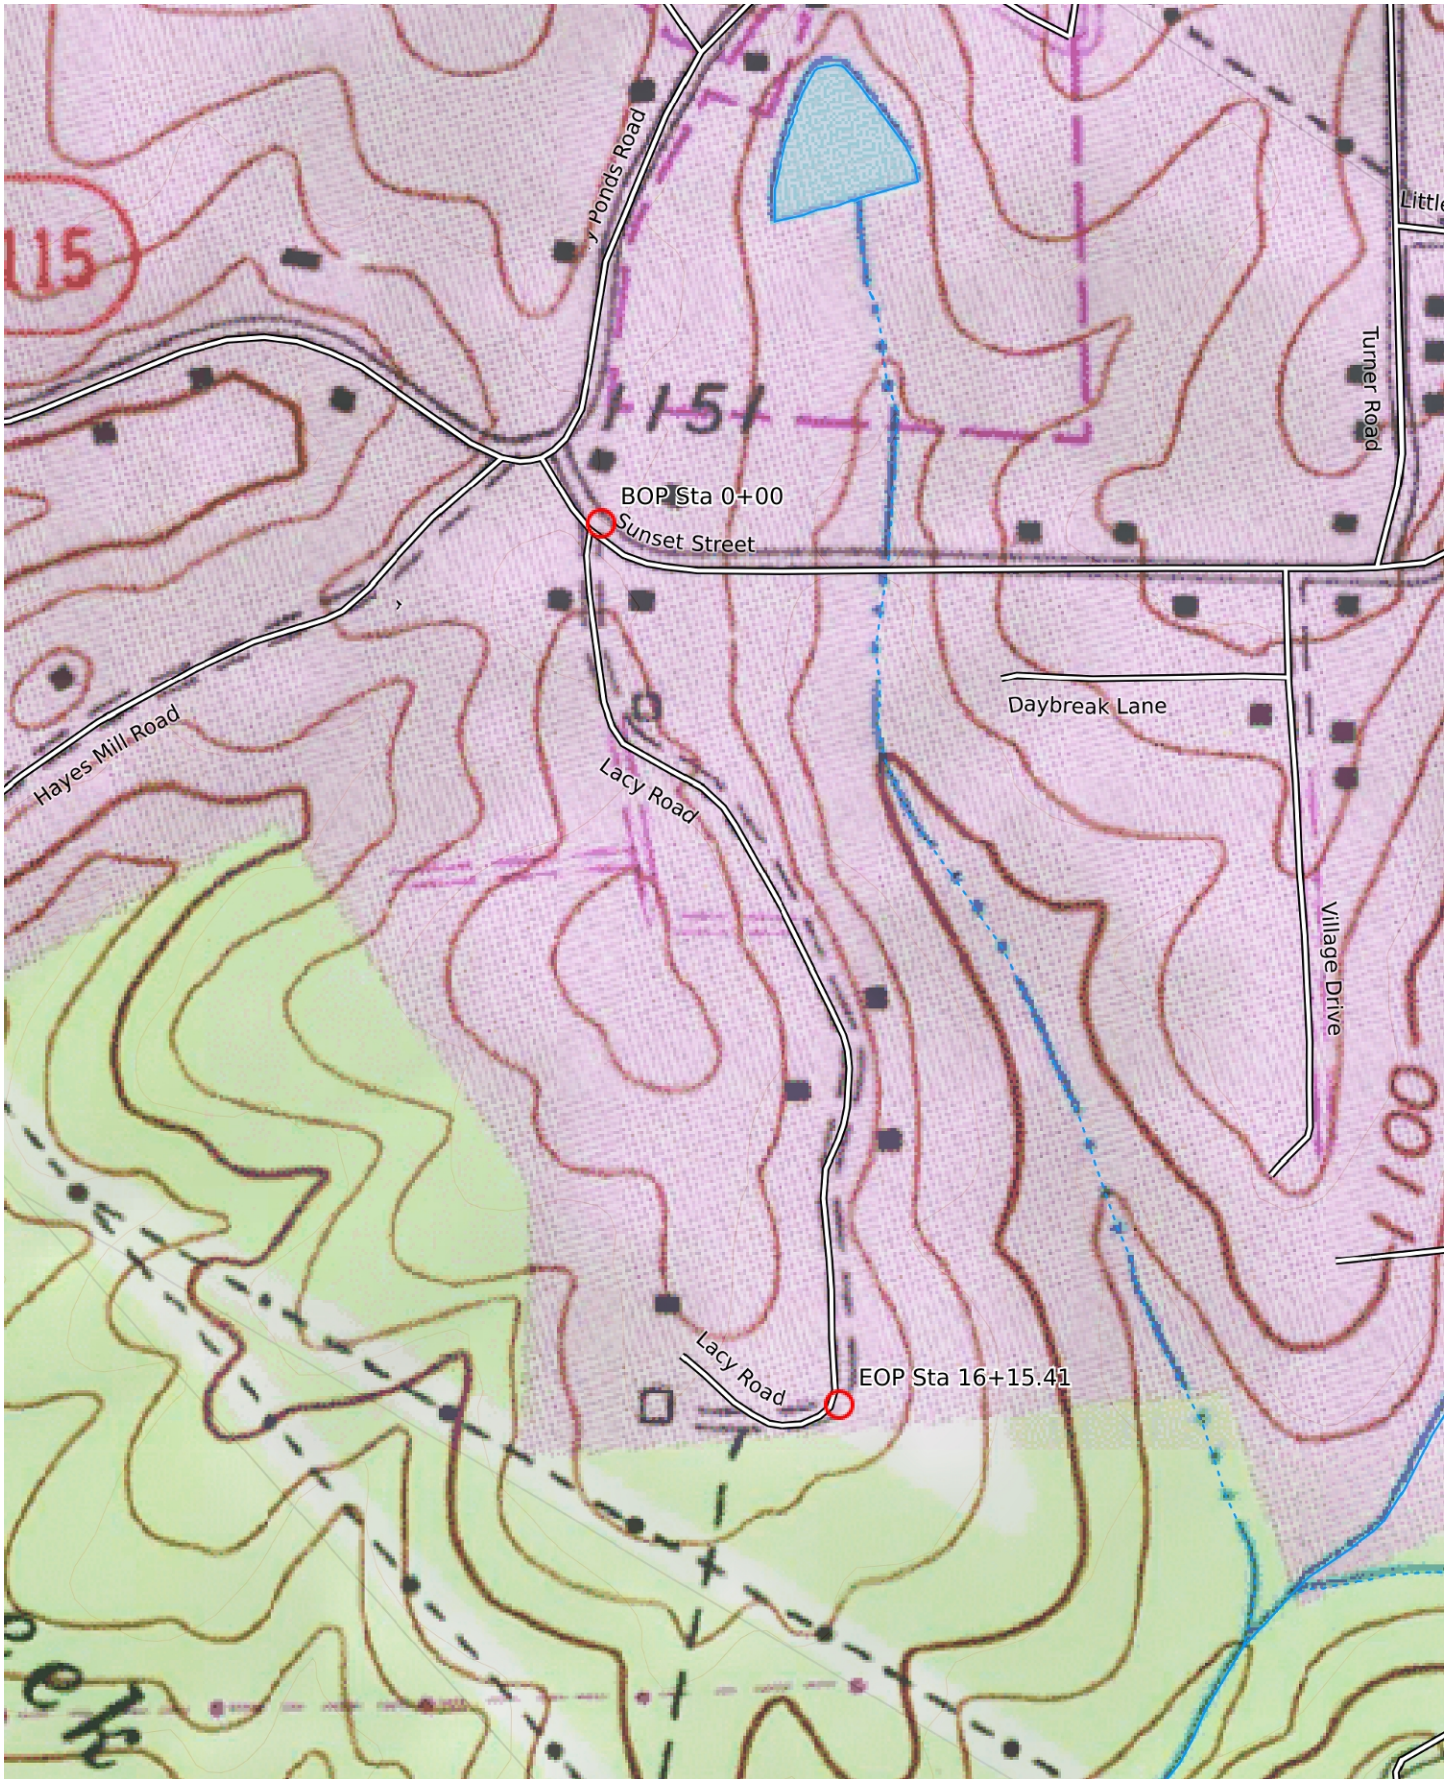

Mercator Projection  
 WGS84  
 USNG Zone 17SMV  
 CalTopo

