


ANNUAL REPORT FOR 2012



Bald Creek Site #8 Mitigation Site
Yancey County
TIP No. R-2518B
COE Action ID: SAW-2007-2197-357/300
DWQ #: 20071134

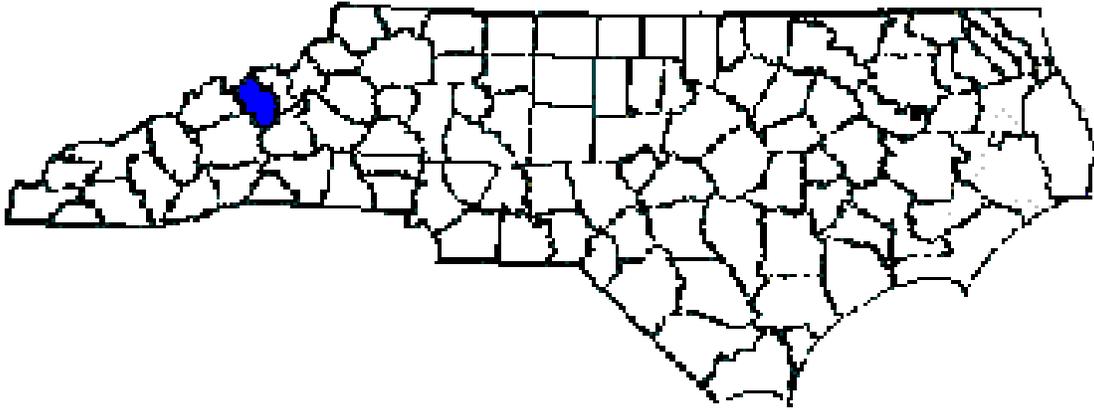

Prepared By:
Natural Environment Section & Roadside Environmental Unit
North Carolina Department of Transportation
December 2012

TABLE OF CONTENTS

SUMMARY	1
1.0 INTRODUCTION:.....	2
.1 Project Description	2
.2 Purpose	2
.3 Project History	2
.4 Debit Ledger.....	2
2.0 STREAM ASSESSMENT:	5
.1 Success Criteria	5
.2 Stream Description.....	5
.2.1 Post Construction Conditions.....	5
.2.2 Monitoring Conditions	5
.3 Results of Stream Assessment	6
.3.1 Site Data	6
3.0 VEGETATION	7
.1 Description of Species.....	7
.2 Results of Vegetation Monitoring.....	7
.3 Conclusions	7
4.0 OVERALL CONCLUSIONS/RECOMMENDATIONS	7
5.0 REFERENCES:	8

FIGURES

Figure 1 – Vicinity Map	3
Figure 2 – Site #8 Map	4

TABLES

Table 1 – Site #8 Morphological Summary	6
---	---

APPENDICES

Appendix A – Cross Sections and Longitudinal Profile

Appendix B – Site Photographs

SUMMARY

The following report summarizes the stream monitoring activities that have occurred during the Year 2012 at the Bald Creek Site #8 Mitigation Site in Yancey County. The North Carolina Department of Transportation (NCDOT) completed this project in August 2009. This report provides the monitoring results for the third formal year of monitoring (Year 2012). The Year 2012 monitoring period was the third of five scheduled years of monitoring on the Bald Creek Site #8 Mitigation Site (See Success Criteria Section 2.1).

Based on the overall conclusions of monitoring at Bald Creek Site #8, it has met the required monitoring protocols for the third formal year of monitoring on the stream and first formal year of monitoring on the planted vegetation. The channel throughout the stream enhancement site is stable at this time. The streambank and buffer area were planted in March 2012 with live stakes and bareroot seedlings. The planted vegetation is surviving at this time. NCDOT plans to complete a supplemental planting by March 2013 on the right buffer where temporary erosion control devices were removed. NCDOT will continue stream and vegetation monitoring at the Bald Creek Site #8 Mitigation Site in 2013.

1.0 INTRODUCTION

1.1 Project Description

The following report summarizes the stream monitoring activities that have occurred during the Year 2012 at the Bald Creek Site #8 Mitigation Site. Site #8 is located on US 19 in Yancey County at Sta. 175+65 to Sta. 178+50 -L- (Figure 1). The Bald Creek Site #8 was constructed to provide mitigation for stream impacts associated with Transportation Improvement Program (TIP) number R-2518B in Yancey County.

The mitigation site provided approximately 997 linear feet of stream enhancement. Construction was completed during August 2009 by the NCDOT. Stream enhancement involved excavation of bankfull benches and installation of in-stream structures. In-stream structures, such as J-hooks and cross vanes were used to stabilize channel pattern and improve bed form diversity and habitat. The riparian buffer zone was also planted.

1.2 Purpose

In order for a mitigation site to be considered successful, the site must meet the success criteria. This report details the monitoring in 2012 at the Bald Creek Site #8 Mitigation Site. Hydrologic monitoring was not required for this site.

1.3 Project History


August 2009	Construction Completed
October 2009	As-Built Survey Completed
February 2010	Site Planted (Type I only)
November 2010	Stream Channel Monitoring (Year 1)
November 2011	Stream Channel Monitoring (Year 2)
March 2012	Site Planted (Type I and II)
September 2012	Vegetation Monitoring (Year 1)
November 2012	Stream Channel Monitoring (Year 3)

1.4 Debit Ledger

The entire Bald Creek Site #8 stream mitigation site was used for the R-2518B project to compensate for unavoidable stream impacts.



Figure 1. Vicinity Map

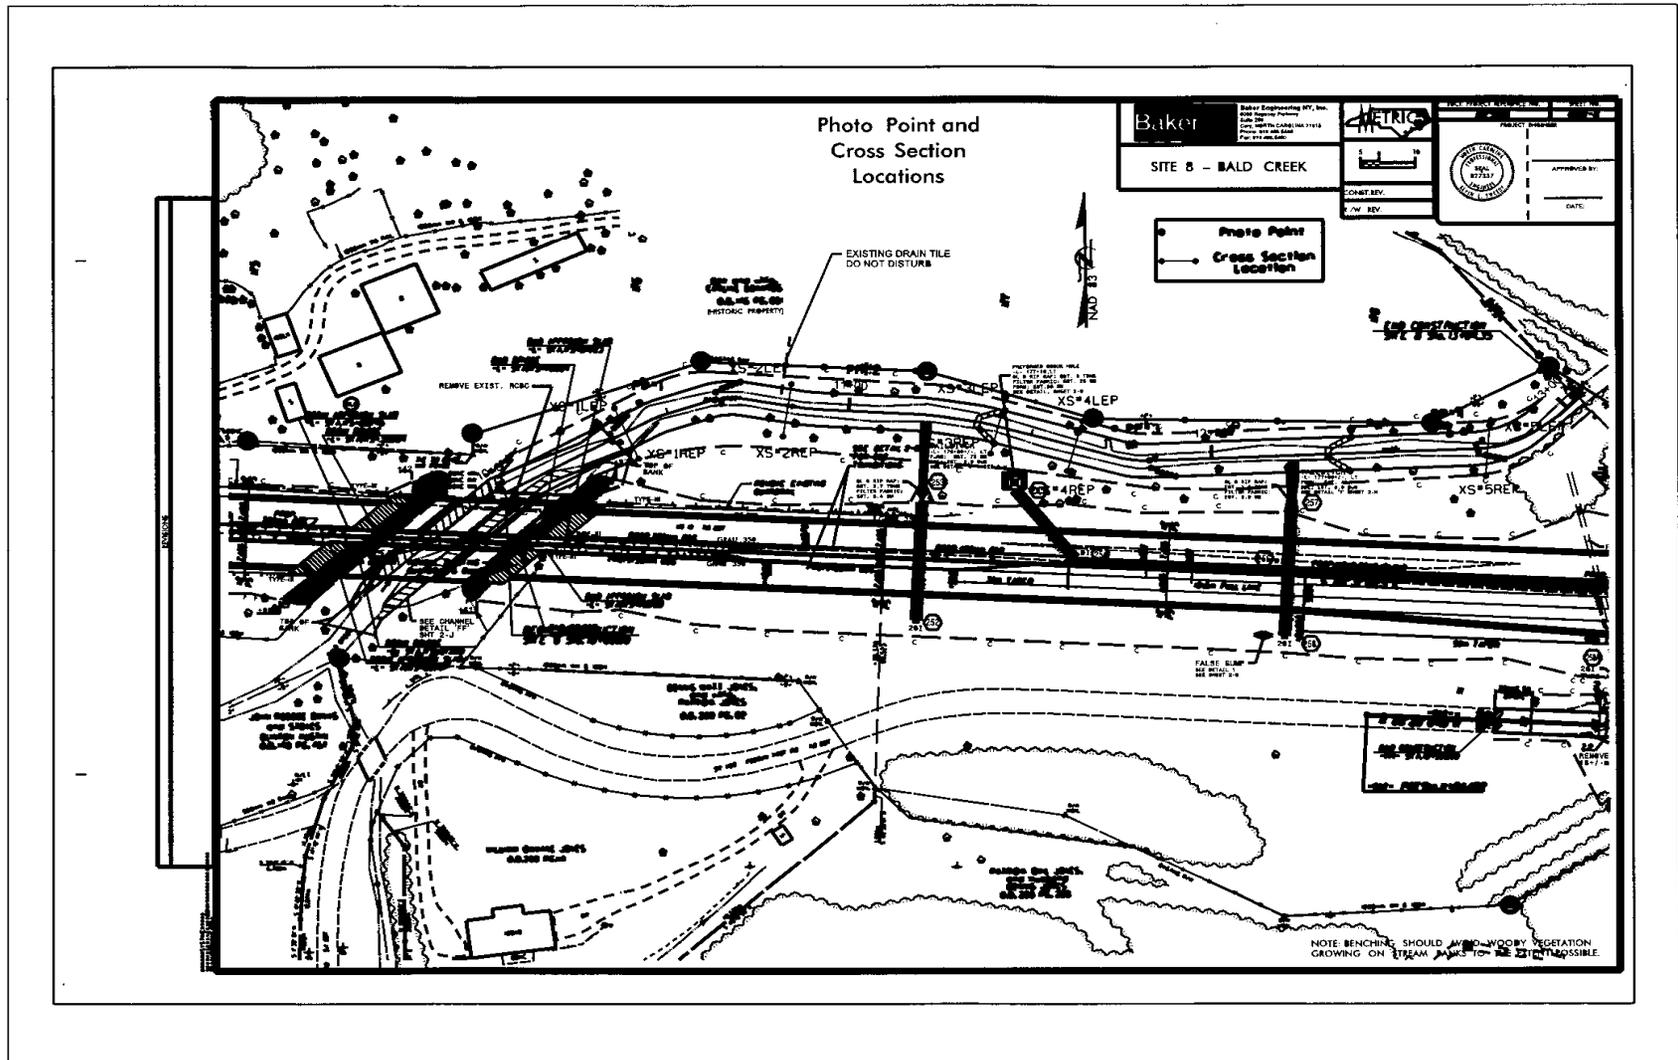

R2518B_rdy_psh_OSM8_asbuilt.dgn 12/21/2010 8:33:36 AM

Figure 2. Site #8 Map

2.0 STREAM ASSESSMENT

2.1 Success Criteria

The permittee shall monitor the restoration and enhancement mitigation sites following the Level 1 protocols outlined in the “Stream Mitigation Guidelines,” dated April 2003 with the following exceptions:

1. Pebble counts shall not be conducted.
2. Two cross sections shall be conducted for streams less than 500 linear feet and five (5) cross sections shall be conducted for streams greater than 500 linear feet.
3. Riparian success shall be by visual inspection of plant survival. Photos will be taken and comments noted on plant survival.

The permittee shall monitor the preservation sites by visual inspection. Photos will be taken and comments noted on plant survival. The monitoring shall be conducted annually for a minimum of five (5) years after final planting. The monitoring results shall be submitted to DWQ in a final report within sixty (60) days after completing monitoring. After 5 years the NCDOT shall contact the DWQ to schedule a site visit to “close out” the mitigation site.

2.2 Stream Description

2.2.1 Post-Construction Conditions

The enhancement of Bald Creek Site #8 Mitigation Site involved excavation of bankfull benches and installation of in-stream structures. In-stream structures, such as J-hooks and cross vanes were used to stabilize channel pattern and improve bed form diversity and habitat. The riparian buffer zone was also planted.

2.2.2 Monitoring Conditions

The objective of the Bald Creek Site #8 stream enhancement was to enhance a E4 stream as identified in Rosgen’s Applied River Morphology. A total of five cross sections (two in a riffle and three in a pool) were surveyed. For this report, only cross sections containing riffles were used in the comparison of channel morphology presented below in Table 1 (Site #8).

Table 1. Abbreviated Morphological Summary (Bald Creek Site #8)

Variable	Proposed	Cross-Section #2 (Riffle)	Cross-Section #4 (Riffle)	Min. – Max Values (Riffle Sections Only)
		2012	2012	2012
Drainage Area (mi ²)	17.1	17.1	17.1	17.1
Bankfull Cross Sectional Area (ft ²)	75	40.05	33.97	33.97 – 40.05
Maximum Bankfull Depth (ft.)	3.6	3.57	2.62	2.62 – 3.57
Width of the Floodprone Area (ft.)	> 80	51.9	55.48	51.9 – 55.48
Bankfull Mean Depth (ft.)	2.5	1.89	1.85	1.85 – 1.89
Width/Depth Ratio	12	11.2	9.94	9.94 – 11.2
Entrenchment Ratio	> 3.2	2.45	3.02	2.45 – 3.02
Bankfull Width (ft.)	30	21.16	18.38	18.38 – 21.16

* Riffle values are used for classification purposes, pool values are shown in Appendix A.

2.3 Results of the Stream Assessment

2.3.1 Site Data

The assessment included the survey of five cross sections and the longitudinal profile of Bald Creek Site #8 established by NCDOT after construction. The length of the profile along Bald Creek Site #8 was approximately 900 linear feet. Five cross sections were established during the as-built monitoring year. Cross section locations were subsequently based on the stationing of the longitudinal profile and are presented below. The location of the cross sections and longitudinal profile are shown in Appendix A.

Bald Creek Site #8 Cross-Sections:

- ◆ Cross-Section #1: Bald Creek Site #8, Station 23+00, midpoint of pool
- ◆ Cross-Section #2: Bald Creek Site #8, Station 177+00, midpoint of riffle
- ◆ Cross-Section #3: Bald Creek Site #8, Station 366+00, midpoint of pool
- ◆ Cross-Section #4: Bald Creek Site #8, Station 438+06, midpoint of riffle
- ◆ Cross-Section #5: Bald Creek Site #8, Station 812+05, midpoint of pool

Based on comparisons of the As-Built to the monitoring data, all of the cross sections appear stable with little or no active bank erosion. Graphs of the cross sections are presented in Appendix A. Future survey data will vary depending on actual location of rod placement and alignment; however, this information should remain similar in appearance. The longitudinal profile showed that the channel was stable for the 2012 monitoring evaluation. NCDOT noted that a bankfull event had occurred since last monitoring evaluation. Pebble counts were not required per the permit conditions and therefore were not completed.

3.0 VEGETATION: BALD CREEK SITE #8

3.1 Description of Species

The following tree species were planted on the streambank:

Salix nigra, Black Willow

Cornus amomum, Silky Dogwood

The following tree species were planted in the buffer area:

Liriodendron tulipifera, Yellow Poplar

Platanus occidentalis, Sycamore

Fraxinus pennsylvanica, Green Ash

Quercus alba, White Oak

3.2 Results of Vegetation Monitoring

Streambank & Buffer Vegetation: The streambank reforestation was completed in March 2012. The Year 1 vegetation monitoring evaluation noted: Type I: Black Willow, Silky Dogwood and Type II: Sycamore, Green Ash, Tulip Poplar and White Oak were surviving at the time of the monitoring evaluation. There was missing planted vegetation from Sta. 10+00 to 11+00 along the right buffer where temporary erosion control devices had been removed.

3.3 Conclusions

NCDOT plans to complete a supplemental planting by March 2013 on the right buffer where temporary erosion control devices were removed. NCDOT will continue to monitor the planted vegetation in 2013.

4.0 OVERALL CONCLUSIONS/RECOMMENDATIONS

The Bald Creek Site #8 Mitigation Site has met the required monitoring protocols for the third formal year of monitoring on the stream and the first formal year of monitoring on the planted vegetation. The channel throughout the stream enhancement site is stable and the planted vegetation is surviving at this time. NCDOT plans to complete a supplemental planting by March 2013 on the right buffer where temporary erosion control devices were removed. NCDOT will continue monitoring the Bald Creek Site #8 Mitigation Site in 2013.

5.0 REFERENCES

Stream Mitigation Plan, US Highway 19, R-2518B On-Site Mitigation
Yancey County, North Carolina, February 2007.

Stream Mitigation Plan Sheets for R-2518B, US 19 from east of the Madison
County line to SR 1336, Stream Mitigation (Preservation, Enhancement,
and Restoration), Buck Engineering.

North Carolina Department of Transportation (NCDOT), April 29, 2008. 404 and
401 Individual Permits for R-2518A and R-2518B (ACOE Permit No. 2007-
2197-357/300 and DWQ Project No. 20071134, Individual Certification No.
3706).


Rosgen, D.L, 1996. Applied River Morphology. Wildland Hydrology, Pagosa
Springs, Colorado.

US Army Corps of Engineers (USACE), 2003. Stream Mitigation Guidelines.
Prepared with cooperation from the US Environmental Protection Agency,
NC Wildlife Resources Commission, and the NC Division of Water Quality.

APPENDIX A

CROSS SECTIONS AND LONGITUDINAL PROFILE


R-2518B Site 8 XS-1 @ Sta. 23+00

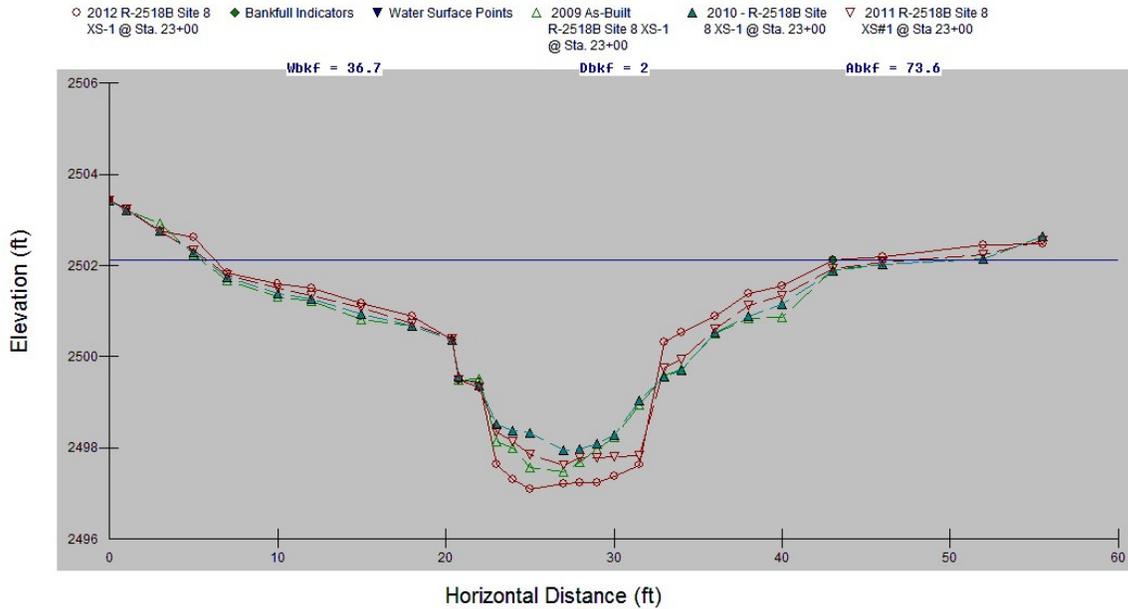

Site #8: Cross-Section #1 (Pool) Abbreviated Morphological Summary*					
	2010	2011	2012	2013	2014
Bankfull Cross Sectional Area (ft²)	63.37	66.88	73.56		
Maximum Bankfull Depth (ft.)	3.93	4.31	5.03		
Bankfull Mean Depth (ft.)	1.73	1.83	2		
Bankfull Width (ft.)	36.56	36.53	36.71		


* According to the Rosgen Classification of Natural Rivers floodprone width, entrenchment ratio, and width depth ratio are not measured in pool, glide, or run features.

R-2518B Site 8 XS-2 @ Sta 177+00

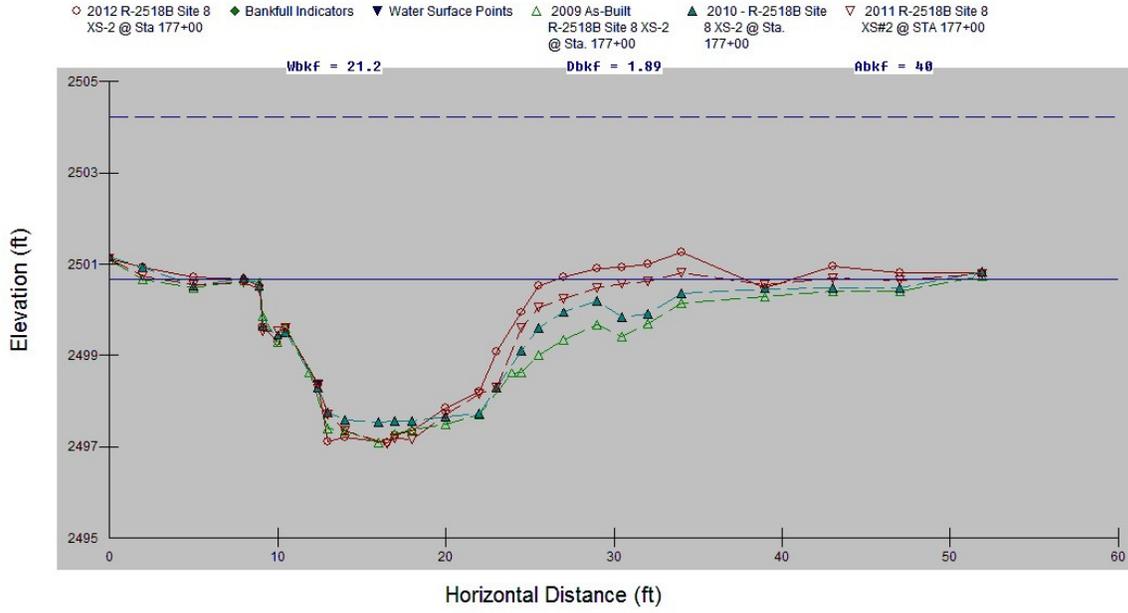

Site #8: Cross-Section #2 (Riffle) Abbreviated Morphological Summary					
	2010	2011	2012	2013	2014
Bankfull Cross Sectional Area (ft. ²)	39.07	41.53	40.05		
Maximum Bankfull Depth (ft.)	2.81	3.54	3.57		
Width of the Floodprone Area (ft.)	51.9	51.9	51.9		
Bankfull Mean Depth (ft.)	1.56	1.79	1.89		
Width/Depth Ratio	16.06	12.99	11.2		
Entrenchment Ratio	2.07	2.23	2.45		
Bankfull Width (ft.)	25.06	23.25	21.16		


R-2518B Site 8 XS-3 @ Sta 366+00

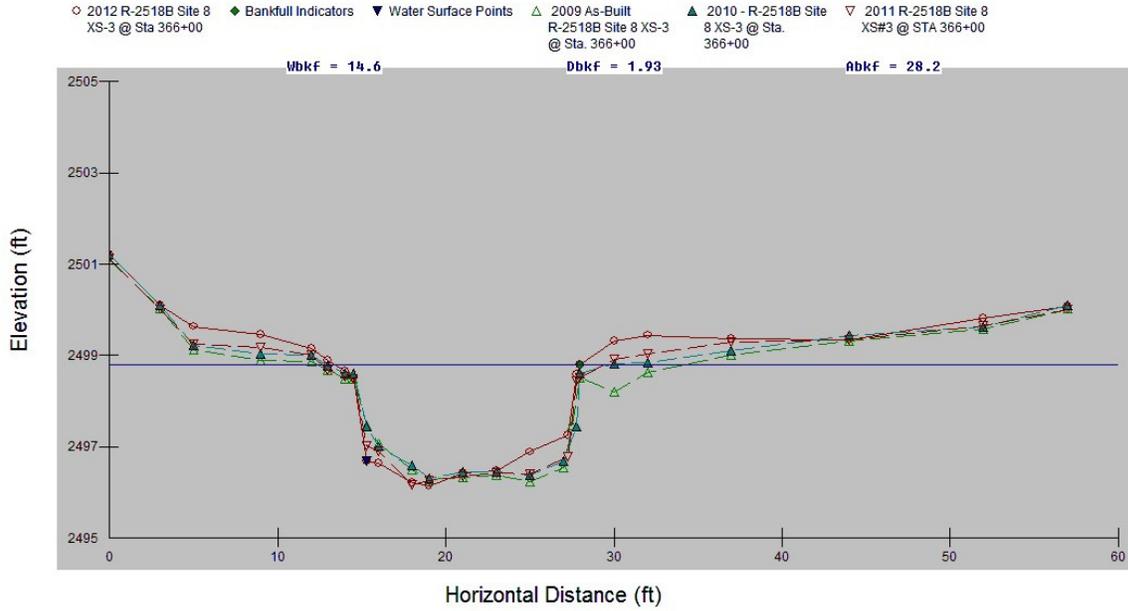

Site #8: Cross-Section #3 (Pool) Abbreviated Morphological Summary*					
	2010	2011	2012	2013	2014
Bankfull Cross Sectional Area (ft²)	25.73	25.79	28.22		
Maximum Bankfull Depth (ft.)	2.28	2.36	2.64		
Bankfull Mean Depth (ft.)	1.91	1.86	1.93		
Bankfull Width (ft.)	13.5	13.9	14.58		


* According to the Rosgen Classification of Natural Rivers floodprone width, entrenchment ratio, and width depth ratio are not measured in pool, glide, or run features.

R-2518B Site 8 XS-4 @ Sta 438+06

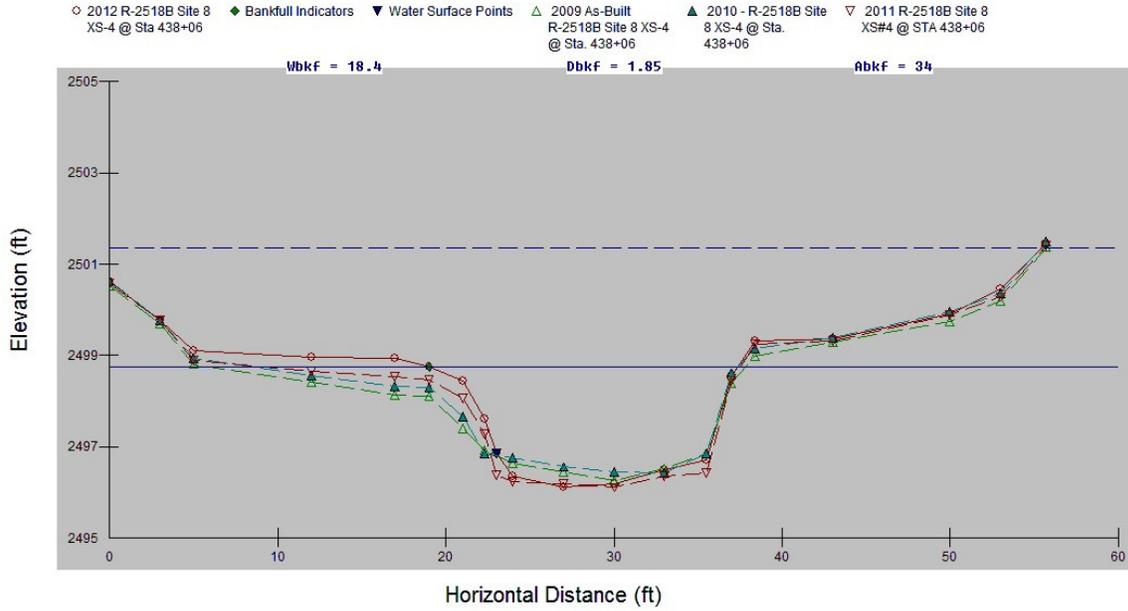

Site #8: Cross-Section #4 (Riffle) Abbreviated Morphological Summary					
	2010	2011	2012	2013	2014
Bankfull Cross Sectional Area (ft ²)	25.58	31.87	33.97		
Maximum Bankfull Depth (ft.)	1.88	2.36	2.62		
Width of the Floodprone Area (ft.)	50.11	54.31	55.48		
Bankfull Mean Depth (ft.)	1.44	1.77	1.85		
Width/Depth Ratio	12.32	10.19	9.94		
Entrenchment Ratio	2.83	3.01	3.02		
Bankfull Width (ft.)	17.74	18.04	18.38		


R-2518B Site 8 XS-5 @ Sta. 812+05

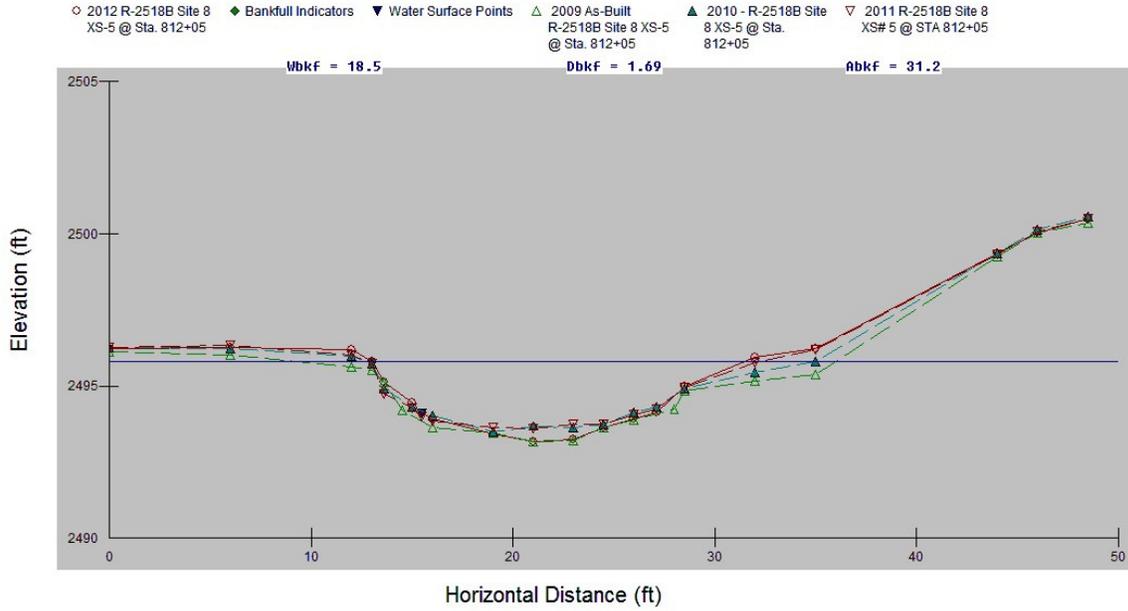

Site #8: Cross-Section #5 (Pool) Abbreviated Morphological Summary*					
	2010	2011	2012	2013	2014
Bankfull Cross Sectional Area (ft²)	29.34	28.13	31.18		
Maximum Bankfull Depth (ft.)	2.25	2.11	2.62		
Bankfull Mean Depth (ft.)	1.36	1.49	1.69		
Bankfull Width (ft.)	21.57	18.82	18.48		

* According to the Rosgen Classification of Natural Rivers floodprone width, entrenchment ratio, and width depth ratio are not measured in pool, glide, or run features.

2012 R-2518B Site 8 Profile

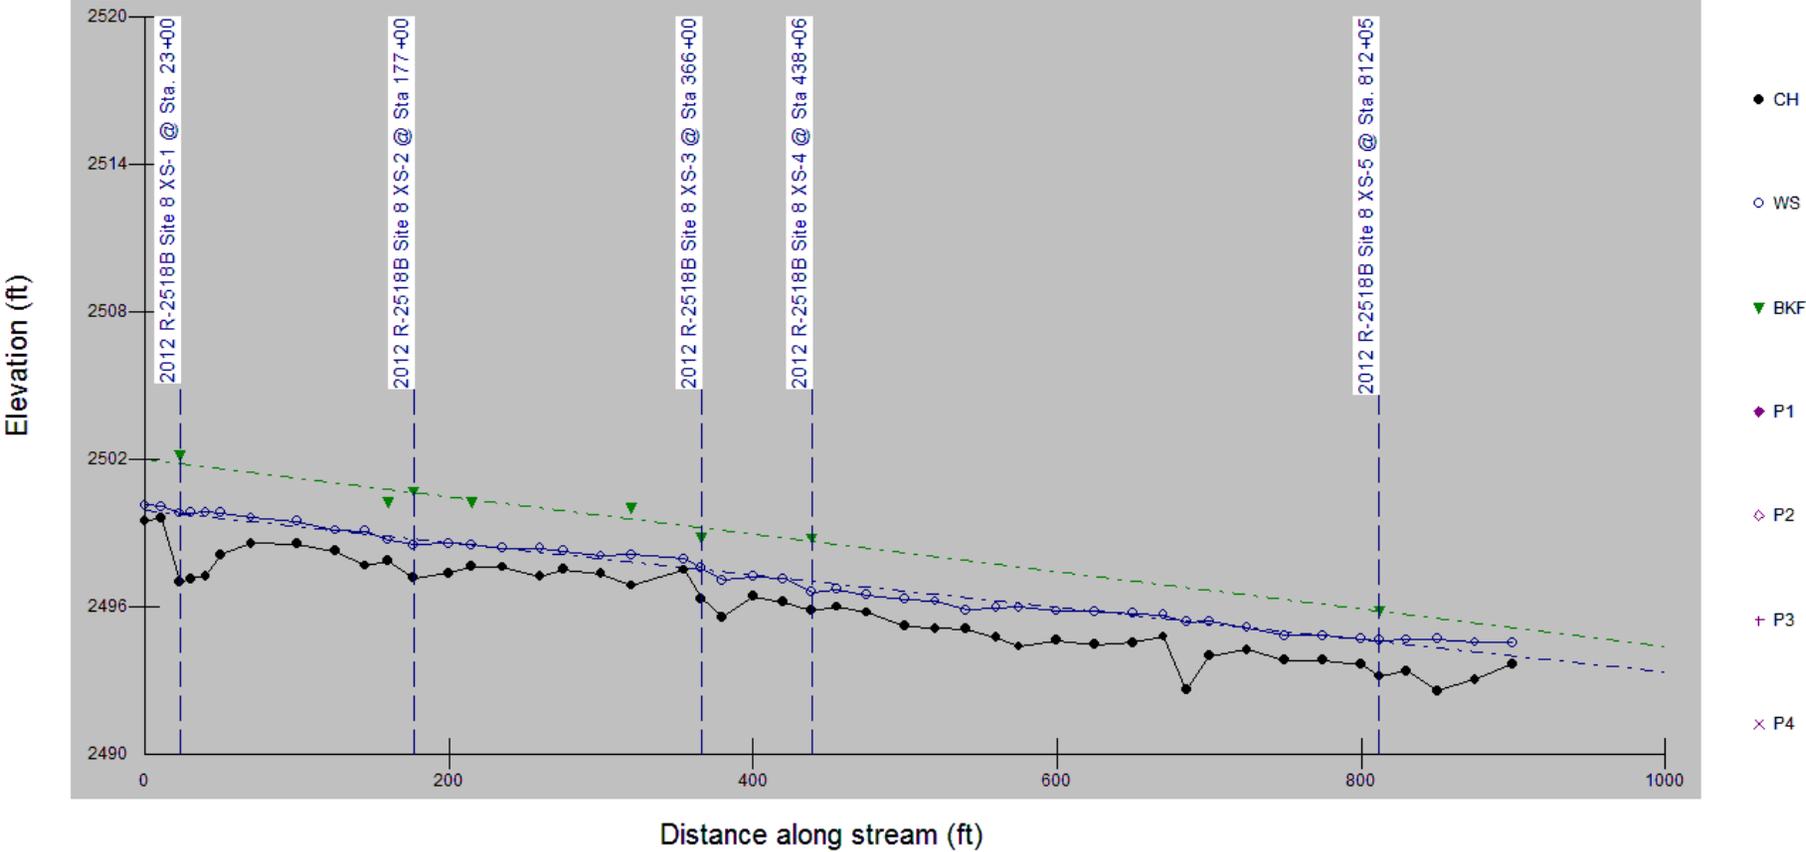

APPENDIX B
SITE PHOTOGRAPHS

Bald Creek Site #8



Photo Point #1 (Upstream)



Photo Point #1 (Downstream)



Photo Point #2 (Upstream)



Photo Point #2 (Downstream)



Photo Point #3 (Upstream)
November 2012



Photo Point #3 (Downstream)

Bald Creek Site #8



Photo Point #4 (Upstream)
November 2012



Photo Point #4 (Downstream)

Bald Creek Site #8



Vegetation Overview Photo



Vegetation Overview Photo



Vegetation Overview Photo

September 2012
