

#### **NORTH CAROLINA**

Department of Transportation



















## NCDOT Construction Projects

M. Lamar Sylvester, PE


October 2018

#### Project Delivery - All Projects

Fiscal Years 2014 - 2018

- Total Number of Projects = 2,907
- Projects Completed by Original Completion Date = 1,373
- Projects Completed by Revised Completion Date = 971
- Projects Not Completed by Original or Revised

Completion Date = 563

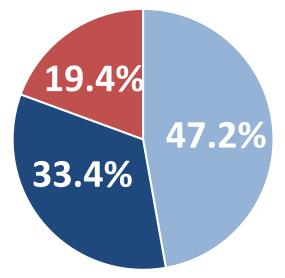


- % Complete by Original Completion Date
- % Complete by Revised Completion Date
- Not Complete by Original or Revised Completion Date

#### Project Delivery - All Projects

2018 Fiscal Year


- Total Number of Projects = 541
- Projects Completed by Original Completion Date = 247
- Projects Completed by Revised Completion Date = 198
- Projects Not Completed by Original or Revised
  Completion Date = 96

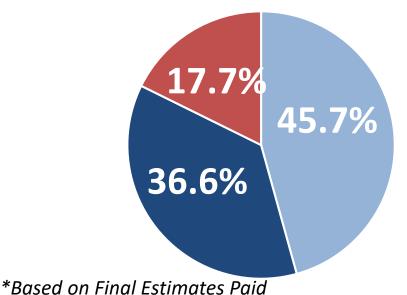

- % Complete by Original Completion Date
- % Complete by Revised Completion Date
- Not Complete by Original or Revised Completion Date

#### Project Delivery - All Projects

Fiscal Years 2014 - 2018

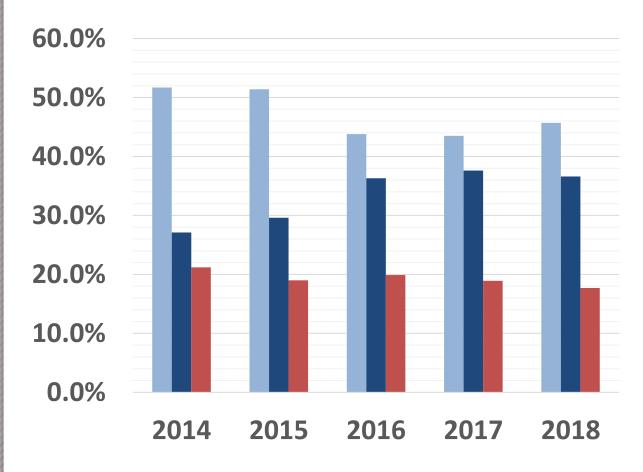


- % Complete by Original Completion Date
- % Complete by Revised Completion Date
- % Not Complete by Original or Revised Completion Date

#### Project Delivery - Resurfacing

Fiscal Years 2014 - 2018

- Total Number of Projects = 956
- Projects Completed by Original Completion Date = 463
- Projects Completed by Revised Completion Date = 245
- Projects Not Completed by Original or Revised
  Completion Date = 248

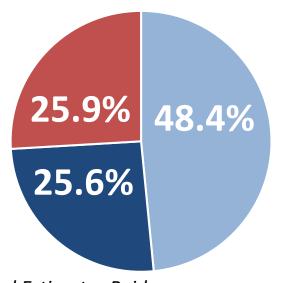


- % Complete by Original Completion Date
- % Complete by Revised Completion Date
- Not Complete by Original or Revised Completion Date

# Project Delivery - Resurfacing

2018 Fiscal Year

- Total Number of Projects = 143
- Projects Completed by Original Completion Date = 65
- Projects Completed by Revised Completion Date = 40
- Projects Not Completed by Original or Revised


Completion Date = 38

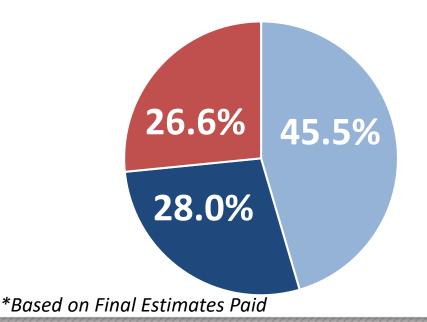

- % Complete by Original Completion Date
- % Complete by Revised Completion Date
- Not Complete by Original or Revised Completion Date

## Project Delivery - Resurfacing

Fiscal Years 2014 - 2018

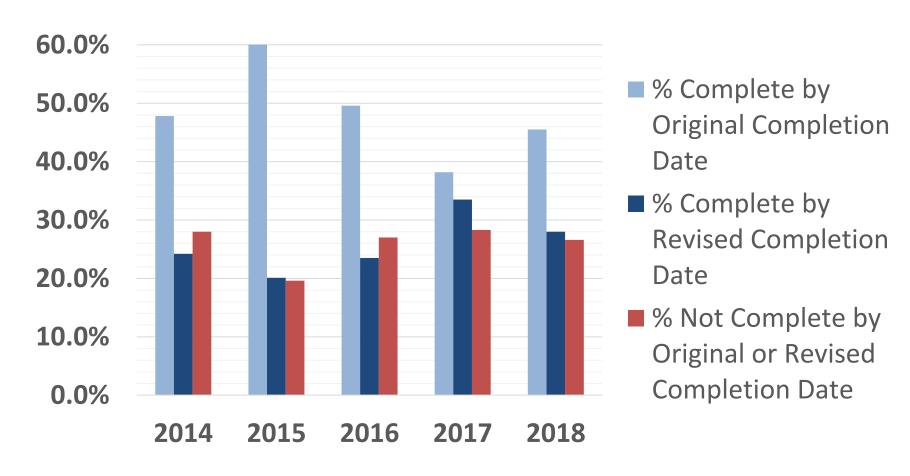

#### Questions?

