


# ANNUAL REPORT FOR 2015



**Shoal Creek Site #29 Mitigation Site  
Yancey County  
TIP No. R-2519A  
COE Action ID: SAW-2007-2197-357/300  
DWR #: 2007-1134V.4**

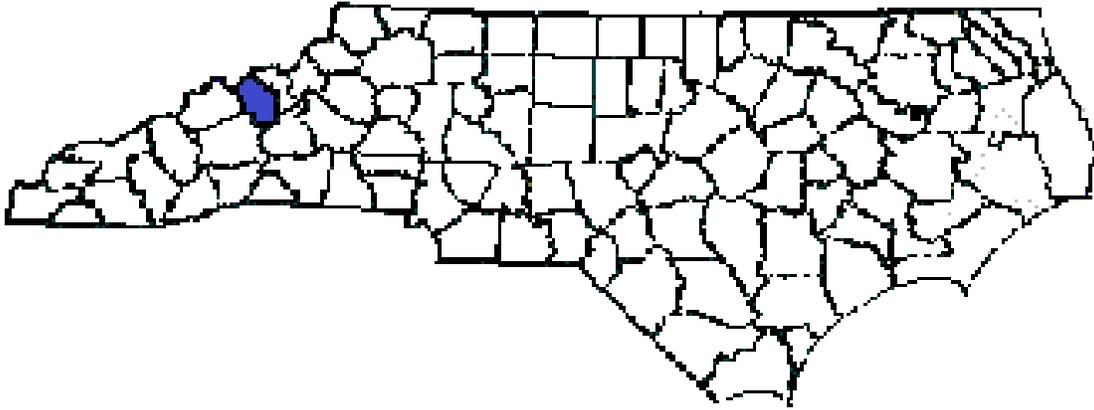

Prepared By:  
Natural Environment Section & Roadside Environmental Unit  
North Carolina Department of Transportation  
November 2015

# TABLE OF CONTENTS

SUMMARY .....	1
1.0 INTRODUCTION:.....	2
.1 Project Description .....	2
.2 Purpose .....	2
.3 Project History .....	2
.4 Debit Ledger.....	2
2.0 STREAM ASSESSMENT: .....	6
.1 Success Criteria .....	6
.2 Stream Description.....	6
.2.1 Post Construction Conditions.....	6
.2.2 Monitoring Conditions .....	6
.3 Results of Stream Monitoring .....	7
.3.1 Site Data .....	7
3.0 VEGETATION.....	8
.1 Description of Species.....	8
.2 Results of Vegetation Monitoring.....	8
.3 Conclusions .....	8
4.0 OVERALL CONCLUSIONS/RECOMMENDATIONS .....	8
5.0 REFERENCES: .....	9

## FIGURES

Figure 1 – Vicinity Map .....	3
Figure 2 – Site #29 Map .....	4
Figure 3 – Site #29 Reforestation Plan .....	5

## TABLES

Table 1 – Site #29 Morphological Summary .....	7
--	---

## APPENDICES

- Appendix A – Cross Sections and Longitudinal Profile
- Appendix B – Site Photographs

## **SUMMARY**

The following report summarizes the stream monitoring activities that have occurred during the Year 2015 at the Shoal Creek Site #29 Mitigation Site in Yancey County. The North Carolina Department of Transportation (NCDOT) completed this project in the fall of 2013. This report provides the monitoring results for the second formal year of monitoring (Year 2015). The Year 2015 monitoring period was the second of five scheduled years of monitoring on the Shoal Creek Site #29 Mitigation Site (See Success Criteria Section 2.1).

Based on the overall conclusions of monitoring at the Shoal Creek Site #29, it has met the required monitoring protocols for the second formal year of monitoring on the stream and the first formal year of monitoring on the planted vegetation. The channel throughout the stream site is stable at this time. The streambank and buffer were planted in March 2015. The planted vegetation is surviving at this time.

NCDOT will continue stream and vegetation monitoring at the Shoal Creek Site #29 Mitigation Site in 2016.

## 1.0 INTRODUCTION

### 1.1 Project Description

The following report summarizes the stream monitoring activities that have occurred during the Year 2015 at the Shoal Creek Site #29 Mitigation Site. Site #29 is located at the intersection of US 19 and Shoal Creek Road in Yancey County at Sta. 10+28 to 10+98 -Y30- Rt. (Figure 1). The Shoal Creek Site #29 was constructed to provide mitigation for stream impacts associated with Transportation Improvement Program (TIP) number R-2519A in Yancey County.

The mitigation site provided approximately 233 linear feet of stream restoration. Construction was completed during Fall 2013 by the NCDOT. The restoration of the Shoal Creek Site #29 Mitigation Site involved backfilling the existing channel so the roadway could be extended. A new floodplain and channel were excavated and cross vanes were installed. The riparian buffer zone was also planted.

### 1.2 Purpose

In order for a mitigation site to be considered successful, the site must meet the success criteria. This report details the monitoring in 2015 at the Shoal Creek Site #29 Mitigation Site. Hydrologic monitoring was not required for this site.


### 1.3 Project History

August 2013	Sprayed Kudzu
Fall 2013	Construction Completed
January 2014	As-Built Survey Completed
May & June 2014	Sprayed Kudzu and Japanese Knotweed
November 2014	Stream Channel Monitoring (Year 1)
March 2015	Site Planted
July 2015	Vegetation Monitoring (Year 1)
July 2015	Sprayed Kudzu and Japanese Knotweed
November 2015	Stream Channel Monitoring (Year 2)

### 1.4 Debit Ledger

The entire Shoal Creek Site #29 stream mitigation site was used for the R-2519A project to compensate for unavoidable stream impacts.

35.916253, -82.248413

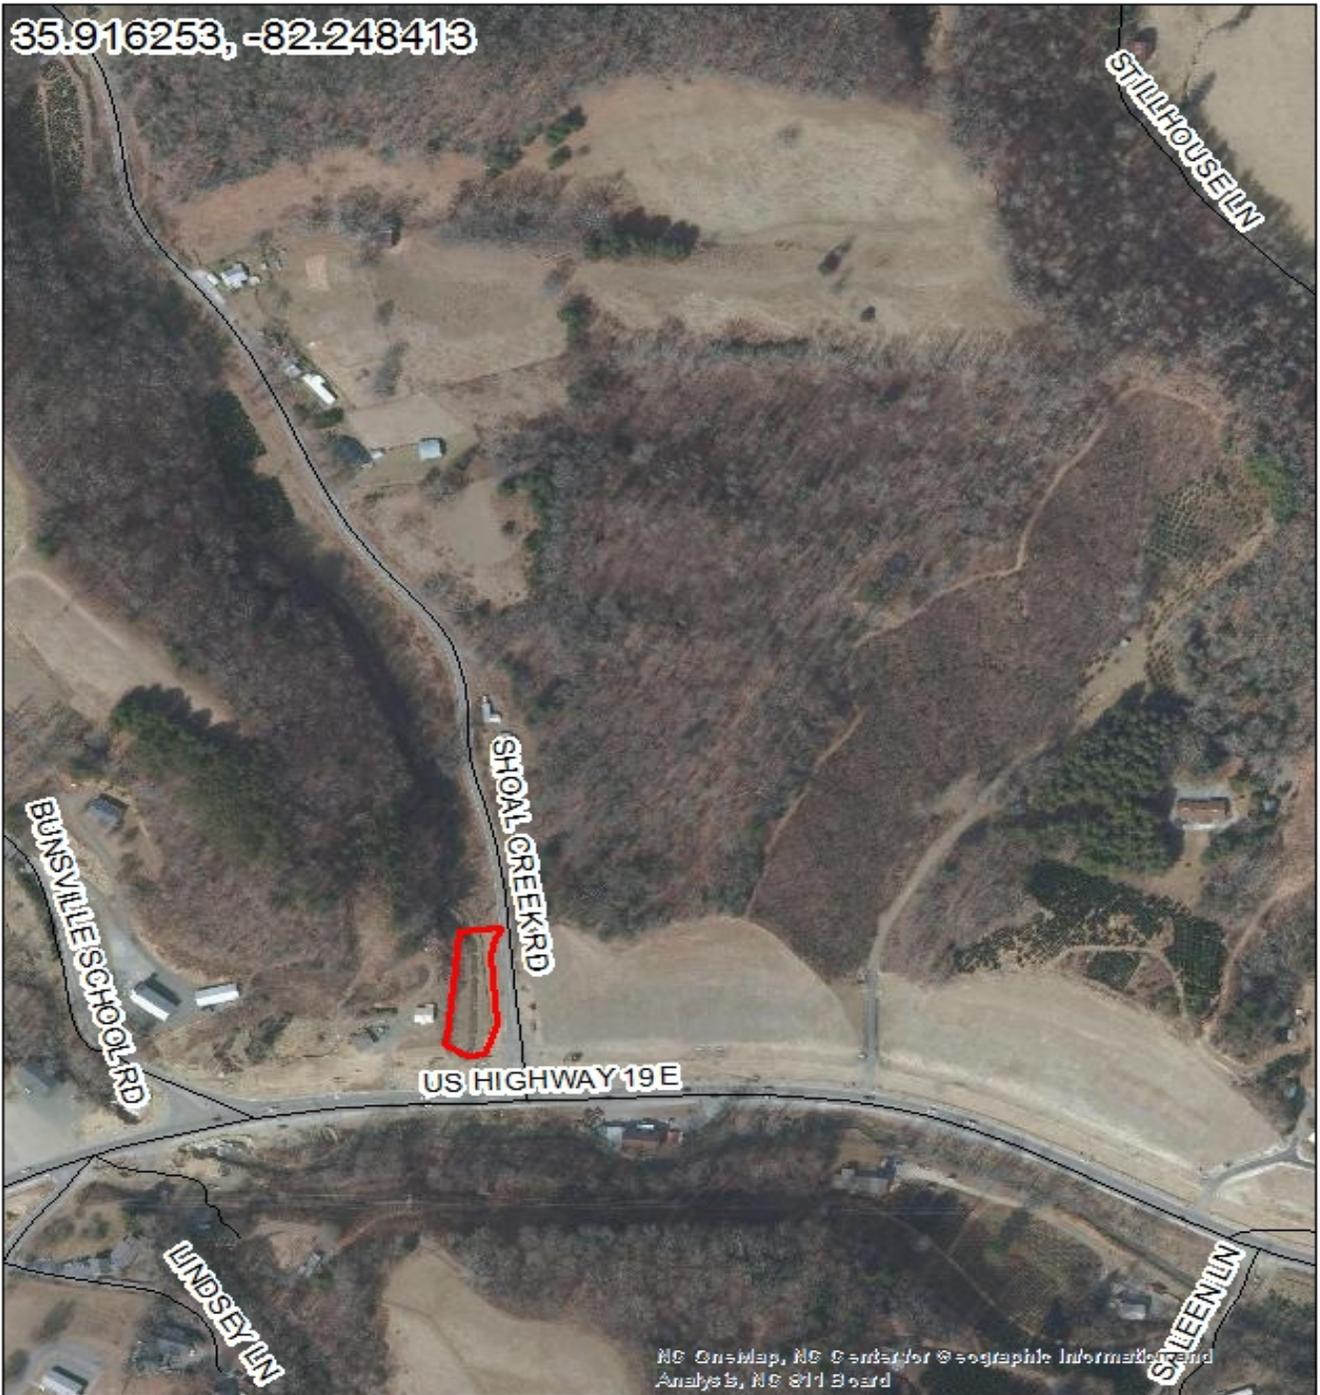

NC OneMap, NC Center for Geographic Information and Analysis, NC GIS Board




Figure 1. Vicinity Map

# SHOAL CREEK STREAM RELOCATION

## PHOTO POINT AND CROSS SECTION LOCATIONS

PROJECT REFERENCE NO.		SHEET NO.	
R/W SHEET NO.		ROADWAY DESIGN ENGINEER	
CONST. REV.		HYDRAULICS ENGINEER	
R/W REV.			





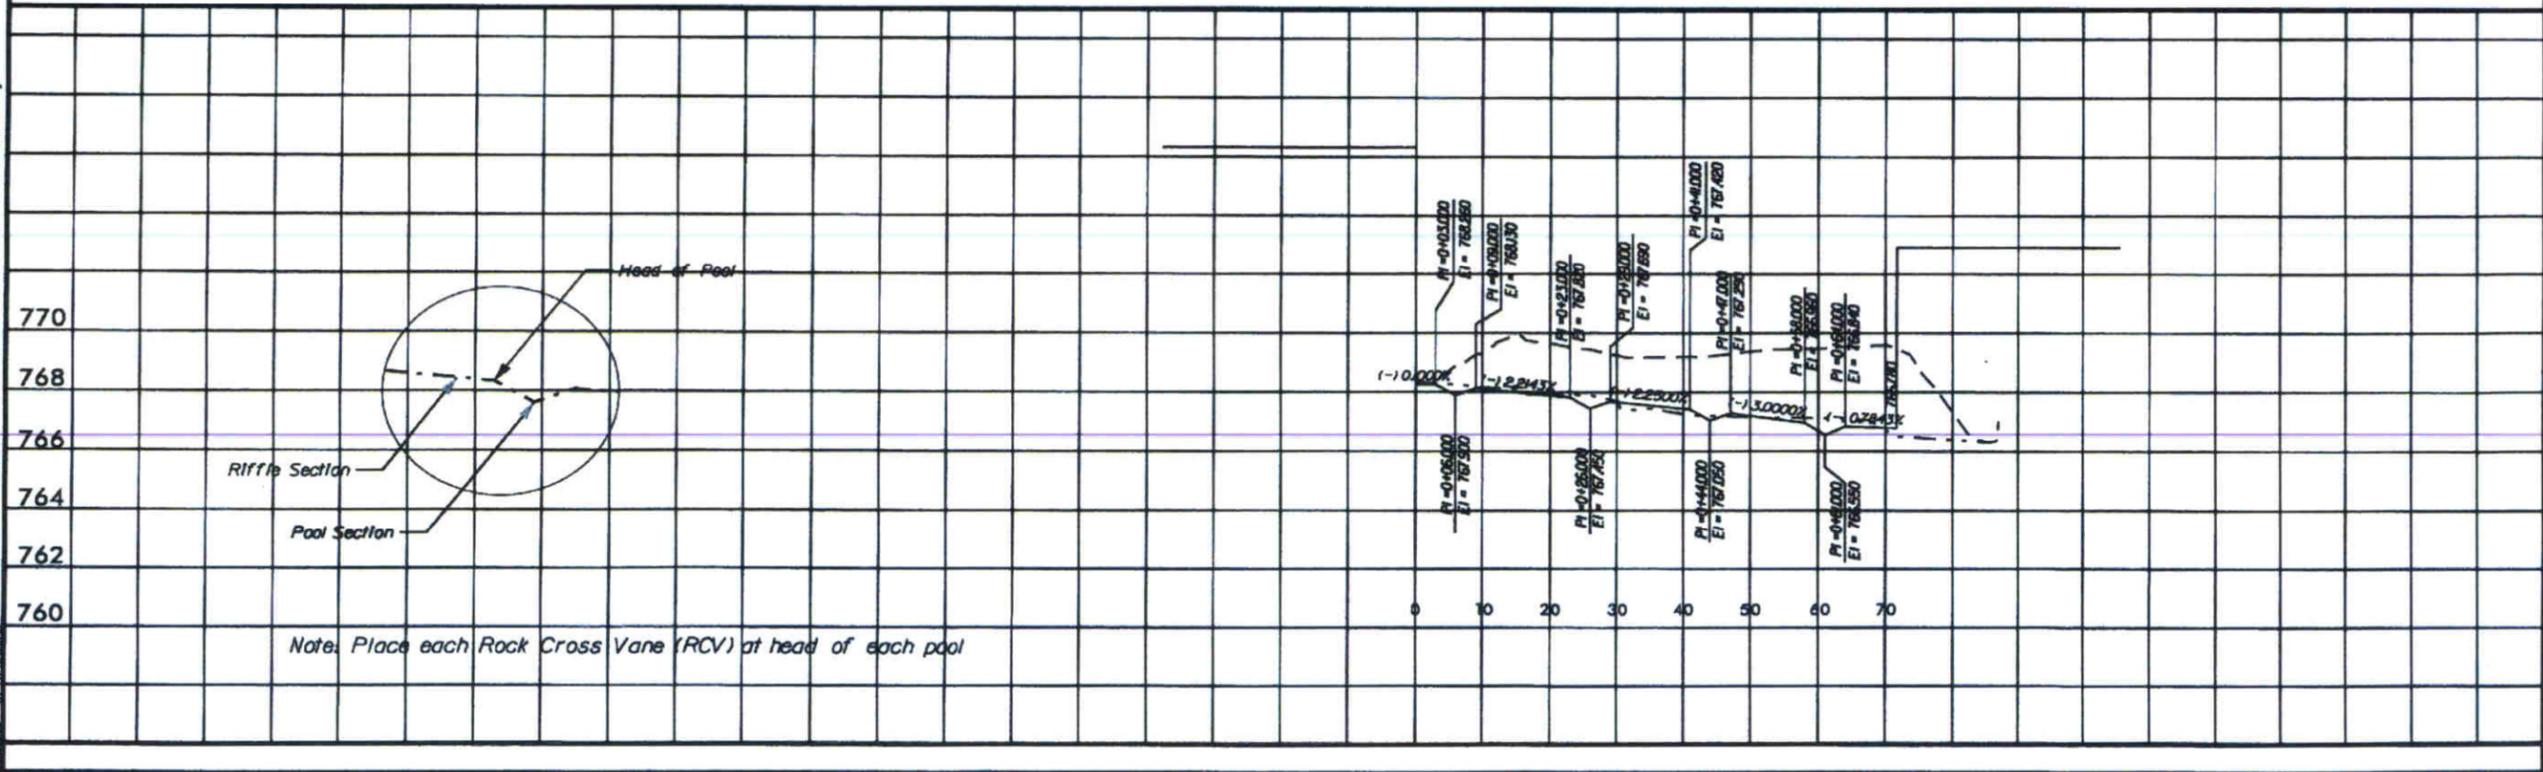


Figure 2. Site #29 Map

# 0.13 HECTARE STREAMBANK REFORESTATION

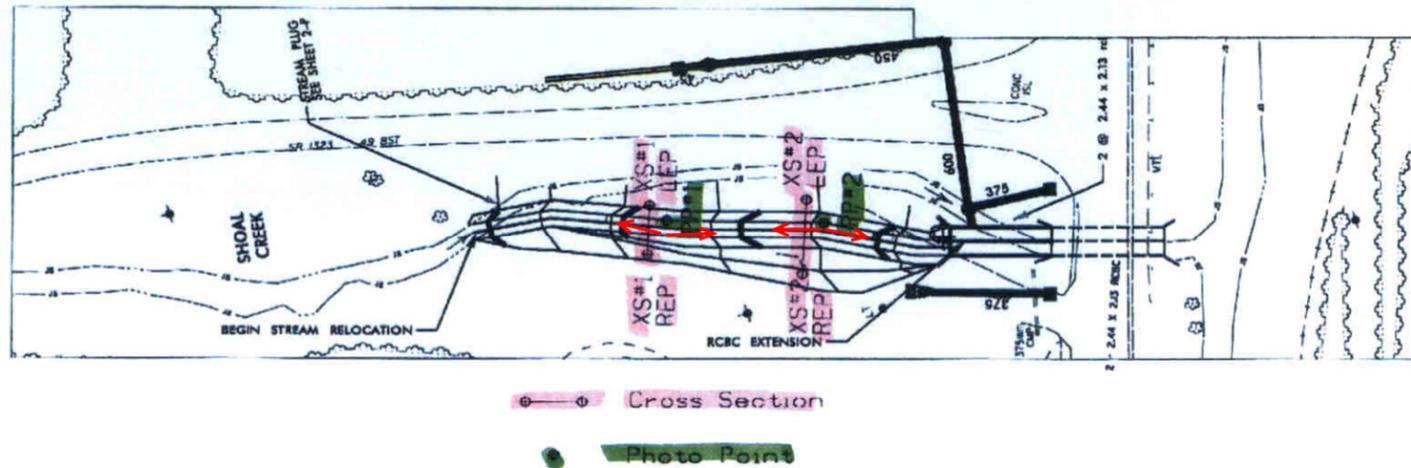

PROJECT REFERENCE NO. R-25/9A	SHEET NO. EC-94/CONST.31
R/W SHEET NO.	
ROADWAY DESIGN ENGINEER	HYDRAULICS ENGINEER

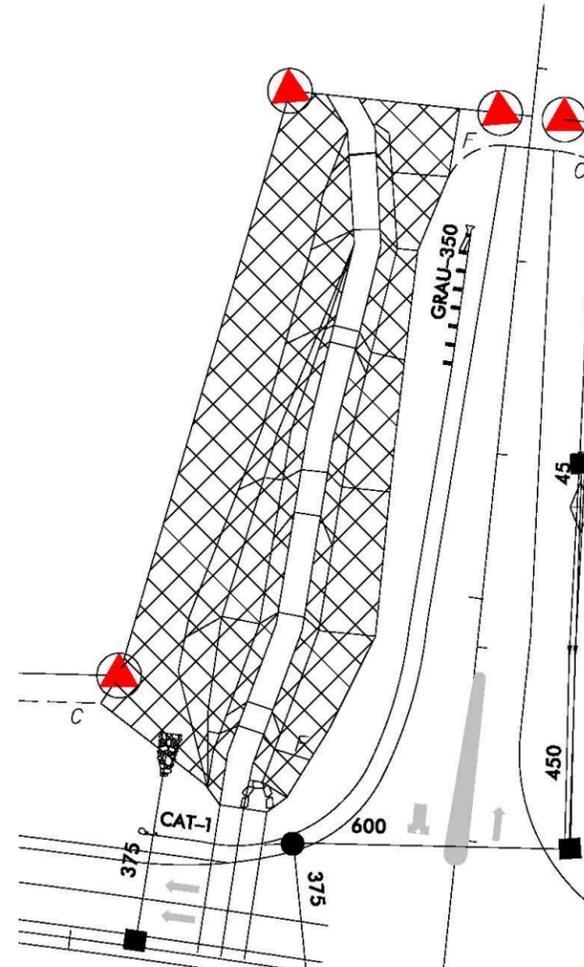

SEE RF-2, RF-3 AND PROJECT SPECIAL PROVISIONS

Figure 3. Site #29 Reforestation Plan

## **2.0 STREAM ASSESSMENT**

### **2.1 Success Criteria**

The permittee shall monitor the stream relocation sites following the Level 1 protocols outlined in the Stream Mitigation Guidelines date April 2003 with the following exceptions:

1. Pebble counts shall not be conducted.
2. Two cross sections shall be conducted for streams less than 500 linear feet and five (5) cross sections shall be conducted for streams greater than 500 linear feet.
3. Riparian success shall be by visual inspection of plant survival. Photos will be taken and comments noted on plant survival.

The monitoring shall be conducted annually for a minimum of five (5) years after final planting. The monitoring results shall be submitted to DWR in a final report within sixty (60) days after completing monitoring. After 5 years the NCDOT shall contact the DWR to schedule a site visit to “close out” the mitigation site.

### **2.2 Stream Description**

#### ***2.2.1 Post-Construction Conditions***

The restoration of the Shoal Creek Site #29 Mitigation Site involved backfilling the existing channel so the roadway could be extended. A new floodplain and channel were excavated and cross vanes were installed. The riparian buffer zone was also planted.

#### ***2.2.2 Monitoring Conditions***

The objective of the Shoal Creek Site #29 stream restoration was to restore a B4 stream as identified in Rosgen’s Applied River Morphology. A total of two cross sections (one in a riffle and one in a pool) were surveyed. For this report, only cross sections containing riffles were used in the comparison of channel morphology presented below in Table 1 (Site #29).

**Table 1. Abbreviated Morphological Summary (Site #29 – Shoal Creek Mitigation Site)**

Variable	Proposed	Cross-Section #2 (Riffle)				
		2014	2015	2016	2017	2018
Drainage Area (mi <sup>2</sup> )	2.72	2.72	2.72			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	30.6	36.94	35.43			
Maximum Bankfull Depth (ft.)	2.13	3.01	3.02			
Width of the Floodprone Area (ft.)	32.8 – 43.3	42	42			
Bankfull Mean Depth (ft.)	1.55	1.8	1.81			
Width/Depth Ratio	12.7	11.37	10.83			
Entrenchment Ratio	1.7 – 2.2	2.05	2.14			
Bankfull Width (ft.)	19.7	20.47	19.61			

\* Riffle values are used for classification purposes, pool values are shown in Appendix A.

## 2.3 Results of the Stream Assessment

### 2.3.1 Site Data

The assessment included the survey of two cross sections and the longitudinal profile of the Shoal Creek Site #29 Mitigation Site established by NCDOT after construction. The length of the profile along the Shoal Creek Site #29 Mitigation Site was approximately 233 linear feet. Two cross sections were established during the as-built monitoring year. Cross section locations were subsequently based on the stationing of the longitudinal profile and are presented below. The location of the cross sections and longitudinal profile are shown in Appendix A.

Shoal Creek Site #29 Cross-Sections:

- ◆ Cross-Section #1: Shoal Creek Site #29, Station 91+00, midpoint of pool
- ◆ Cross-Section #2: Shoal Creek Site #29, Station 169+00, midpoint of riffle

Based on comparisons of the As-Built to the monitoring data, all of the cross sections appear stable with little or no active bank erosion. Graphs of the cross sections are presented in Appendix A. Future survey data will vary depending on actual location of rod placement and alignment; however, this information should remain similar in appearance. The longitudinal profile showed that the channel was stable for the 2015 monitoring evaluation. Pebble counts were not required per the permit conditions and therefore were not completed. Two bankfull events were documented visually by a noted wrack line at Site #29 during the 2014 and 2015 monitoring years.

### **3.0 VEGETATION: SHOAL CREEK SITE #29**

#### **3.1 Description of Species**

The following tree species were planted on the streambank:

*Salix sericea*, Silky Willow

*Cornus amomum*, Silky Dogwood

The following tree species were planted in the buffer area:

*Liriodendron tulipifera*, Yellow Poplar

*Platanus occidentalis*, Sycamore

*Fraxinus pennsylvanica*, Green Ash

*Quercus alba*, White Oak

#### **3.2 Results of Vegetation Monitoring**

**Streambank & Buffer Vegetation:** The streambank reforestation was completed in March 2015. The Year 1 vegetation monitoring evaluation noted Type I: Silky Willow and Silky Dogwood and Type II: Yellow Poplar, Sycamore, Green Ash, and White Oak were surviving at the time of the monitoring evaluation. The kudzu and Japanese knotweed that was noted onsite was sprayed in July 2015.

#### **3.3 Conclusions**

NCDOT will continue to monitor the planted vegetation in 2015 and will continue to spray the invasive species as needed.

### **4.0 OVERALL CONCLUSIONS/RECOMMENDATIONS**

The Shoal Creek Site #29 Mitigation Site has met the required monitoring protocols for the second formal year of monitoring on the stream and the first formal year of monitoring on the planted vegetation. The channel throughout the stream site is stable and the planted vegetation is surviving at this time.

NCDOT will continue stream and vegetation monitoring at the Shoal Creek Site #29 Mitigation Site in 2016.

## 5.0 REFERENCES

R-2519A, US 19 from East of SR 1336 (Jacks Creek Road) to SR 1186 (Old US 19), Yancey County, Division 13: Natural Stream Design For: Site 29, Shoal Creek Sta. 10+28 to 10+98 -Y30- Rt.

Permit Mod. R-2519A, Yancey County from SR 1336 (Jacks Creek Road) to SR 1186 (Old US 19) west of Micaville, Action ID No. SAW-2007-2197-357/300 and DWQ Project No. 2007-1134V.4, February 4, 2010

As-Built Report for Stream Relocations on R-2519A, Yancey County, TIP Project No. R-2519A, USACE Permit No. 2007-2197-357/300, WQC#3706, DWQ Project #20071134V.4

Rosgen, D.L, 1996. Applied River Morphology. Wildland Hydrology, Pagosa Springs, Colorado.


US Army Corps of Engineers (USACE), 2003. Stream Mitigation Guidelines. Prepared with cooperation from the US Environmental Protection Agency, NC Wildlife Resources Commission, and the NC Division of Water Resources.

## **APPENDIX A**

### **CROSS SECTIONS AND LONGITUDINAL PROFILE**

### R-2519A Site 29 XS#1 @ STA 91+00

○ 2015 Year 2 R-2519A Site 29 XS#1 @ STA 91+00    
 ◆ Bankfull Indicators    
 ▼ Water Surface Points    
 △ 2014 Year 1 R-2519A Site 29 XS#1 @ Sta. 91+00    
 ▲ 2014 As-built R-2519A Site 29 XS#1 @ Sta. 91+00

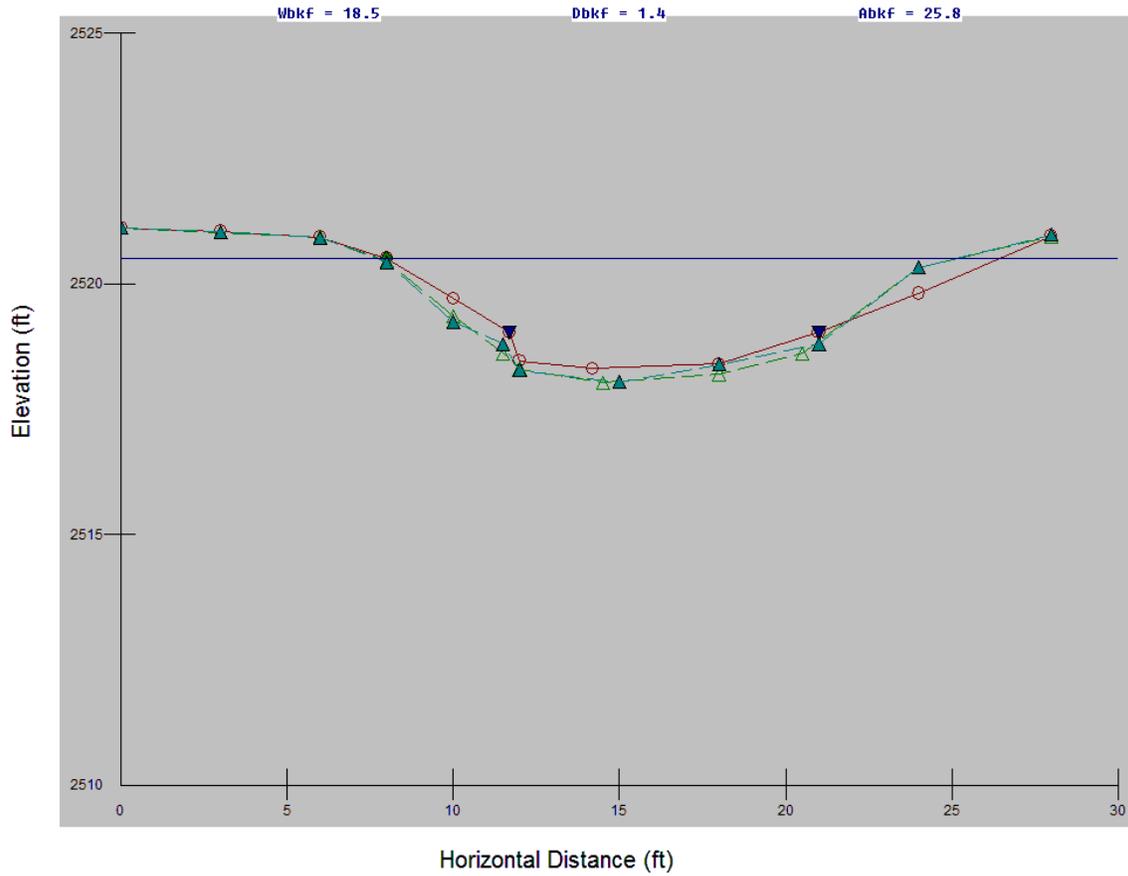


Site #29: Cross-Section #1 (Pool) Abbreviated Morphological Summary					
	2014	2015	2016	2017	2018
<b>Bankfull Cross Sectional Area (ft<sup>2</sup>)</b>	24.81	25.81			
<b>Maximum Bankfull Depth (ft.)</b>	2.3	2.21			
<b>Bankfull Mean Depth (ft.)</b>	1.57	1.4			
<b>Bankfull Width (ft.)</b>	15.78	18.47			

\*According to the Rosgen Classification of Natural Rivers floodprone width, entrenchment ratio, and width depth ratio are not measured in pool, glide, or run features.


### R-2519A Site 29 XS#2 @ STA 169+00

○ 2015 Year 2 R-2519A Site 29 XS#2 169+00    ◆ Bankfull Indicators    ▼ Water Surface Points    △ 2014 Year 1 R-2519A Site 29 XS#2 @ Sta. 169+00    ▲ 2014 As-built R-2519A Site 29 XS#2 @ Sta. 169+00

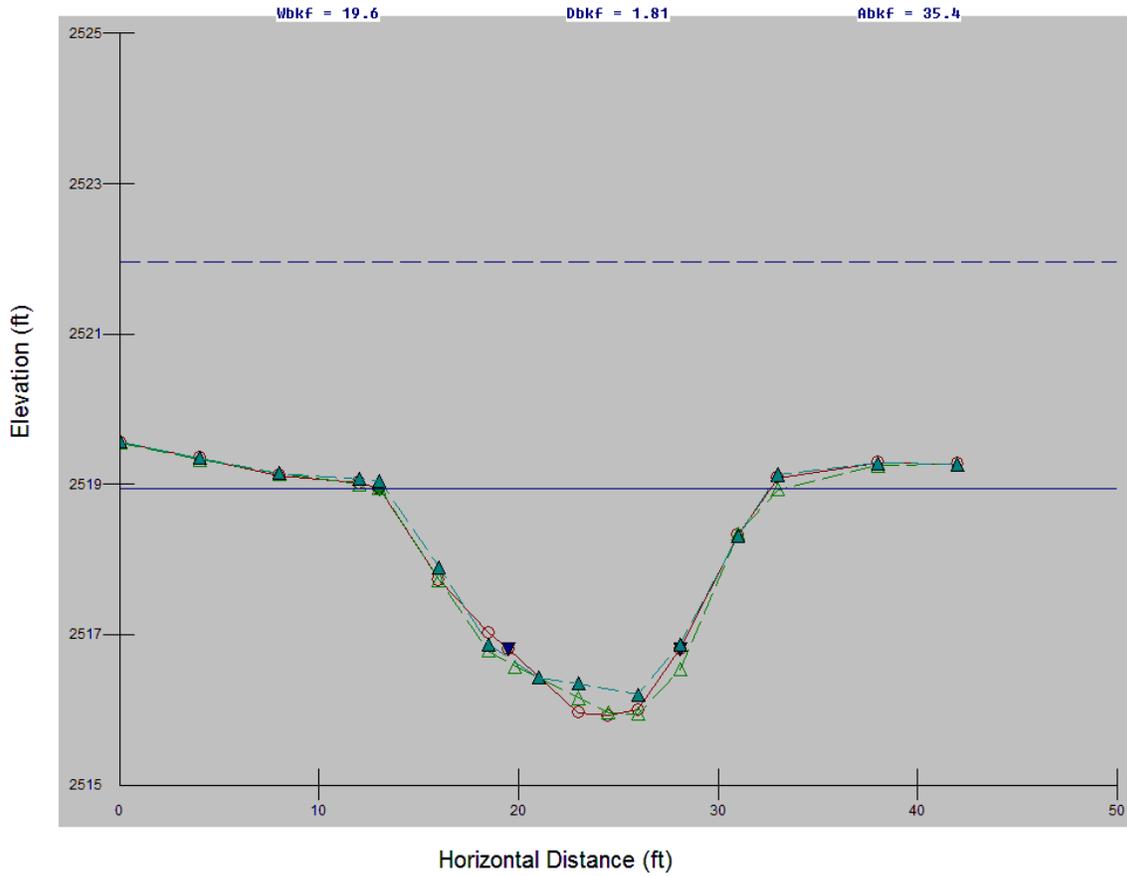

Site #29: Cross-Section #2 (Riffle) Abbreviated Morphological Summary					
	2014	2015	2016	2017	2018
Bankfull Cross Sectional Area (ft <sup>2</sup> )	36.94	35.43			
Maximum Bankfull Depth (ft.)	3.01	3.02			
Width of the Floodprone Area (ft.)	42	42			
Bankfull Mean Depth (ft.)	1.8	1.81			
Width/Depth Ratio	11.37	10.83			
Entrenchment Ratio	2.05	2.14			
Bankfull Width (ft.)	20.47	19.61			

### 2015 Year 2 R-2519A Site 29 Profile

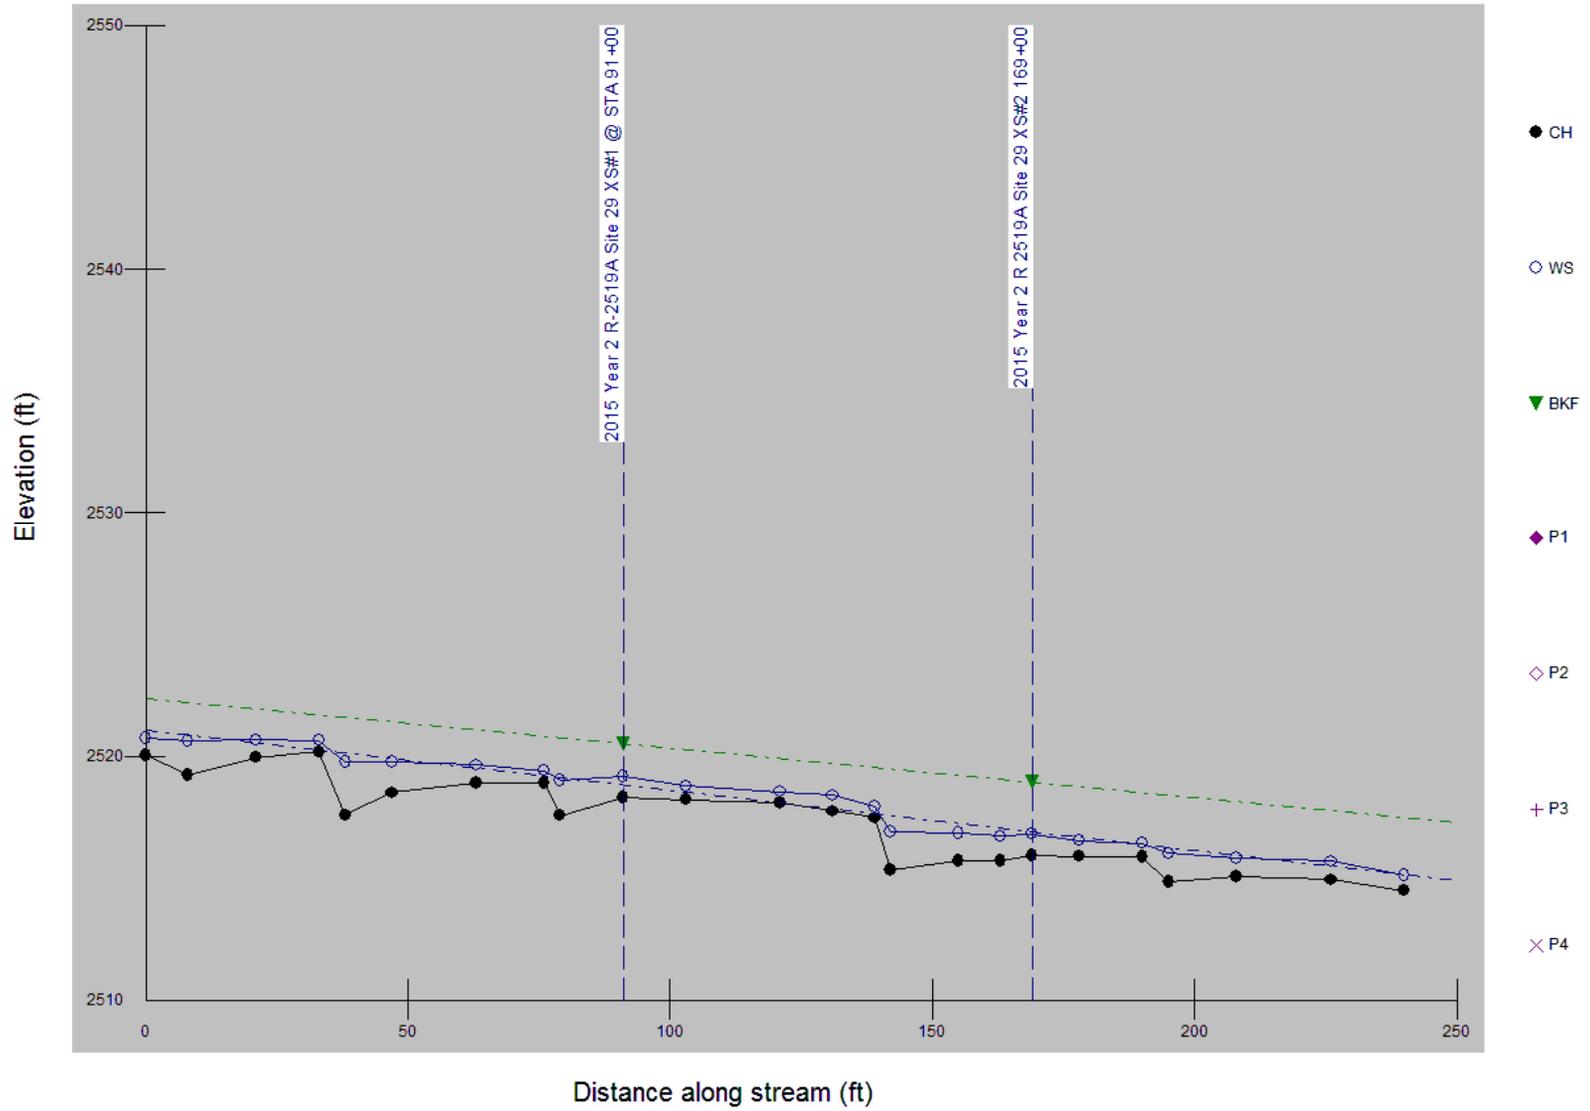

**APPENDIX B**  
**SITE PHOTOGRAPHS**

# Shoal Creek Site #29



Photo Point #1 (Upstream)



Photo Point #1 (Downstream)



Photo Point #2 (Upstream)



Photo Point #2 (Downstream)

November 2015

# Shoal Creek Site #29



Vegetation Overview Photo

July 2015
