


PAY RECORD BOOK ENTRY EXAMPLE

Line Code #284 Grooving Bridge Floors

6,220 SF @ \$ 0.65

8

Station	Rt./Lt.	Span	SF	Date	Initials	Remarks
103+35.85	Lt./Rt.	"A"	1992.9	9-23-98	DK7	Completed satisfactorily.

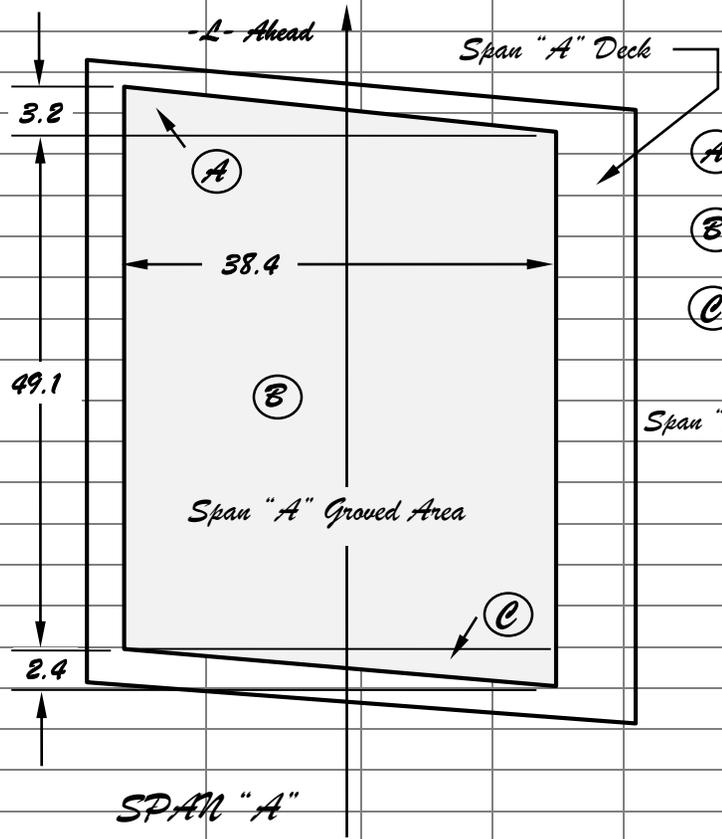

- (A) $0.5 \times 3.2 \times 38.4 = 61.4$
- (B) $38.4 \times 49.1 = 1,885.4$
- (C) $0.5 \times 2.4 \times 38.4 = 46.1$

Span "A" Total: 1,992.9

Page Total: 1992.9 9-23-98 DK7

Checked By: ML7
Date: 6-19-99


PAY RECORD BOOK ENTRY EXAMPLE

Line Code #284 Grooving Bridge Floors

6,220 SF @ \$ 0.65

38

<i>Station</i>	<i>Rt./Lt.</i>	<i>Span</i>	<i>SF</i>	<i>Date</i>	<i>Initials</i>	<i>Remarks</i>
<i>103+35.85</i>	<i>Lt./Rt.</i>	<i>"A"</i>	<i>1992.9</i>	<i>DK7</i>	<i>9-23-98</i>	<i>Completed satisfactorily.</i>

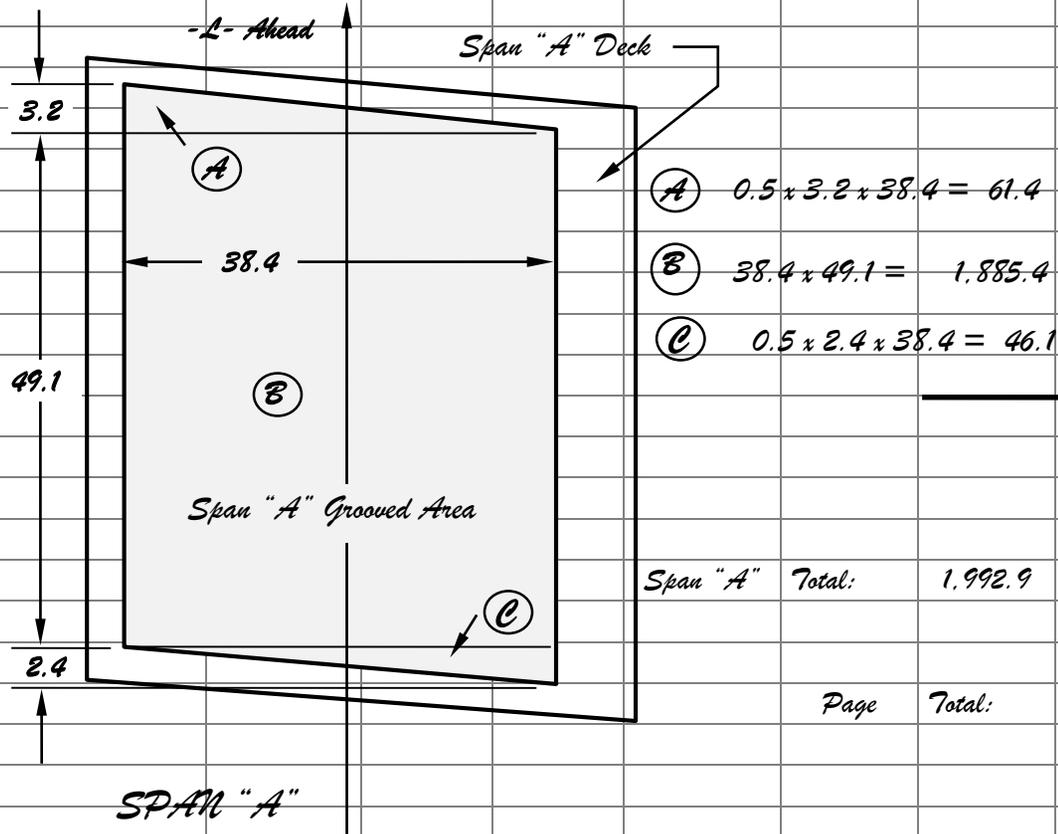

Span "A" Total: 1,992.9

Page Total: 1992.9 DK7 9-23-98

*Checked By: ML7
Date: 6-19-99*
