



Florence & Hutcheson

CONSULTING ENGINEERS

Project: WBS 33604.3.1 (B-4262)
Bridge #217 on SR 1520 over Tributary to Cathy's Creek
Rutherford County

To: Meeting Attendees
Subject: Revised MINUTES OF MEETING
Date Prepared: November 18, 2010
Prepared by: Jim Mondolfi

PURPOSE/DESCRIPTION:		Pre-Bid Meeting
DATE & TIME:		Wednesday, October 27, 2010 10:30 AM
LOCATION:		NCDOT Bridge Management Unit Large Conference Room Raleigh, North Carolina
ATTENDEES		
Name	Representing	Telephone Number
	See Meeting Roster	
Jim Mondolfi	Ko/Florence & Hutcheson, Inc.	919-851-6066

The following is my understanding of items discussed:

- 1) On Page 6 of the Proposal, the revised date of availability for this contract is the date the Contractor begins work, but not before the issuance of the Purchase Order and no later than July 1, 2011.
- 2) On Page 7 of the Proposal under Section H, "Traffic Control", add statement "The Contractor will be responsible for stripping and all pavement markings". Cost of stripping and pavement markings shall be included in the lump sum price bid for Item "Generic Traffic Control".
- 3) Item "Generic Traffic Control" is added to the contract. A revised bid sheet is attached.
- 4) On Page 9 of the Proposal under Section N, Paragraph 1, the Engineer for this project will be Mr. Gary Moore.

- 5) On Page 16 of the Proposal under "Good Faith Effort for Projects with Goals More Than Zero", submit only one copy of the DBE information required to the Bridge Management office.
- 6) The Contractor will remove and salvage the existing steel beams, diaphragms, three beam bridge rail and bridge rail posts to the Division. The steel will be delivered to the Rutherford County maintenance yard located at 909 Ledbetter Road, Spindale, NC 28160. Contact Scott Bailey. Phone #828-286-3191.
- 7) A list of prequalified suppliers of aluminum box culverts is attached.
- 8) Shop drawings for the aluminum box culvert will be submitted to the NCDOT Bridge Management Unit for review.
- 9) Boring logs and soil profile sheets are attached.
- 10) Item "Select Granular Backfill" is added to the contract. A revised bid sheet is attached.
- 11) The quantity for item "Filter Fabric for Drainage, Type 2" is increased from 710 SY to 1270 SY. A revised bid sheet is attached.
- 12) A sketch of the headwalls is attached for information only.
- 13) Backfill along the full length of the culvert with Select Granular Material for a width of four feet up to the height of the culvert. "Select Granular Material, Class 4 or Class 6" shall be used, or as per the recommendations of the manufacturer and as directed by the Engineer. Refer to Sections 265 and 300 of the Standard Specifications.
- 14) A pre-installation meeting is required prior to installation. Representatives from the Contractor, the Aluminum Culvert Manufacturer and the Department shall attend this meeting. The Aluminum Box Culvert Manufacturer shall be on site during installation.

JEM/

BID SHEETS (Revised 11-1-10)**CONTRACT COST PROPOSAL**

The Contractor agrees to provide the services outlined in this proposal for the following fixed price:

BRIDGE REPLACEMENT WITH AN ALUMINUM BOX CULVERT

LINE NO.	ITEM NO.	SEC NO.	DESCRIPTION	QUANTITY	UNIT COST	AMOUNT
1.	0000100000-N	800	MOBILIZATION	LS	<u>LS</u>	_____
2.	0195000000-E	265	SELECT GRANULAR MATERIAL	400 CY	_____	_____
3.	0248000000-N	SP	GENERIC GRADING ITEM (EXCAVATION AND EMBANKMENT)	LS	<u>LS</u>	_____
4.	0318000000-E	300	FOUNDATION CONDITIONING MATERIAL, MINOR STRUCTURES	20 TON	_____	_____
5.	0366000000-E	310	15" RC PIPE CULVERT, CL III	112 LIN. FT.	_____	_____
6.	0372000000-E	310	18" RC PIPE CULVERT, CL III	68 LIN. FT.	_____	_____
7.	0995000000-E	340	PIPE REMOVAL	112 LIN. FT.	_____	_____
8.	1220000000-E	545	INCIDENTAL STONE BASE	100 TON	_____	_____
9.	1489000000-E	610	ASPHALT CONCRETE BASE COURSE, TYPE B 25.0B	200 TON	_____	_____
10.	1525000000-E	610	ASPHALT CONCRETE SURFACE COURSE, TYPE SF 9.5A	175 TON	_____	_____
11.	1560000000-E	620	ASPHALT BINDER FOR PLANT MIX, TYPE PG 64-22	20 TON	_____	_____
12.	3030000000-E	862	STEEL BEAM GUARDRAIL	150 LIN. FT.	_____	_____
13.	3045000000-E	862	STEEL BEAM GUARDRAIL (SHOP CURVED)	100 LIN. FT.	_____	_____
14.	3150000000-N	862	ADDITIONAL GUARDRAIL POSTS	5 EACH	_____	_____
15.	3195000000-N	862	GUARDRAIL ANCHOR UNIT, TYPE AT-1	4 EACH	_____	_____

Revised 11-1-10

LINE NO.	ITEM NO.	SEC NO.	DESCRIPTION	QUANTITY	UNIT COST	AMOUNT
16.	3656000000-E	876	FILTER FABRIC FOR DRAINAGE, TYPE 2	1270 SY	_____	_____
17.	4589000000-N	1101	GENERIC TRAFFIC CONTROL ITEM	LS	_____ <u>LS</u>	_____
18.	6000000000-E	1605	TEMPORARY SILT FENCE	975 LIN. FT.	_____	_____
19.	6006000000-E	1610	STONE FOR EROSION CONTROL, CLASS A	135 TON	_____	_____
20.	6009000000-E	1610	STONE FOR EROSION CONTROL, CLASS B	75 TON	_____	_____
21.	6012000000-E	SP	SEDIMENT CONTROL STONE	130 TON	_____	_____
22.	6024000000-E	1622	TEMPORARY SLOPE DRAINS	200 LIN. FT.	_____	_____
23.	6027000000-N	1622	INLET PROTECTION AT TEMPORARY SLOPE DRAINS	4 EACH	_____	_____
24.	6029000000-E	SP	SAFETY FENCE	800 LIN. FT.	_____	_____
25.	6030000000-E	1630	SILT EXCAVATION	115 CY	_____	_____
26.	6036000000-E	1631	MATTING FOR EROSION CONTROL	2,000 SY	_____	_____
27.	6038000000-E	SP	PERMANENT SOIL REINFORCEMENT MAT	350 SY	_____	_____
28.	6042000000-E	SP	¼" HARDWARE CLOTH	50 LIN. FT.	_____	_____
29.	6070000000-N	SP	SPECIAL STILLING BASINS	4 EACH	_____	_____
30.	6071010000-E	SP	WATTLE	55 LIN. FT.	_____	_____
31.	6071020000-E	SP	POLYACRYLAMIDE	30 LB.	_____	_____
32.	6071030000-E	SP	COIR FIBER BAFFLE	60 LIN. FT.	_____	_____

Revised 11-1-10

LINE NO.	ITEM NO.	SEC NO.	DESCRIPTION	QUANTITY	UNIT COST	AMOUNT
33.	6111000000-E	SP	IMPERVIOUS DIKE	30 LIN. FT.	_____	_____
34.	6133000000-N	SP	GENERIC EROSION CONTROL	LS	_____ <u>LS</u> _____	_____
35.	8035000000-N	402	REMOVAL OF EXISTING STRUCTURES	LS	_____ <u>LS</u> _____	_____
36.	8133000000-E	414	FOUNDATION CONDITIONING MATERIAL	139 TON	_____	_____
37.	8175000000-E	420	CLASS 'AA' CONCRETE	10.3 CY	_____	_____
38.	8217000000-E	425	REINFORCING STEEL	2,710 LB	_____	_____
39.	8590000000-E	876	PLAIN RIP RAP, CLASS I	55 TON	_____	_____
40.	8594000000-E	876	PLAIN RIP RAP, CLASS B	5 TON	_____	_____
41.	8804000000-N	SP	7'-9" X 32'-7" ALUMINUM BOX CULVERT	LS	_____ <u>LS</u> _____	_____

TOTAL PROJECT BID _____

Wafa, Zaki H

From: Wilson, Troy S
Sent: Friday, November 12, 2010 8:23 AM
To: Wafa, Zaki H
Cc: Moore, Garry L
Subject: Approved Pipe Vendors List and Web site B-4262 Rutherford #217

Zaki,

Here is the link to the web site and a copy of the suppliers. We also sent a headwall detail for the pipe. Please let me know if you need additional information.

Thanks,
Troy


<https://apps.dot.state.nc.us/vendor/approvedproducts/Producer.aspx>

Product ID	Producer Name	Facility Name	Facility Type	Plant ID
Contech Construction Products, Inc.	Contech Construction Products, Inc.	Contech Const. Prod, Inc. - Charlotte	Metal Pipe	MP11
Contech Construction Products, Inc.	Contech Construction Products, Inc.	Contech Const. Prod., Inc. - Raleigh	Metal Pipe	MP1
Contech Construction Products, Inc.	Contech Construction Products, Inc.	Contech Const. Prod., Inc. - Winchester, KY	Metal Pipe	MP14
Contech Construction Products, Inc.	Contech Construction Products, Inc.	Contech Const. Prod., Inc. - Conyers, GA	Metal Pipe	MP10
Contech Construction Products, Inc.	Contech Construction Products, Inc.	Contech Const. Prod., Englewood, Tn.	Metal Pipe	MP20
Contech Construction Products, Inc.	Contech Construction Products, Inc.	Contech Const. Prod., Inc - Ashland	Metal Pipe	MP22
Lane Enterprises, Inc.	Lane Enterprises, Inc.	Lane Enterprises, Inc. - Dublin	Metal Pipe	MP17
Lane Enterprises, Inc.	Lane Enterprises, Inc.	Lane Enterprises, Inc. - Bedford	Metal Pipe	MP8
Lane Enterprises, Inc.	Lane Enterprises, Inc.	Lane Enterprises, Inc. - Statesville	Metal Pipe	MP3
Lane Enterprises, Inc.	Lane Enterprises, Inc.	Lane Enterprises, Inc. - Pulaski	Metal Pipe	MP5
Lane Enterprises, Inc.	Lane Enterprises, Inc.	Lane Enterprises, Inc. - Bealeton	Metal Pipe	MP9
Smith Setzer & Sons	Smith Setzer & Sons	Smith Setzer & Sons - Catawba	Metal Pipe	MP6
Southeast Culvert, Inc	Southeast Culvert, Inc	Southeast Culvert, Inc	Metal Pipe	MP21
Southeastern Pipe & Drain Systems.	Southeastern Pipe & Drain Systems,	Southeastern Pipe & Drain Systems,	Metal Pipe	MP18

11/12/2010


CROSS SECTION END BENT ONE

BRIDGE NO. 217
33604.1.1 (B-4262)

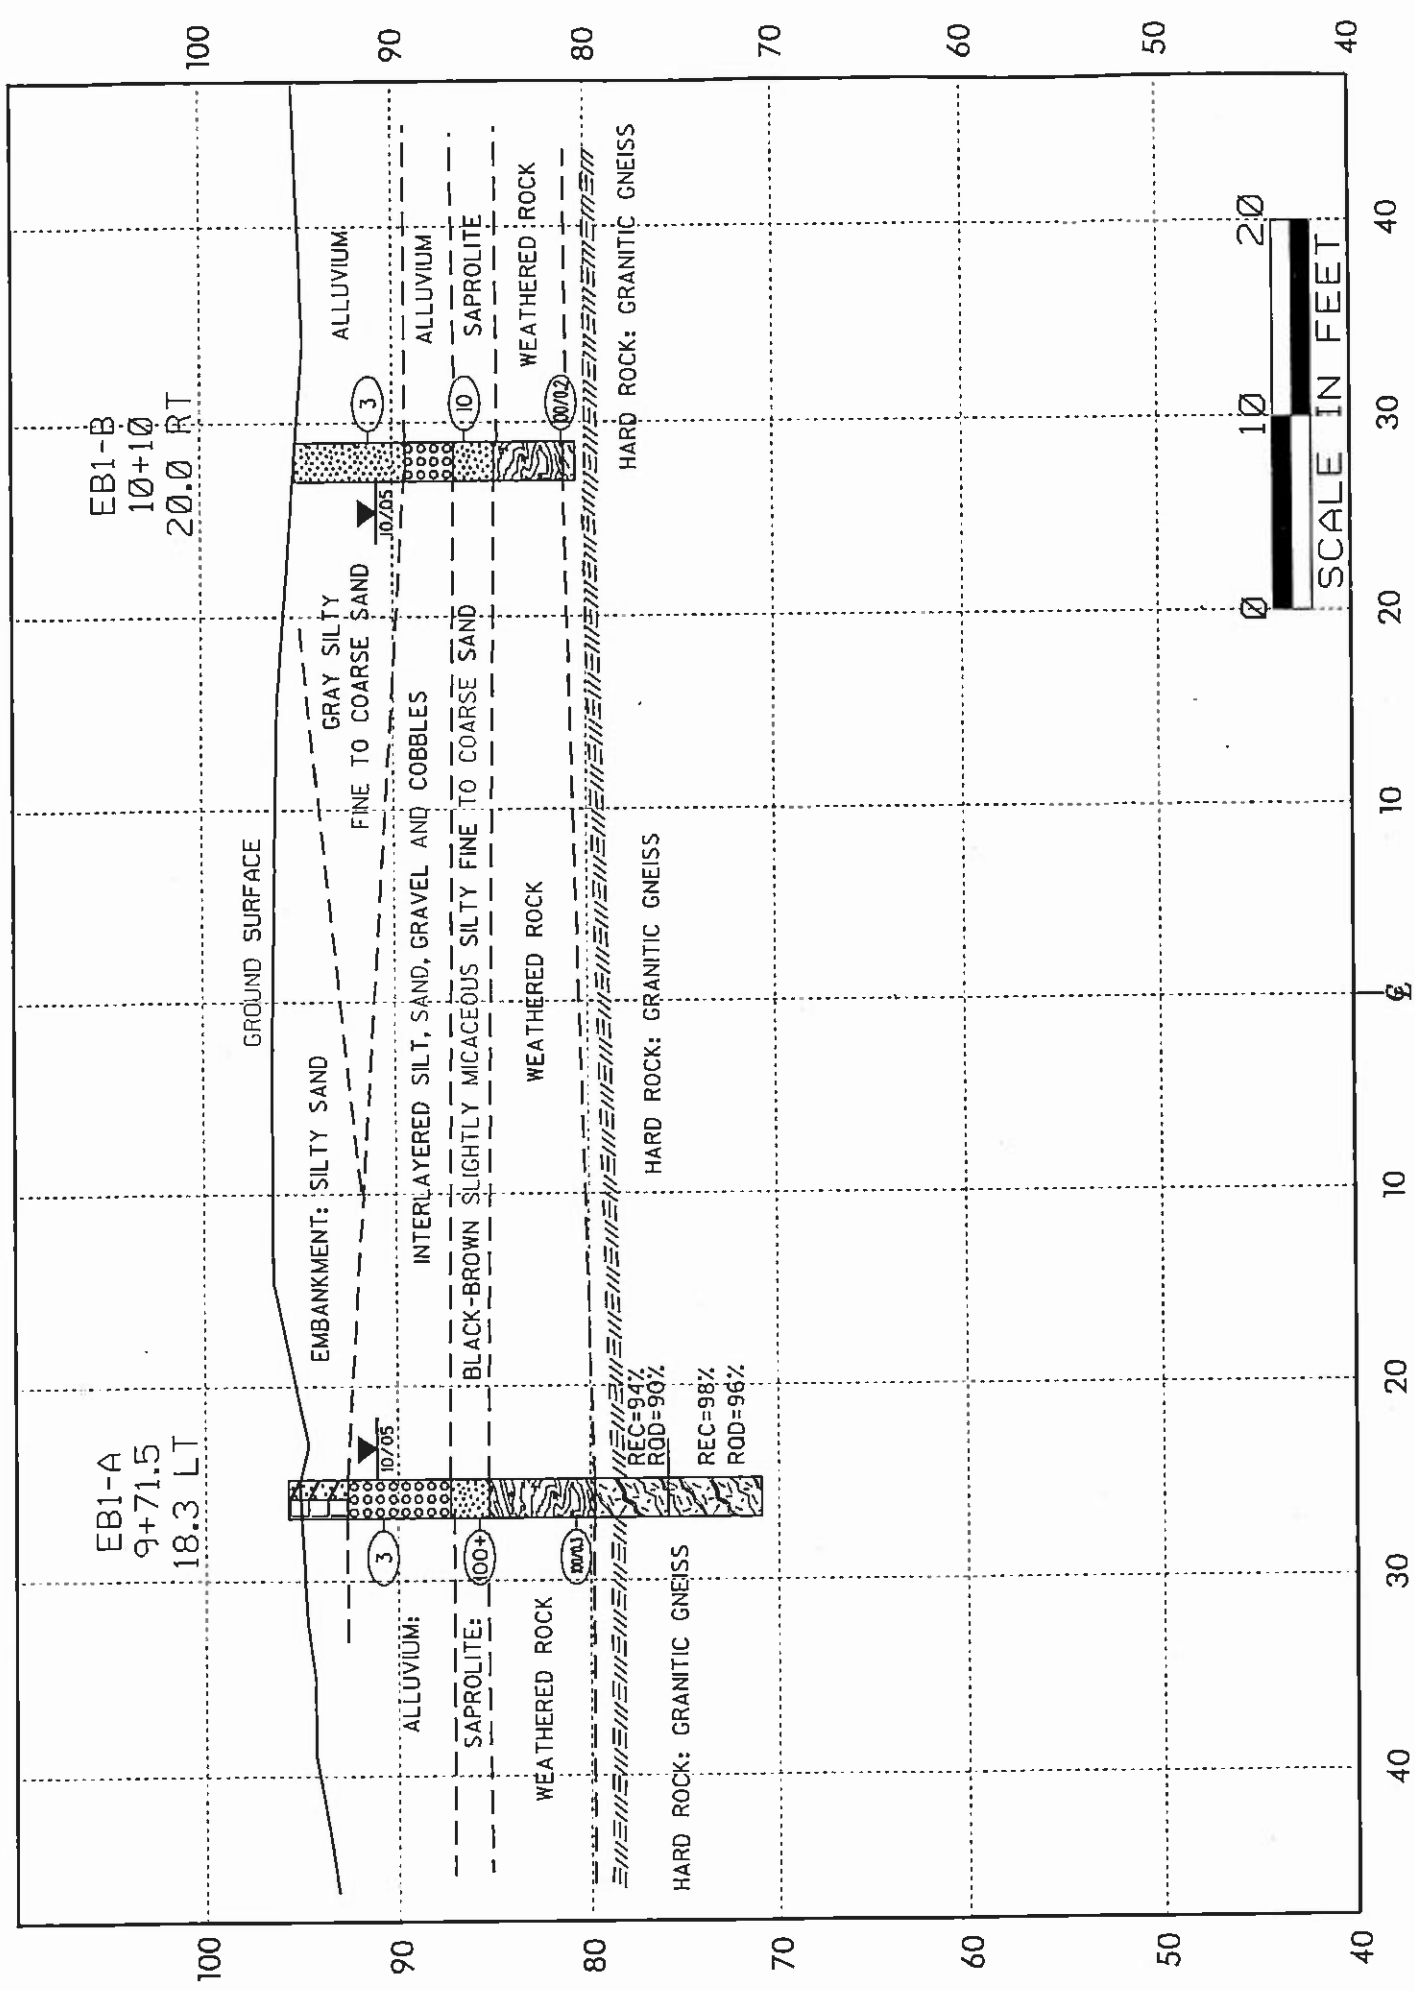

CROSS SECTION THRU END BENT TWO

BRIDGE NO. 217
33604.1.1 (B-4262)

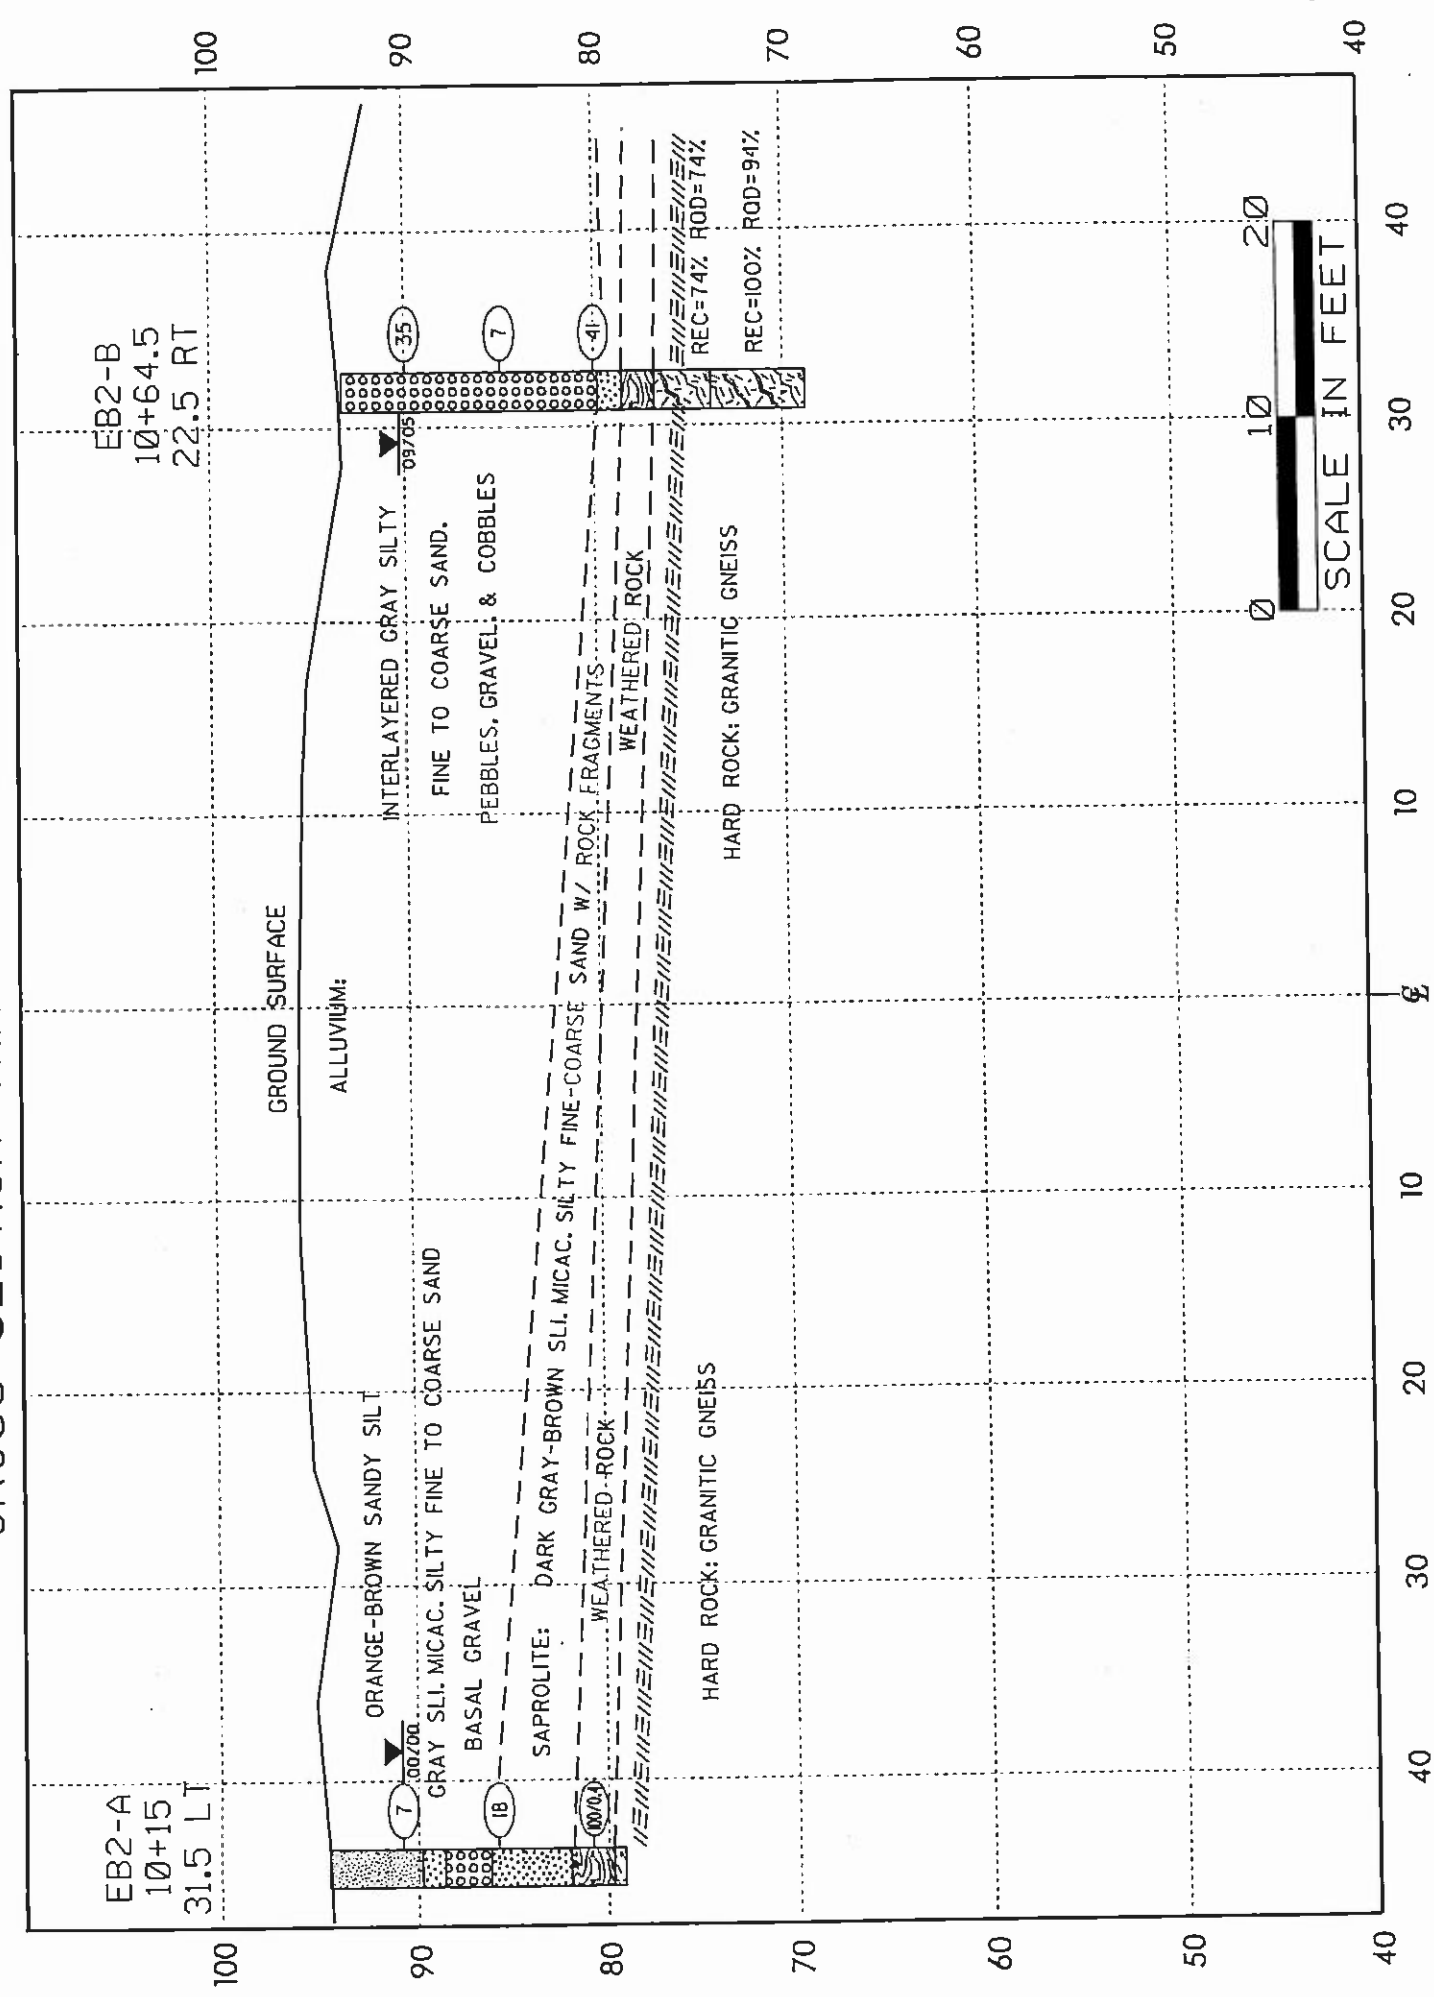

NORTH CAROLINA DEPARTMENT OF TRANSPORTATION
GEOTECHNICAL UNIT BORING LOG

NORTH CAROLINA DEPARTMENT OF TRANSPORTATION
GEOTECHNICAL UNIT BORING LOG

PROJECT NO 33604.1.1		ID B-4262		COUNTY RUTHERFORD		GEOLOGIST M.A. HAGAR								
SITE DESCRIPTION BRIDGE NO. 217 ON SR- 1520 OVER TRIB. CATHY'S CR.							GND WATER							
BORING NO EB1-A		NORTHING 0.00		EASTING 0.00		0 HR N/A								
ALIGNMENT -L-		BORING LOCATION 9+71.500		OFFSET 18.30ft LT		24 HR 4.60ft								
COLLAR ELEV 95.69ft		TOTAL DEPTH 24.80ft		START DATE 10/03/05		COMPLETION DATE 10/03/05								
DRILL MACHINE CME-550			DRILL METHOD SPT CORE BORING			HAMMER TYPE AUTOMATIC								
SURFACE WATER DEPTH				DEPTH TO ROCK 15.90ft				Log EB1-A, Page 1 of 1						
ELEV	DEPTH	BLOW CT			PEN (ft)	BLOWS PER FOOT					SAMPLE NO	LOG MOI	SOIL AND ROCK DESCRIPTION	
		6in	6in	6in		0	25	50	75	100				
95.69														Ground Surface
	4.90	2	1	2	1.0									EMBANKMENT: SILTY SAND
	9.90	24	76		0.8									ALLUVIUM: INTERLAYERED SILT, SAND, PEBBLES, GRAVEL, & COBBLES
	14.90	100			0.3									SAPROLITE: BLACK SILTY FINE TO COARSE SAND
														WEATHERED ROCK
														HARD ROCK: REC=94% RQD=90%
														HARD ROCK: REC=98% RQD=96%
														BORING TERMINATED AT ASSUMED ELEV. 70.9' IN HARD ROCK

PROJECT NO 33604.1.1		ID B-4262		COUNTY RUTHERFORD		GEOLOGIST M.A. HAGAR								
SITE DESCRIPTION BRIDGE NO. 217 ON SR- 1520 OVER TRIB. CATHY'S CR.							GND WATER							
BORING NO EB1-B		NORTHING 0.00		EASTING 0.00		0 HR N/A								
ALIGNMENT -L-		BORING LOCATION 10+10.000		OFFSET 20.00ft RT		24 HR 4.20ft								
COLLAR ELEV 95.01ft		TOTAL DEPTH 14.50ft		START DATE 10/04/05		COMPLETION DATE 10/04/05								
DRILL MACHINE CME-550			DRILL METHOD SPT CORE BORING			HAMMER TYPE AUTOMATIC								
SURFACE WATER DEPTH				DEPTH TO ROCK 13.90ft				Log EB1-B, Page 1 of 1						
ELEV	DEPTH	BLOW CT			PEN (ft)	BLOWS PER FOOT					SAMPLE NO	LOG MOI	SOIL AND ROCK DESCRIPTION	
		6in	6in	6in		0	25	50	75	100				
95.01														Ground Surface
	3.80	1	1	2	1.0									ALLUVIUM: GRAY SILTY FINE TO COARSE SAND
	8.80	3	4	6	1.0									ALLUVIAL BASAL GRAVEL
	13.80	100			0.1									SAPROLITE: BROWN SLIGHTLY MICACEOUS SILTY FINE TO COARSE SAND
														WEATHERED ROCK
														HARD ROCK
														BORING TERMINATED AT ASSUMED ELEV. 80.5' IN HARD ROCK

NORTH CAROLINA DEPARTMENT OF TRANSPORTATION
GEOTECHNICAL UNIT BORING LOG


PROJECT NO 33604.1.1		ID B-4262		COUNTY RUTHERFORD		GEOLOGIST M.A. HAGAR							
SITE DESCRIPTION BRIDGE NO. 217 ON SR- 1520 OVER TRIB. CATHY'S CR.							GND WATER						
BORING NO EB2-A		NORTHING 0.00		EASTING 0.00		0 HR N/A							
ALIGNMENT -L-		BORING LOCATION 10+15.000		OFFSET 31.50ft LT		24 HR 3.80ft							
COLLAR ELEV 94.59ft		TOTAL DEPTH 15.50ft		START DATE 10/04/05		COMPLETION DATE 10/04/05							
DRILL MACHINE CME-550			DRILL METHOD SPT CORE BORING			HAMMER TYPE AUTOMATIC							
SURFACE WATER DEPTH			DEPTH TO ROCK 14.90ft			Log EB2-A, Page 1 of 1							
ELEV	DEPTH	BLOW CT			PEN (ft)	BLOWS PER FOOT				SAMPLE NO	LOG	SOIL AND ROCK DESCRIPTION	
		6in	6in	6in		0	25	50	75				100
94.59													Ground Surface
90.00	3.80	4	4	3	1.0								ALLUVIUM: ORANG-BROWN SANDY SILT
	8.80	4	10	8	1.0								ALLUVIUM: GRAY SLI. MICAC. SILTY FINE TO COARSE SAND
													ALLUVIAL BASAL GRAVEL
													SAPROLITE: DARK GRAY-BROWN SILTY FINE TO COARSE SAND W/ ROCK FRAGMENTS
80.00	13.80	100			0.3								WEATHERED ROCK
79.09													HARD ROCK
--- BORING TERMINATED AT ASSUMED ELEV. 79.1' IN HARD ROCK ---													

NORTH CAROLINA DEPARTMENT OF TRANSPORTATION
GEOTECHNICAL UNIT BORING LOG

PROJECT NO 33604.1.1		ID B-4262		COUNTY RUTHERFORD		GEOLOGIST M.A. HAGAR							
SITE DESCRIPTION BRIDGE NO. 217 ON SR- 1520 OVER TRIB. CATHY'S CR.							GND WATER						
BORING NO EB2-B		NORTHING 0.00		EASTING 0.00		0 HR N/A							
ALIGNMENT -L-		BORING LOCATION 10+64.500		OFFSET 22.50ft RT		24 HR 3.00ft							
COLLAR ELEV 93.28ft		TOTAL DEPTH 24.50ft		START DATE 9/22/05		COMPLETION DATE 09/27/05							
DRILL MACHINE CME-550			DRILL METHOD SPT CORE BORING			HAMMER TYPE AUTOMATIC							
SURFACE WATER DEPTH			DEPTH TO ROCK 16.50ft			Log EB2-B, Page 1 of 1							
ELEV	DEPTH	BLOW CT			PEN (ft)	BLOWS PER FOOT				SAMPLE NO	LOG	SOIL AND ROCK DESCRIPTION	
		6in	6in	6in		0	25	50	75				100
93.28													Ground Surface
90.00	3.30	5	25	10	1.0								ALLUVIUM: INTERLAYERED GRAY SILTY FINE TO COARSE SAND W/ SUB-ANGULAR PEBBLES, GRAVEL, & COBBLES
	8.30	14	5	2	1.0								SS-1
80.00	13.30	5	17	24	1.0								SS-2
	16.00	4	7	93	1.0								CORE 1
													CORE 2
70.00													SAPROLITE: BROWN SLI. MICAC. SILTY FINE TO COARSE SAND
68.78													WEATHERED ROCK
													HARD ROCK: REC=74% RQD=74%
													HARD ROCK: REC=100% RQD=94%
--- BORING TERMINATED AT ASSUMED ELEV. 68.8' IN HARD ROCK ---													

RUTH 217
B-4262


99'




6.75'

TYPICAL RIB
STIFFENER

13.5'

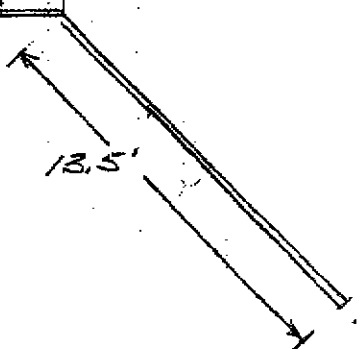

37'6" / 18"

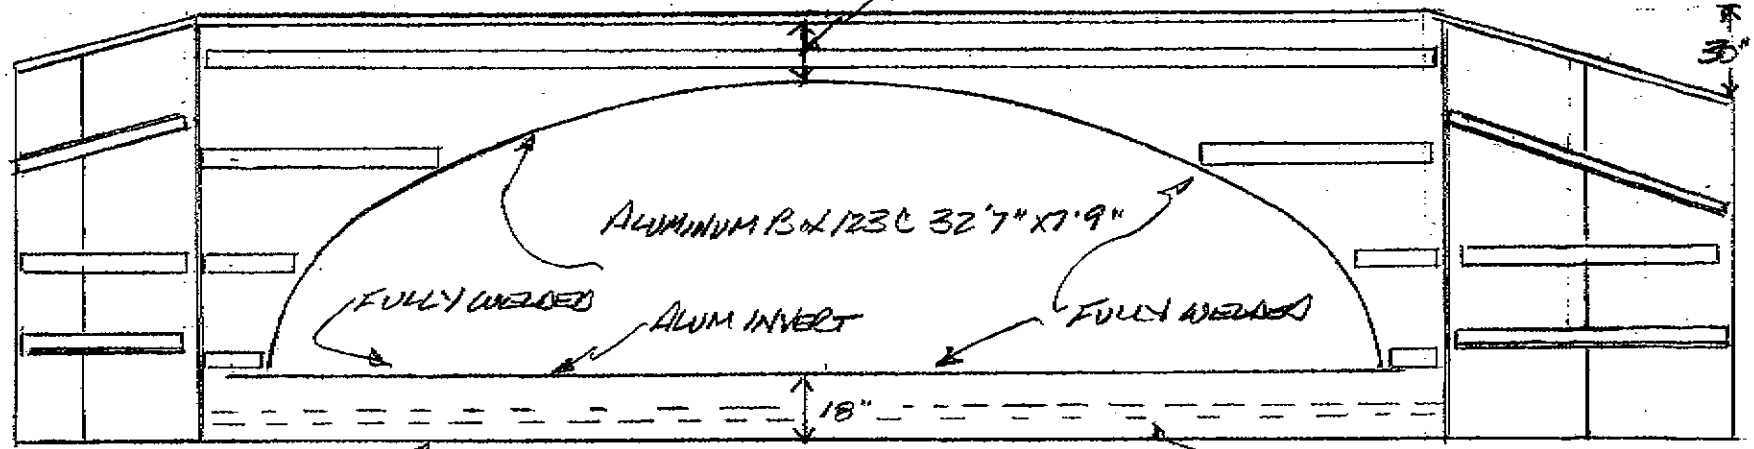

ALUMINUM B&I 230 32'7" X 7'9"

FULLY WELDED

ALUM INVERT

FULLY WELDED

18"

6.75'

13.75'

INTEGRAL
TOEWALL

ELEVATION BOTH ENDS

ALUMINUM CHANNEL
STIFFENER

NO SCALE

NC DOT BRIDGE 217 SR 1520
HEADWALL/JONGWALL DETAIL

**OFFICIAL ROSTER OF PRE-BID CONFERENCE ATTENDEES
NCDOT- BRIDGE MANAGEMENT UNIT -POC**

DATE: Wednesday, Oct. 27, 2010
TIME: 10:00 a.m.

BRIDGE REPLACEMENT CONTRACTS:

1. Cumberland Co. Br. # 11, DO00087 (BK-5110)
2. Montgomery Co. Br. # 90, DO00088 (BK-5112)
- ③ Burke Co. Br. # 118, DO00055 (BK-5232)
- ④ Rutherford Co. Br. #217, D000080 (B-4262)

* CIRCLE THE NUMBER CORRESPONDING TO THE PROJECT THAT YOU PLAN TO BID ON.

NAME	*PROJECT	COMPANY REPRESENTED AND ADDRESS	CONTACT INFORMATION
PETE CAMP	<ol style="list-style-type: none"> 1 2 ③ 4 5 	Apple Tack Assoc. P.O. 904 Rutherfordton N.C.	Email: _____ Phone: 828-287-3767 Fax: _____
Browder Shelton	<ol style="list-style-type: none"> ① 2 3 4 5 	TCB BUILDERS LLC P.O. Box 1625 Lexington NC 27293	Email: TCBBuilders@AOL.com Phone: 336-224-2200 Fax: 336-224-2299
Clark Ledbetter	<ol style="list-style-type: none"> 1 2 ③ 4 5 	Clark Ledbetter Gradco → Hauling Inc. 1506 Gates Rd S/W/MS	Email: CLedbetter3@Carolina Phone: 704-472-2185 Fax: 704-434-5906
Kenny Brady	<ol style="list-style-type: none"> ① 2 3 4 5 	Sanford Contractors, Inc. 629 Rocky Fork Church Rd. Sanford, N.C. 27332	Email: kbrady@sanfordcontractors.com Phone: 919-775-7882 Fax: 919-775-3406
ARTHUR HARELL	<ol style="list-style-type: none"> 1 2 ③ 4 5 	Country Boy Landscaping PO Box 290 Harmony NC 28034	Email: Seed4u@bellsouth Phone: 704-902-0155 Fax: 704-904-3432
Erick Frazier	<ol style="list-style-type: none"> ① 2 3 4 5 	S.T. Wooten Corp P.O. Box 2408 Wilson, NC 27894	Email: ERICK@STWCORP.COM Phone: 252-291-5165 Fax: 252-293-0901



**OFFICIAL ROSTER OF PRE-BID CONFERENCE ATTENDEES
NCDOT- BRIDGE MANAGEMENT UNIT -POC**

DATE: Wednesday, Oct. 27, 2010
TIME: 10:00 a.m.

BRIDGE REPLACEMENT CONTRACTS:

- | | |
|---|--|
| 1. Cumberland Co. Br. # 11, DO00087 (BK-5110) | 4. Rutherford Co. Br. #217, D000080 (B-4262) |
| 2. Montgomery Co. Br. # 90, DO00088 (BK-5112) | |
| 3. Burke Co. Br. # 118, DO00055 (BK-5232) | |

*** CIRCLE THE NUMBER CORRESPONDING TO THE PROJECT THAT YOU PLAN TO BID ON.**

NAME	*PROJECT	COMPANY REPRESENTED AND ADDRESS	CONTACT INFORMATION
PETE WERNER	1 2 3 4 5	DANIE CONST. INC PO Box 800 MOORESVILLE NC 28115	Email: <u>DETE@DANIECONST.MOORESVILLE.COM</u> Phone: <u>704-664-5042</u> Fax: <u>704-663-2475</u>
Joe Hollis	1 2 3 4 5	United Contractors Inc of Iowa 7562 High Rd Sims NC 27880 P.O. Box 347 Johnston Iowa 50131	Email: <u>joe.hollis@unitedcontractors.net</u> Phone: <u>515-577-4776</u> Fax: <u>515-276-3053</u>
Jim Mondolfi	1 2 3 4 5	FLORENCE & HUTCHESON, INC 5121 KINGDOM WAY, SUITE 100 RALEIGH, NC 27607	Email: <u>Jmondolfi@fhut.com</u> Phone: <u>919-851-6066</u> Fax: <u>919-851-6846</u>
BRANDON SHORE	1 2 3 4 5	DAVIE GRADING INC. 1623 US HWY 158 MOCKSVILLE, NC 27028	Email: <u>DAVIEGRADING@PATTEL.NC</u> Phone: <u>336-751-0022</u> Fax: <u>336-751-1022</u>
Michael Moore	1 2 3 4 5	Palmetto Infrastructure Inc. 10535 Baverille Rd Greer SC 29651	Email: <u>graniff@palmettoii.com</u> Phone: <u>864-879-2166</u> Fax: <u>864-879-2167</u>
DAVID SIMPSON	1 2 3 4 5	SIMPSON ENGINEERS & ASSOCIATES 5520 DILLARD DRIVE SUITE 120 CARY, NC 27518	Email: <u>DSIMPSON@SIMPSONENGR.COM</u> Phone: <u>919-852-0468</u> Fax: <u>919-852-0598</u>



**OFFICIAL ROSTER OF PRE-BID CONFERENCE ATTENDEES
NCDOT- BRIDGE MANAGEMENT UNIT-POC**

DATE: Wednesday, Oct. 27, 2010
TIME: 10:00 a.m.

BRIDGE REPLACEMENT CONTRACTS:

- | | |
|---|--|
| 1. Cumberland Co. Br. # 11, DO00087 (BK-5110) | 4. Rutherford Co. Br. #217, D000080 (B-4262) |
| 2. Montgomery Co. Br. # 90, DO00088 (BK-5112) | |
| 3. Burke Co. Br. # 118, DO00055 (BK-5232) | |

* CIRCLE THE NUMBER CORRESPONDING TO THE PROJECT THAT YOU PLAN TO BID ON.

NAME	PROJECT	COMPANY REPRESENTED AND ADDRESS	CONTACT INFORMATION
Horry Parker	<input checked="" type="radio"/> 1 <input type="radio"/> 2 <input type="radio"/> 3 <input type="radio"/> 4 <input type="radio"/> 5	Cape Roman Contracting, Inc. 612 Cape Roman Road Wando, SC. 29492	Email: <u>horry@caperomancontracting.com</u> Phone: <u>843-884-5167</u> Fax: <u>843-884-0516</u>
Mike Miller	<input type="radio"/> 1 <input type="radio"/> 2 <input checked="" type="radio"/> 3 <input type="radio"/> 4 <input type="radio"/> 5	Miller Engineering Co. Inc PO Box 1048 Marion, NC 29752	Email: _____ Phone: <u>828-738-8441</u> Fax: <u>828-738-8440</u>
GARRY MOORE	<input type="radio"/> 1 <input type="radio"/> 2 <input checked="" type="radio"/> 3 <input checked="" type="radio"/> 4 <input type="radio"/> 5	NCDOT DIV 13 BRIDGES	Email: <u>GMOORE@NCDOT.GOV</u> Phone: <u>828-298-1128</u> Fax: <u>828-299-0654</u>
Carl Washburn	<input type="radio"/> 1 <input type="radio"/> 2 <input type="radio"/> 3 <input type="radio"/> 4 <input type="radio"/> 5	Concrete Construction PO Box 550 587 Rock Road Blairsville Ga. 30514	Email: _____ Phone: <u>706 745 6239</u> Fax: <u>706 745 9582</u>
Troy Wilson	<input type="radio"/> 1 <input type="radio"/> 2 <input type="radio"/> 3 <input type="radio"/> 4 <input type="radio"/> 5	NCDOT DIV 13	Email: <u>tswilson@ncdot.gov</u> Phone: <u>828-298-1128</u> Fax: <u>828-299-0654</u>
L.L. "SONNY" UPDE	<input checked="" type="radio"/> 1 <input type="radio"/> 2 <input type="radio"/> 3 <input type="radio"/> 4 <input type="radio"/> 5	NCDOT DIV 6	Email: <u>LUPDE@NCDOT</u> Phone: <u>910-829-6345</u> Fax: <u>910-829-6349</u>



**OFFICIAL ROSTER OF PRE-BID CONFERENCE ATTENDEES
NCDOT- BRIDGE MANAGEMENT UNIT -POC**

DATE: Wednesday, Oct. 27, 2010
TIME: 10:00 a.m.

BRIDGE REPLACEMENT CONTRACTS:

- | | |
|---|--|
| 1. Cumberland Co. Br. # 11, DO00087 (BK-5110) | 4. Rutherford Co. Br. #217, D000080 (B-4262) |
| 2. Montgomery Co. Br. # 90, DO00088 (BK-5112) | |
| 3. Burke Co. Br. # 118, DO00055 (BK-5232) | |

*** CIRCLE THE NUMBER CORRESPONDING TO THE PROJECT THAT YOU PLAN TO BID ON.**

NAME	*PROJECT	COMPANY REPRESENTED AND ADDRESS	CONTACT INFORMATION
Kevin Austin	1 2 3 4 5	Mulkey Engineers + Consultants 6750 Tryon Rd Cary, NC	Email: <u>kaustina@mulkeyinc.com</u> Phone: <u>(919) 858-1790</u> Fax: <u>(919) 851-1918</u>
KEVIN BURNS	① ② ③ ④ 5	REBURNS + SONS STATESVILLE NC	Email: <u>kevin@reburns.com</u> Phone: _____ Fax: <u>704 924 8607</u>
Frank Fulp	① ② ③ ④ 5	Smith-Rowe, Inc. 639 Old US 52 South Mount Airy, NC 27030	Email: <u>ffulp@triad.rr.com</u> Phone: <u>336-789-8221</u> Fax: <u>336-789-6807</u>
Gary Eisner	1 2 ③ ④ 5	JR Vannoy & Son's 1608 HW 221 N Jefferson NC 28640	Email: <u>Gary.Eisner@jrvannoy.com</u> Phone: <u>336-846-2191</u> Fax: <u>336-846-7112</u>
MICHAEL G. PHILLIPS	1 2 3 4 5	NCDOT - Div. 8	Email: <u>mphilips@ncdot.gov</u> Phone: <u>910-944-7554</u> Fax: _____
Philip Creasman	1 2 3 4 5	Taylor + Murphy Construction PO BOX 6215 ASHEVILLE NC 28812	Email: <u>pcreasman@taylorandmurphy.com</u> Phone: <u>828-667-4526</u> Fax: <u>828-667-1770</u>



**OFFICIAL ROSTER OF PRE-BID CONFERENCE ATTENDEES
NCDOT- BRIDGE MANAGEMENT UNIT -POC**

DATE: Wednesday, Oct. 27, 2010
TIME: 10:00 a.m.

BRIDGE REPLACEMENT CONTRACTS:

- | | |
|---|--|
| <ul style="list-style-type: none"> 1. Cumberland Co. Br. # 11, DO00087 (BK-5110) 2. Montgomery Co. Br. # 90, DO00088 (BK-5112) 3. Burke Co. Br. # 118, DO00055 (BK-5232) | <ul style="list-style-type: none"> 4. Rutherford Co. Br. #217, D000080 (B-4262) |
|---|--|

*** CIRCLE THE NUMBER CORRESPONDING TO THE PROJECT THAT YOU PLAN TO BID ON.**

NAME	*PROJECT	COMPANY REPRESENTED AND ADDRESS	CONTACT INFORMATION
Mikel Garren	1 2 3 4 5	31 Airport RD Whittemore NC	Email: <u>MGarrell@NCDOT.Gov</u> Phone: <u>910 642 4388</u> Fax: _____
Kevin Worley	1 2 3 4 5	31 Airport RD Whittemore NC	Email: <u>KSWorley@NCDOT.Gov</u> Phone: <u>910-642-4388</u> Fax: _____
Wesley Wokusch	1 2 3 4 5	3105 Chapel Hill Road Raleigh, NC 27667 Fred Smith Company	Email: <u>Wesley.Wokusch@fredsmith.com</u> Phone: <u>(919) 868-3294</u> Fax: <u>919 582-3563</u>
Tommy Penninger	1 2 3 4 5	Bryant's land & Devl, 157 Depot St Burnesville NC.	Email: <u>AMBRYANT@INDUSTRIAL</u> Phone: <u>(828) 678-9966</u> Fax: <u>(828) 678-9708</u>
—	1 2 3 4 5	—	Email: _____ Phone: _____ Fax: _____
—	1 2 3 4 5	—	Email: _____ Phone: _____ Fax: _____
