


8/26/21

+

+

DRAWN BY : J. MYA DATE : 4/2025
CHECKED BY : J. YANNACCONE DATE : 4/2025

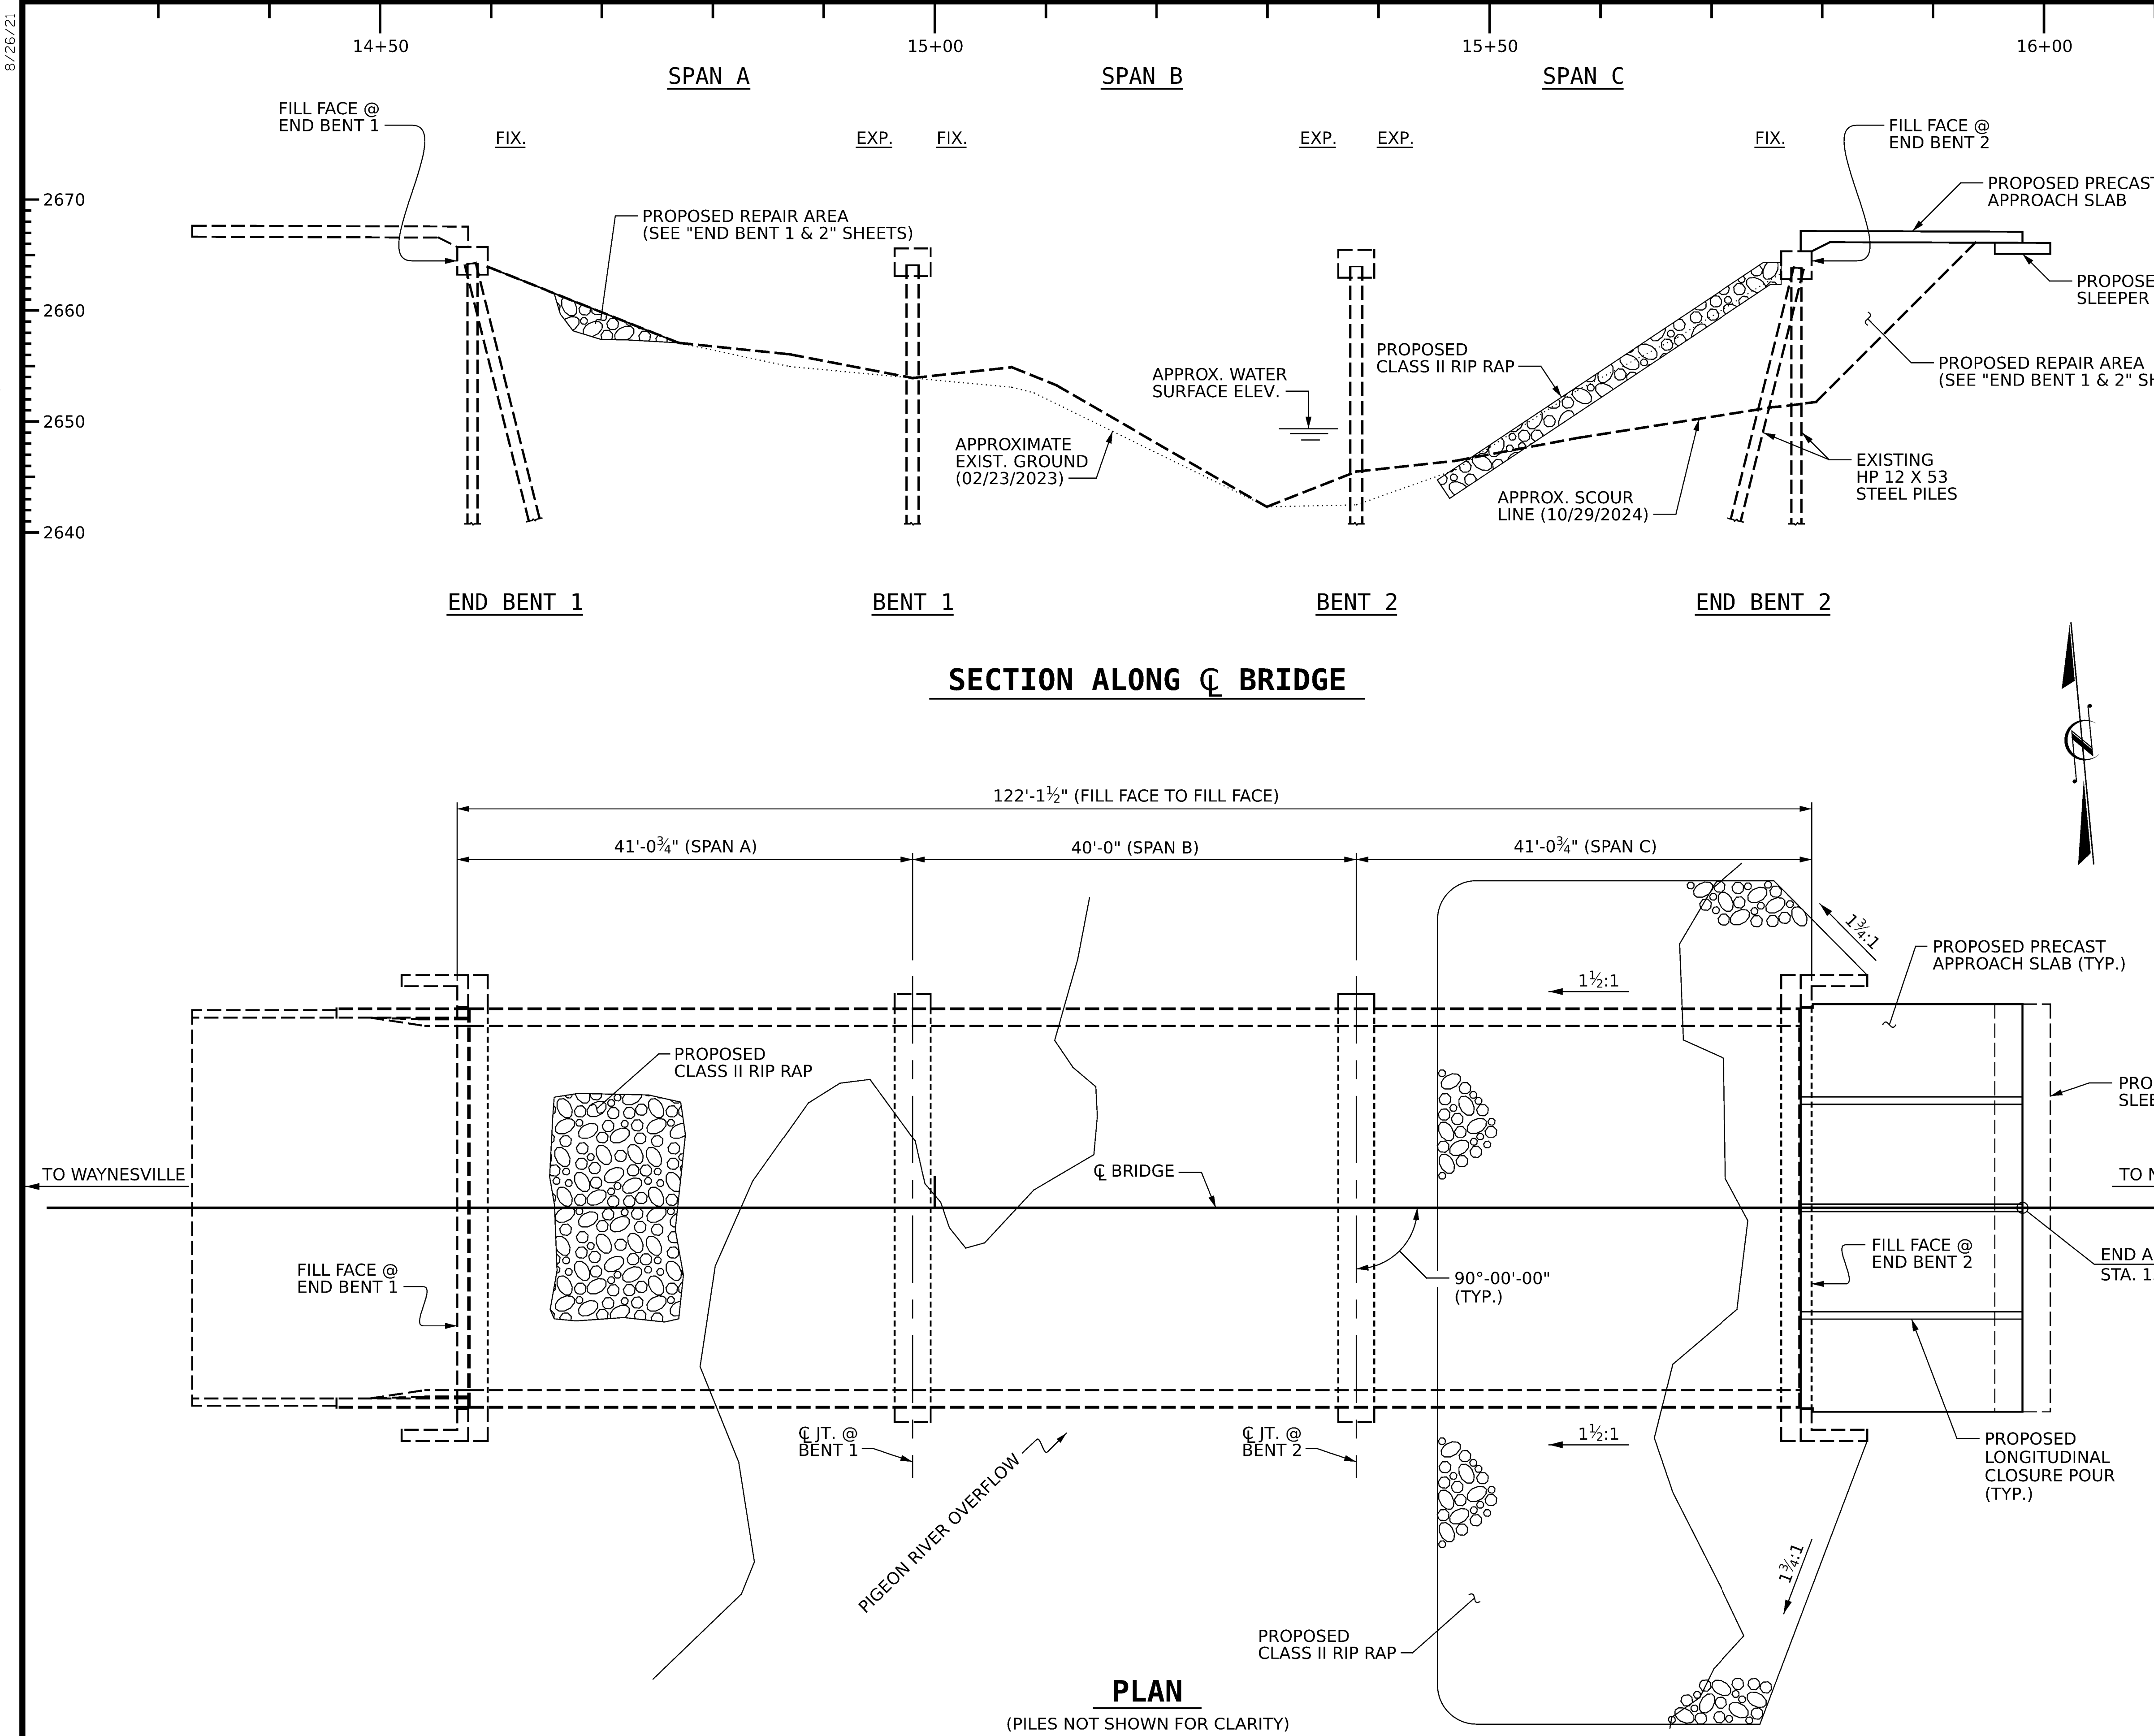


PLAN
(PILES NOT SHOWN FOR CLARITY)



One Glenwood Avenue
Suite 900
Raleigh, NC 27603
919-420-7660
NC Lic. No. F-0270

DOCUMENT NOT CONSIDERED
FINAL UNLESS ALL
SIGNATURES COMPLETED



NOTES:

PROFILE INFORMATION IS TAKEN FROM THE ORIGINAL PLANS, THE ROUTINE INSPECTION REPORT DATED 01/08/2025, AND THE HIGH WATER SUPPLEMENTAL REPORT DATED 10/29/2024.

BRIDGE ORIENTATION CONFORMS TO EXISTING BRIDGE PLANS AND ROUTINE INSPECTION REPORT.

SCOPE OF WORK:

REMOVE REMAINING PORTIONS OF EXISTING APPROACH SLAB AND EXISTING CONCRETE BARRIER RAIL.

REMOVE RIP RAP FROM AROUND EXISTING STEEL PILES DOWN TO APPROXIMATE SCOUR LINE.

CLEAN, REPAIR AND PAINT EXISTING STRUCTURAL STEEL PILES.

RESTORE ROADWAY FILL AROUND STEEL PILES.

INSTALL RIP RAP AT BOTH END BENTS TO MATCH AS-BUILT END SLOPE.

REMOVE AND RESET EXISTING GUARDRAIL.

INSTALL GUARDRAIL ANCHOR UNITS ON EXISTING BRIDGE RAIL.

INSTALL PRECAST APPROACH SLABS AND SLEEPER SLABS WITH LONGITUDINAL CLOSURE POURS.

REMOVE EXISTING JOINT AND INSTALL ASPHALT PLUG JOINTS.

MILL AND REPAVE ASPHALT APPROACH ROADWAY.

I HEREBY CERTIFY YHAT THIS STRUCTURE WAS REHABILITATED
ACCORDING TO THESE PLANS OR AS NOTED HEREIN.

RESIDENT ENGINEER

DATE

PROJECT NO. **18314.1044067**

HAYWOOD COUNTY

BRIDGE: **430163**

SHEET 1 OF 4

STATE OF NORTH CAROLINA
DEPARTMENT OF TRANSPORTATION
RALEIGH

GENERAL DRAWING
FOR BRIDGE ON US 276
(PIGEON RD) OVER WEST FORK
PIGEON RIVER OVERFLOW

REVISIONS						SHEET NO.
NO.	BY:	DATE:	NO.	BY:	DATE:	
1			3			S-1
2			4			
TOTAL SHEETS						14
