


WBS NO: 2026CPT.03.13.20672

CONTRACT: DC00489

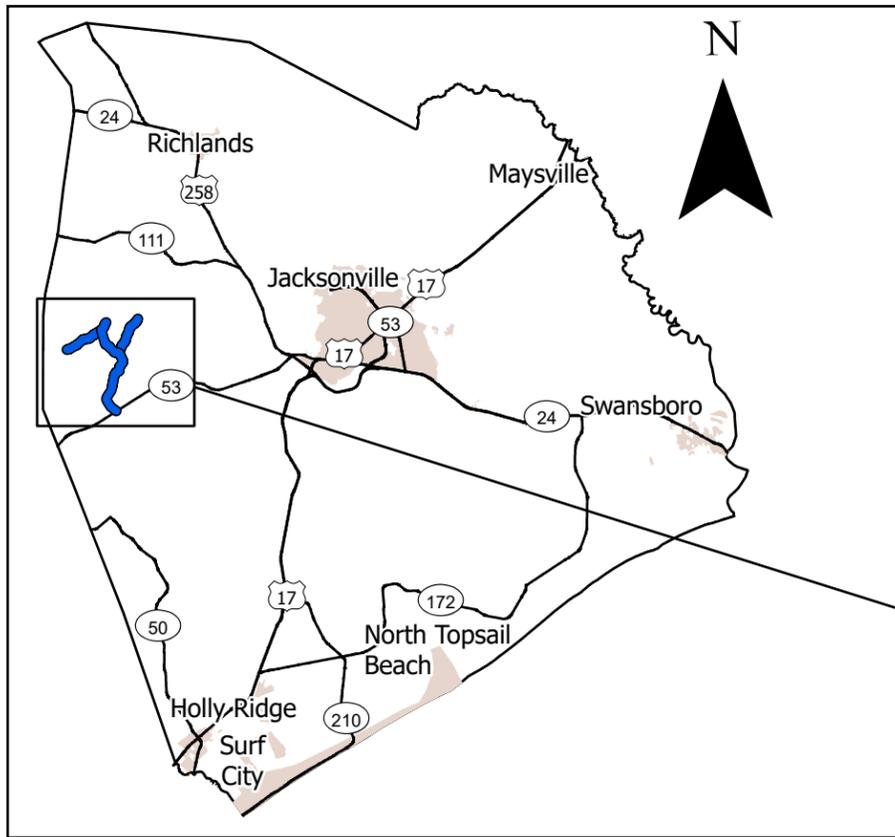


**STATE OF NORTH CAROLINA
DIVISION OF HIGHWAYS
DISTRICT 1 ONSLOW COUNTY**

TYPE OF WORK: PRESERVATION

STATE	STATE PROJECT REFERENCE NUMBER	SHEET NO.
NC	2026CPT.03.13.20672	1
STATE PROJECT NUMBER		DESCRIPTION

- Preservation
- Division 3 Bridges

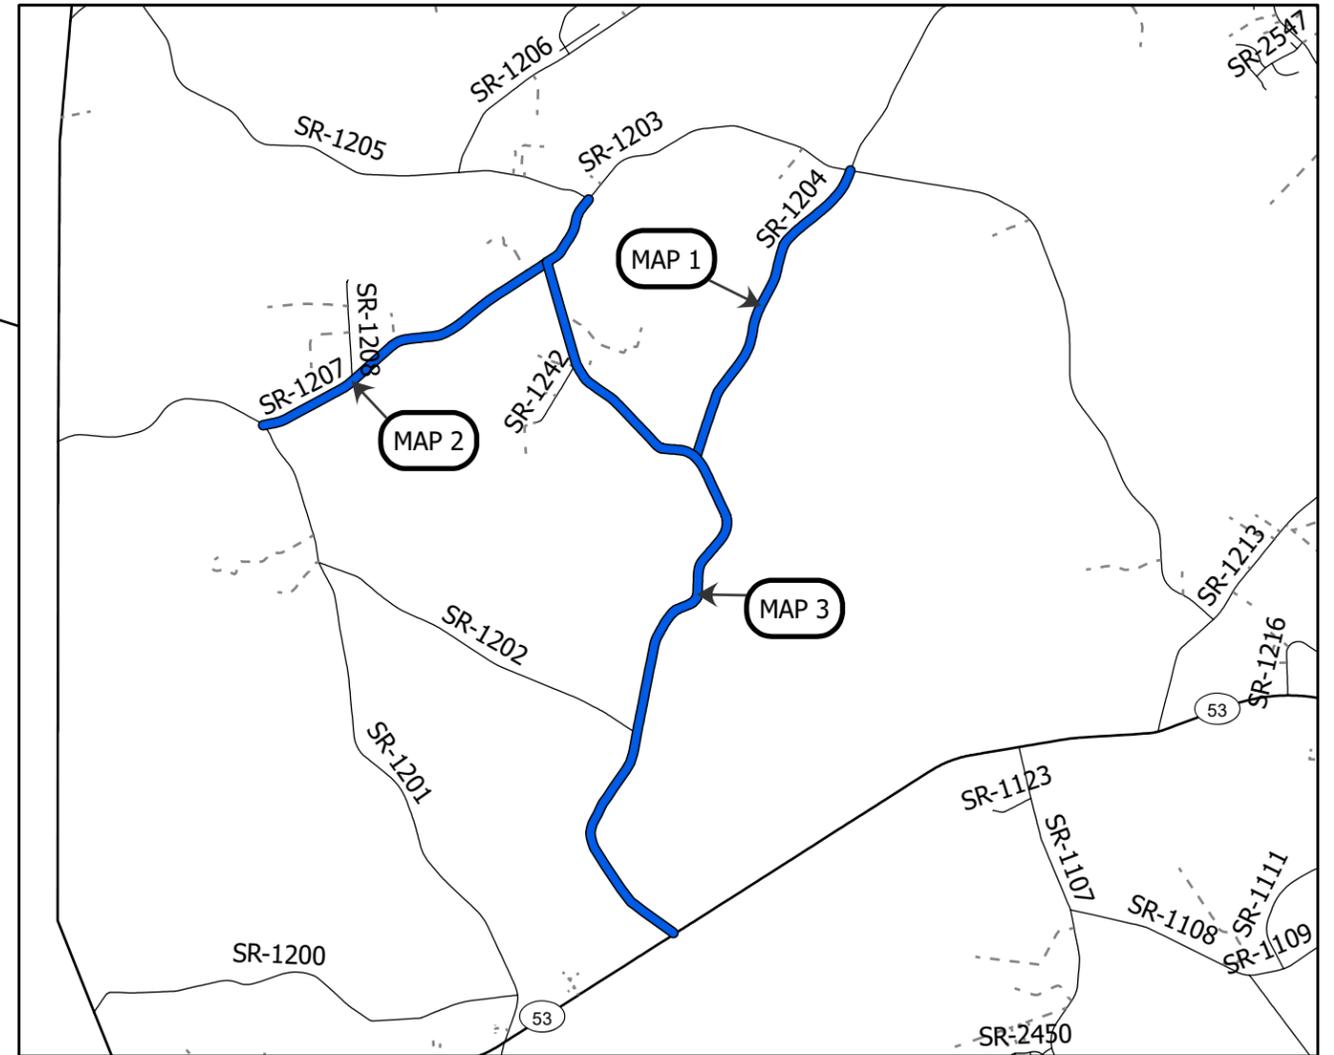

MAP	ROUTE	DESCRIPTION	TYPE
1	SR-1204 / DAVIS RD	FROM SR 1203 (BEN WILLIAMS RD) TO SR 1203 (NINE MILE RD) [MP 0.00 - MP 1.90]	Preservation
2	SR-1207 / HEWITT RD	FROM SR 1203 (NINE MILE RD) TO SR 1201 (GURGANUS RD) [MP 0.00 - MP 1.90]	Preservation
3	SR-1203 / NINE MILE RD	FROM NC 53 (BURGAW HWY) TO SR 1205 (BATCHELOR RD) [MP 0.00 - MP 5.12]	Preservation

PROJECT LENGTH

MAP	MILES
1	1.90
2	1.90
3	5.12


Prepared in the Office of:
DIVISION OF HIGHWAYS
5501 BARBADOS BLVD., CASTLE HAYNE, NC, 28429

This exhibit does not meet NC 47-30 requirements and therefore is not intended for design, construction, or recording or transfer of title.



WBS NO: 36249.5092

CONTRACT: DC00489

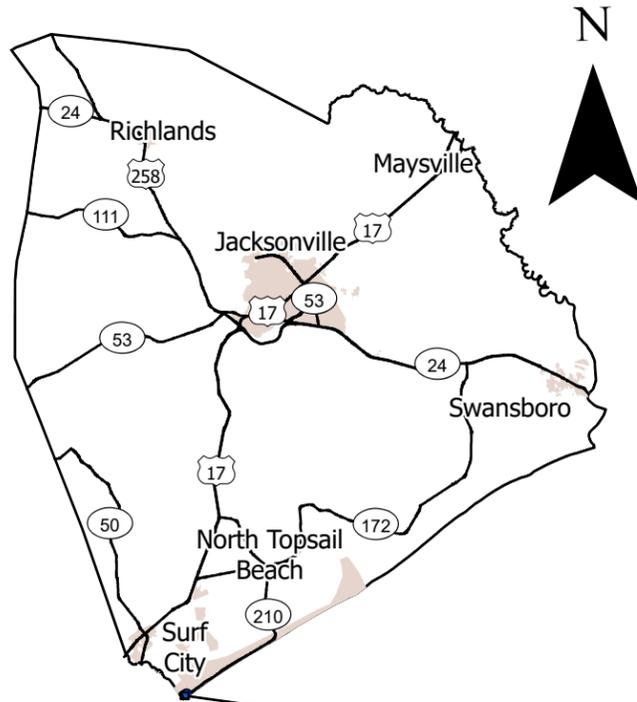


**STATE OF NORTH CAROLINA
DIVISION OF HIGHWAYS
DISTRICT 1 ONSLOW COUNTY**

TYPE OF WORK: PRESERVATION

STATE	STATE PROJECT REFERENCE NUMBER	SHEET NO.
NC	36249.5092	2
STATE PROJECT NUMBER		DESCRIPTION

— Preservation

MAP	ROUTE	DESCRIPTION	TYPE
4	2ND ST	FROM (CANAL ST) TO NC 210 (N NEW RIVER DR)[MP 0.00 - MP 0.09]	Preservation
5	3RD ST	FROM (CANAL ST) TO NC 210 (N NEW RIVER DR)[MP 0.00 - MP 0.09]	Preservation
6	4TH ST	FROM (CANAL ST) TO NC 210 (N NEW RIVER DR)[MP 0.00 - MP 0.09]	Preservation
7	5TH ST	FROM (CANAL ST) TO NC 210 (N NEW RIVER DR)[MP 0.00 - MP 0.09]	Preservation
8	6TH ST	FROM (CANAL ST) TO NC 210 (N NEW RIVER DR)[MP 0.00 - MP 0.09]	Preservation
9	7TH ST	FROM (CANAL ST) TO NC 210 (N NEW RIVER DR)[MP 0.00 - MP 0.08]	Preservation

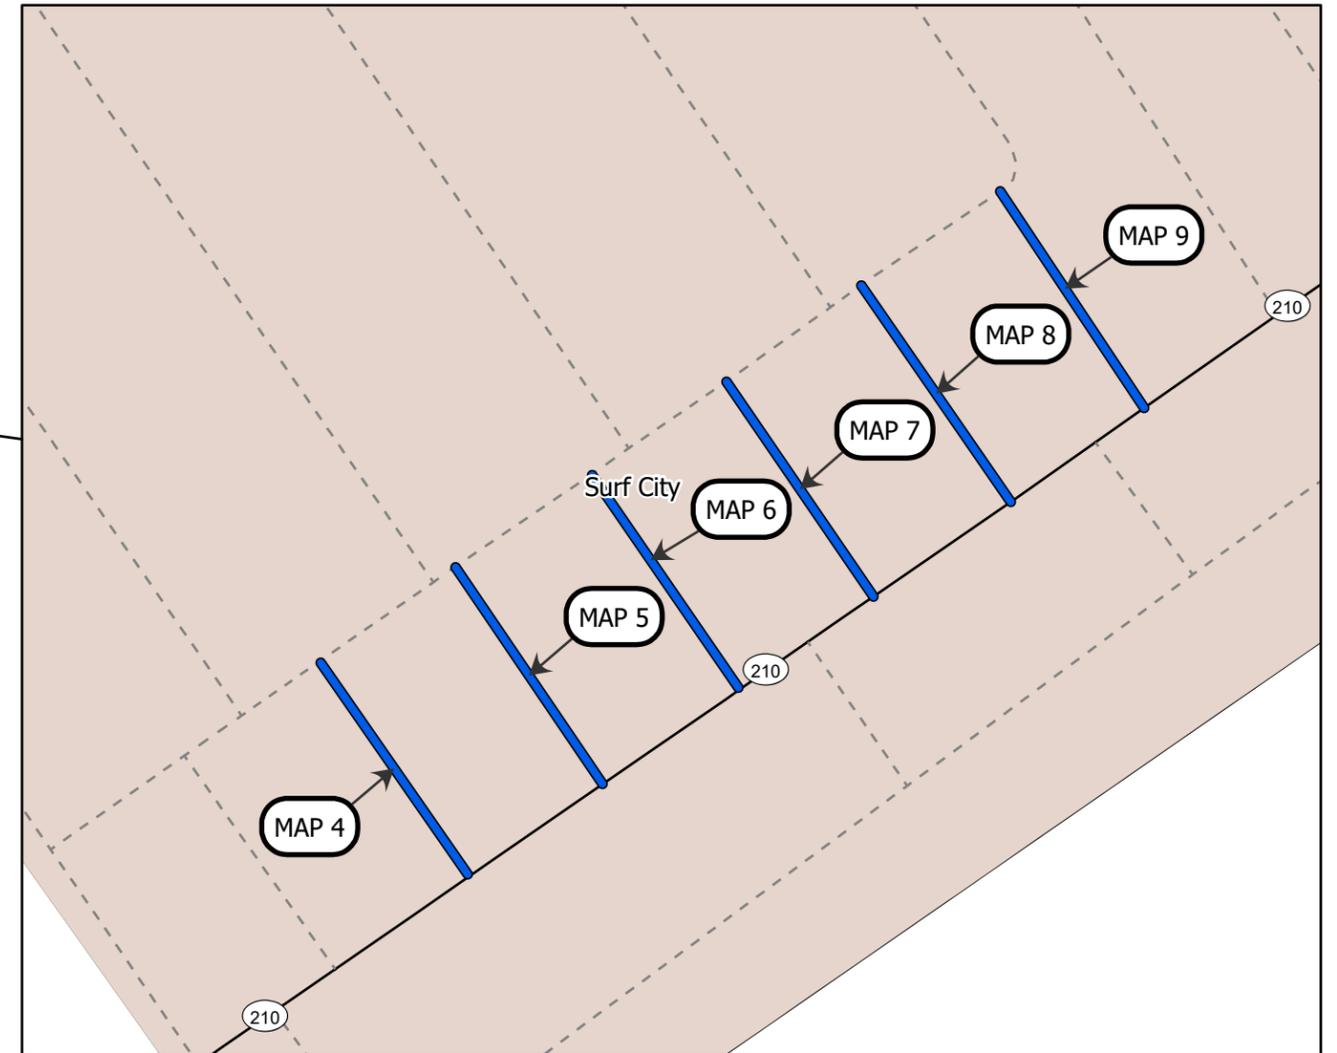

PROJECT LENGTH

MAP	MILES
4	0.09
5	0.09
6	0.09

MAP	MILES
7	0.09
8	0.09
9	0.08

Prepared in the Office of:
DIVISION OF HIGHWAYS
5501 BARBADOS BLVD., CASTLE HAYNE, NC, 28429


This exhibit does not meet NC 47-30 requirements and therefore is not intended for design, construction, or recording or transfer of title.



SIGNING FOR ASPHALT SURFACE TREATMENT

LEGEND

- ◻ PORTABLE SIGN
- └ STATIONARY SIGN
- ← DIRECTION OF TRAFFIC FLOW

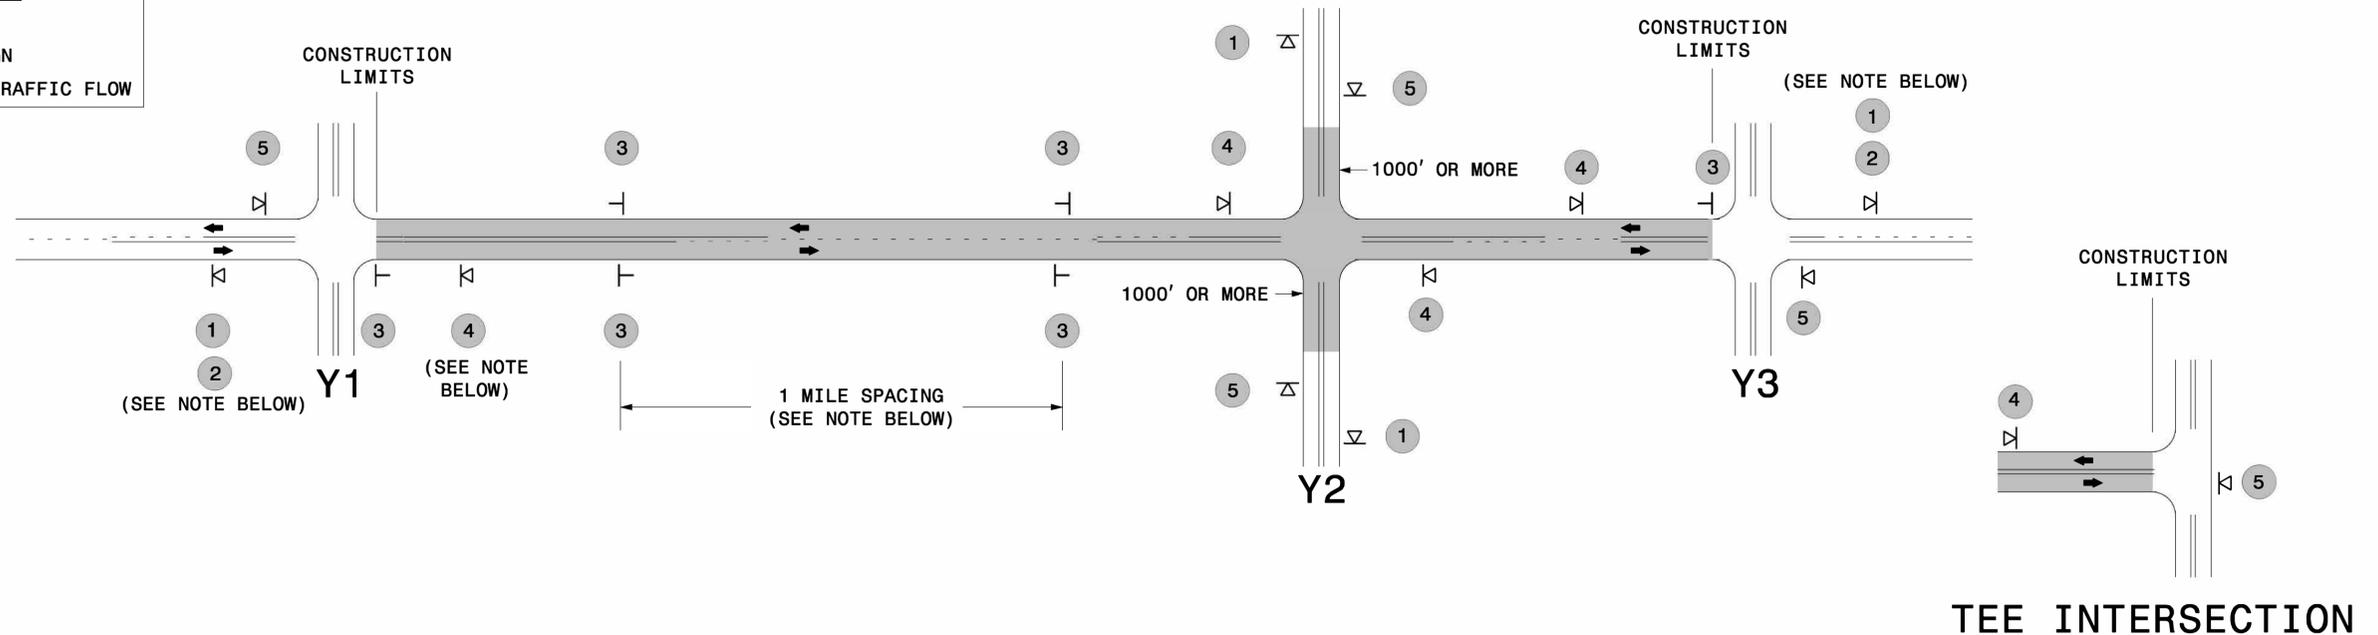

MAINLINE (-L-) SIGNING


-Y- LINE SIGNING

SIGNING NOTES AND PLACEMENT PER DIRECTION	1	 W20-1 48" X 48"	<ul style="list-style-type: none"> - PLACE 1000' PRIOR TO BEGINNING OF CONSTRUCTION LIMITS. ONLY USED ON -Y- LINES IF RESURFACING LIMITS EXTEND 1000' ALONG -Y- LINE. 	<p>STATIONARY SIGNING NOT REQUIRED FOR THE FOLLOWING -Y- LINE CONDITIONS:</p> <ol style="list-style-type: none"> 1) LESS THAN 1000' OF RESURFACING ALONG -Y- LINE 2) SUBDIVISION ROADS 3) DEAD END ROADS <p>WHEN PAVING/CONSTRUCTION ACTIVITIES PROCEED ACROSS AN UNSIGNED -Y- LINE, PORTABLE ADVANCE WARNING SIGNS SHALL BE USED ALONG THE -Y- LINE AS SHOWN BELOW. REMOVE UPON COMPLETION OF WORK.</p> <div style="display: flex; justify-content: space-around; align-items: center;"> <div style="text-align: center;"> <p>W20-1 48" X 48"</p> <p>PLACED 500' IN ADVANCE OF FLAGGER.</p> </div> <div style="text-align: center;"> <p>W20-7 A 48" X 48"</p> <p>PLACED 250' IN ADVANCE OF FLAGGER.</p> </div> </div>
	2	 NEXT W7-3aP 24" X 18"	<ul style="list-style-type: none"> - SIGN #2 ONLY USED WHEN RESURFACING LIMITS ARE 2 OR MORE MILES IN LENGTH. ROUND UP TO THE NEAREST WHOLE NUMBER. DO NOT USE FRACTIONAL OR DECIMAL NUMBERS. 	
	3	 W8-7 48" X 48"	<ul style="list-style-type: none"> - ALTERNATE THE FOLLOWING TWO SIGNS: - STARTING WITH "LOOSE GRAVEL" (W8-7) FOLLOWED BY "UNMARKED PAVEMENT". - PLACE INITIALLY AT THE CONSTRUCTION LIMITS AND SPACED 1 MILE APART THEREAFTER. 	
		 UNMARKED PAVEMENT SP 48" X 48"	<ul style="list-style-type: none"> - AT TEE INTERSECTIONS INSTALL INITIALLY 0.5 MILE FROM INTERSECTION AND SPACE 1 MILE APART THEREAFTER. 	
	4	 ROAD UNDER CONST SP 13106 48" X 48"	<ul style="list-style-type: none"> - THESE ARE FOR -Y- LINES THAT ARE "THROUGH" ROADWAYS. DEAD END AND SUBDIVISION ROADS ARE NOT "THROUGH" ROADWAYS. - INSTALL 500' +/- FROM EACH -Y- LINE APPROACH AS SHOWN ABOVE. - FOR MULTIPLE -Y- LINES THAT ARE SEPARATED BY 0.25 MILES OR LESS, TREAT AS A SINGLE UNIT AND INSTALL WITHIN 500' OF EACH APPROACH. - A MAXIMUM OF 2 SIGN SETS PER MILE. DO NOT INSTALL WHEN -Y- LINES ARE WITHIN 0.5 MILES FROM "END ROAD WORK" SIGN. 	
5	 END ROAD WORK G20-2 A 48" X 24"	<ul style="list-style-type: none"> - PLACE 500' FOLLOWING THE END OF CONSTRUCTION LIMITS OR AS SHOWN WHEN WORK ENDS AT A 3-WAY TEE INTERSECTION. 		

THE ABOVE SIGNS ARE ALL THAT ARE REQUIRED FOR A CONTRACTOR TO BEGIN A RESURFACING CONTRACT. ANY ADDITIONAL SIGNS REQUESTED BY NCDOT DIVISIONS SHALL BE INSTALLED WITHIN 7 BUSINESS DAYS OF THE START OF CONTRACT WORK.

MAPS LESS THAN 2 MILES

FOR AST RESURFACING MAPS WITH CONSTRUCTION LIMITS LESS THAN 2 MILES IN LENGTH, USE A STATIONARY "LOOSE GRAVEL" SIGN AT THE BEGINNING CONSTRUCTION LIMIT FOLLOWED BY AN "UNMARKED PAVEMENT" SIGN MIDWAY THROUGH AND AN "END ROAD WORK" SIGN AT THE END CONSTRUCTION LIMIT.



ADVANCE WARNING SIGNS FOR 2-LANE ROADWAY ASPHALT SURFACE TREATMENT

PROJECT NO.	SHEET NO.
2026CPT.03.13.20672	7
36249.5092	

SUMMARY OF QUANTITIES

PROJECT NO	COUNTY	MAP NO	ROUTE	DESCRIPTION	TYP NO	LANES	LANE TYPE	LENGTH	WIDTH	BEGI	END	1575000000-E	1705500000-E	1775000000-E	1022000000-E	1891000000-E	1891000000-E	2830000000-N
								MI	FT	N MP	MP	ASPHALT BINDER FOR PLANT MIX	PATCHING EXISTING PAVEMENT (MILL)	ASPHALT SURFACE TREATMENT, MATCOAT, #78M STONE	SEALING EXISTING PAVEMENT CRACKS	MICRO SURFACING SINGLE COURSE, TYPE III	MICRO SURFACING SINGLE COURSE, TYPE II	ADJUSTMENT OF MANHOLES
												TON	TON	SY	LB	SY	SY	EA
2026CPT.03.13.20672	Onslow	1	SR-1204 / DAVIS RD	FROM SR 1203 (BEN WILLIAMS RD) TO SR 1203 (NINE MILE RD) [MP 0.00 - MP 1.90]	1	2	2WU	1.90	20	0.00	1.90	4			84	44,587		
TOTAL FOR MAP NO. 1								1.90				4			84	44,587		
2026CPT.03.13.20672	Onslow	2	SR-1207 / HEWITT RD	FROM SR 1203 (NINE MILE RD) TO SR 1201 (GURGANUS RD) [MP 0.00 - MP 1.90]	2	2	2WU	1.90	18	0.00	1.90	4		20,064	84	40,128		
TOTAL FOR MAP NO. 2								1.90				4		20,064	84	40,128		
2026CPT.03.13.20672	Onslow	3	SR-1203 / NINE MILE RD	FROM NC 53 (BURGAW HWY) TO SR 1205 (BATCHELOR RD) [MP 0.00 - MP 5.12]	2	2	2WU	5.12	20	0.00	5.12	7		60,075	227	120,149		1
TOTAL FOR MAP NO. 3								5.12				7		60,075	227	120,149		1
TOTAL FOR PROJ NO. 2026CPT.03.13.20672								8.92				15		80,139	395	204,864		1
36249.5092	Onslow - Surf City	4	2ND ST	NC210 TO CANAL ST	3	2	2WU	0.09	18	0.00	0.09	1	2				957	
TOTAL FOR MAP NO. 4								0.09				1	2				957	
36249.5092	Onslow - Surf City	5	3RD ST	NC210 TO CANAL ST	3	2	2WU	0.09	18	0.00	0.09	1	2				937	
TOTAL FOR MAP NO. 5								0.09				1	2				937	
36249.5092	Onslow - Surf City	6	4TH ST	NC210 TO CANAL ST	3	2	2WU	0.09	18	0.00	0.09	1	2				955	
TOTAL FOR MAP NO. 6								0.09				1	2				955	
36249.5092	Onslow - Surf City	7	5TH ST	NC210 TO CANAL ST	3	2	2WU	0.09	18	0.00	0.09	1	2				904	
TOTAL FOR MAP NO. 7								0.09				1	2				904	
36249.5092	Onslow - Surf City	8	6TH ST	NC210 TO CANAL ST	3	2	2WU	0.09	18	0.00	0.09	1	2				934	
TOTAL FOR MAP NO. 8								0.09				1	2				934	
36249.5092	Onslow - Surf City	9	7TH ST	NC210 TO CANAL ST	3	2	2WU	0.08	18	0.00	0.08	1	2				935	
TOTAL FOR MAP NO. 9								0.08				1	2				935	
TOTAL FOR PROJ NO. 36249.5092								0.51				6	12				5,622	
GRAND TOTAL								9.43				21	12	80,139	395	204,864	5,622	1

PROJECT NO.	SHEET NO.
2026CPT.03.13.20672	8
36249.5092	

THERMOPLASTIC AND PAINT QUANTITIES

PROJECT NO	COUNTY	MAP NO	ROUTE	DESCRIPTION	TYP NO	LANES	LANE TYPE	LENGTH	WIDTH	BEGIN MP	END MP	4413000000-E	4457000000-N	4685000000-E	4688000000-E	4709000000-E	4850000000-E	4890000000-E	4900000000-N		
								MI	FT			WORK ZONE ADVANCE/ GENERAL WARNING SIGNING	TEMPORARY TRAFFIC CONTROL	4" X 90 M WHITE THERMO	4" X 90 M YELLOW THERMO	6" X 90 M WHITE THERMO	6" X 90 M YELLOW THERMO	THERMOPLASTIC PAVEMENT MARKING LINES (24" X 90 MILS)	REMOVAL OF PAVEMENT MARKING LINES (4")	THERMOPLASTIC PROFILED PAVEMENT MARKING LINES (6")	YELLOW & YELLOW MARKERS
								SF	LS	LF	LF	LF	LF	LF	LF	LF	EA				
2026CPT.03.13.20672	Onslow	1	SR-1204 / DAVIS RD	FROM SR 1203 (BEN WILLIAMS RD) TO SR 1203 (NINE MILE RD) [MP 0.00 - MP 1.90]	1	2	2WU	1.90	20	0.00	1.90	212	0.20	40,888	25,080				83		
TOTAL FOR MAP NO. 1								1.90				212	0.20	40,888	25,080				83		
2026CPT.03.13.20672	Onslow	2	SR-1207 / HEWITT RD	FROM SR 1203 (NINE MILE RD) TO SR 1201 (GURGANUS RD) [MP 0.00 - MP 1.90]	2	2	2WU	1.90	18	0.00	1.90	212	0.20		40,888	25,080	64,145	40,888	84		
TOTAL FOR MAP NO. 2								1.90				212	0.20		40,888	25,080		64,145	40,888	84	
2026CPT.03.13.20672	Onslow	3	SR-1203 / NINE MILE RD	FROM NC 53 (BURGAW HWY) TO SR 1205 (BATCHELOR RD) [MP 0.00 - MP 5.12]	2	2	2WU	5.12	20	0.00	5.12	574	0.54		110,182	60,808	172,855	110,182	224		
TOTAL FOR MAP NO. 3								5.12				574	0.54		110,182	60,808		172,855	110,182	224	
TOTAL FOR PROJ NO. 2026CPT.03.13.20672								8.92				998	0.95	40,888	25,080	151,070	85,888		237,000	151,070	391
														65,968	236,958						
36249.5092	Onslow - Surf City	4	2ND ST	NC210 TO CANAL ST	3	2	2WU	0.09	18	0.00	0.09	10	0.009					12			
TOTAL FOR MAP NO. 4								0.09				10	0.01					12			
36249.5092	Onslow - Surf City	5	3RD ST	NC210 TO CANAL ST	3	2	2WU	0.09	18	0.00	0.09	10	0.009					12			
TOTAL FOR MAP NO. 5								0.09				10	0.01					12			
36249.5092	Onslow - Surf City	6	4TH ST	NC210 TO CANAL ST	3	2	2WU	0.09	18	0.00	0.09	10	0.009					12			
TOTAL FOR MAP NO. 6								0.09				10	0.01					12			
36249.5092	Onslow - Surf City	7	5TH ST	NC210 TO CANAL ST	3	2	2WU	0.09	18	0.00	0.09	10	0.009					12			
TOTAL FOR MAP NO. 7								0.09				10	0.01					12			
36249.5092	Onslow - Surf City	8	6TH ST	NC210 TO CANAL ST	3	2	2WU	0.09	18	0.00	0.09	10	0.009					12			
TOTAL FOR MAP NO. 8								0.09				10	0.01					12			
36249.5092	Onslow - Surf City	9	7TH ST	NC210 TO CANAL ST	3	2	2WU	0.08	18	0.00	0.08	10	0.009					12			
TOTAL FOR MAP NO. 9								0.08				10	0.01					12			
TOTAL FOR PROJ NO. 36249.5092								0.51				60	0.05					72			
GRAND TOTAL								9.43				1,058	1	40,888	25,080	151,070	85,888		237,000	151,070	391
														236,958							
