STATE	STATE PROJECT REFERENCE NO.	SHEET NO.	TOTAL SHEETS
N.C.	17BP.14.R.162	1	7

STATE OF NORTH CAROLINA
DEPARTMENT OF TRANSPORTATION
DIVISION OF HIGHWAYS
GEOTECHNICAL ENGINEERING UNIT

STRUCTURE SUBSURFACE INVESTIGATION

PROJ. REFERENCE NO. 17BP.14.R.162 F.A. PROJ. N/A

COUNTY MACON

PROJECT DESCRIPTION DIVISION 14 - LOW IMPACT BRIDGE REPLACEMENT PROGRAM

SITE DESCRIPTION BRIDGE NO. 550088 ON SR 1472 SNOW HILL ROAD) OVER COWEE CREEK.

CONTENTS

SHEET	DESCRIPTION
1	TITLE SHEET
2,2a	LEGEND
3	BORING LOCATIONS
4-7	BORELOGS

PERSONNEL

C. MEATYARD

D. BURLESON

J. SKYTTA, P.E.

E. ROBERTS

INVESTIGATED BY STV ENGINEERS

CHECKED BY J. SKYTTA, P.E.

SUBMITTED BY STV ENGINEERS

DATE JUNE, 2016

CAUTION NOTICE

THE SUBSURFACE INFORMATION AND THE SUBSURFACE INVESTIGATION ON WHICH IT IS BASED WERE MADE FOR THE PURPOSE OF PREPARING THE SCOPE OF WORK TO BE INCLUDED IN THE REQUEST FOR PROPOSAL. THE VARIOUS FIELD BORING LOGS, ROCK CORES, AND SOIL TEST DATA AVAILABLE MAY BE REVIEWED OR INSPECTED IN RALEIGH BY CONTACTING THE N. C. DEPARTMENT OF TRANSPORTATION, GEOTECHNICAL ENGINEERING UNIT AT (919) 250-4088. THE SUBSURFACE PLANS AND REPORTS, FIELD BORING LOGS, ROCK CORES, AND SOIL TEST DATA ARE NOT PART OF THE CONTRACT.

SOIL AND ROCK BOUNDARIES WITHIN A BOREHOLE ARE BASED ON GEOTECHNICAL INTERPRETATION UNLESS ENCOUNTERED IN A SAMPLE. INTERPRETED BOUNDARIES MAY NOT NECESSARILY REFLECT ACTUAL SUBSURFACE CONDITIONS BETWEEN SAMPLED STRATA, AND BOREHOLE INFORMATION MAY NOT NECESSARILY REFLECT ACTUAL SUBSURFACE TEST DATA CAN BE RELIED ON ONLY TO THE DEGREE OF RELIABILITY INHERENT IN THE STANDARD TEST METHOD. THE OBSERVED WATER LEVELS OR SOIL MOISTURE CONDITIONS INDICATED IN THE SUBSURFACE INVESTIGATIONS ARE AS RECORDED AT THE TIME OF THE INVESTIGATION. THESE WATER LEVELS OR SOIL MOISTURE CONDITIONS MAY VARY CONSIDERABLY WITH TIME ACCORDING TO CLIMATIC CONDITIONS INCLUDING TEMPERATURES, PRECIPITATION, AND WIND, AS WELL AS OTHER NON-CLIMATIC FACTORS.

THE DEPARTMENT DOES NOT WARRANT OR GUARANTEE THE SUFFICIENCY OR ACCURACY OF THE INVESTIGATION MADE, OR OPINION OF THE DEPARTMENT AS TO THE TYPE OF MATERIALS AND CONDITIONS TO BE ENCOUNTERED. THE BIDDER OR CONTRACTOR IS CAUTIONED TO MAKE SUCH INDEPENDENT SUBSURFACE INVESTIGATIONS AS HE DEEMS NECESSARY TO SATISFY HIMSELF AS TO CONDITIONS TO BE ENCOUNTERED ON THE PROJECT. THE CONTRACTOR SHALL HAVE NO CLAIM FOR ADDITIONAL COMPENSATION OR FOR AN EXTENSION OF TIME FOR ANY REASON RESULTING FROM THE ACTUAL CONDITIONS ENCOUNTERED AT THE SITE DIFFERING FROM THOSE INDICATED IN THE SUBSURFACE INFORMATION.

NOTE - THE INFORMATION CONTAINED HEREIN IS NOT IMPLIED OR GUARANTEED BY THE N. C. DEPARTMENT OF TRANSPORTATION AS BEING ACCURATE NOR IT IS CONSIDERED TO BE PART OF THE PLANS, SPECIFICATIONS, OR CONTRACT FOR THE PROJECT.

NOTE - BY HAVING REQUESTED THIS INFORMATION THE CONTRACTOR SPECIFICALLY WAIVES ANY CLAIMS FOR INCREASED COMPENSATION OR EXTENSION OF TIME BASED ON DIFFERENCES BETWEEN THE CONDITIONS INDICATED HEREIN AND THE ACTUAL CONDITIONS AT THE PROJECT SITE.

NORTH CAROLINA PROFESSIONAL SEAL 13940 ENGINEER JON R. SKYTTA

DRAWN BY: J. SKYTTA, P.E.

PROJECT REFERENCE NO.	SHEET NO.
17BP.14.R.162	2

NORTH CAROLINA DEPARTMENT OF TRANSPORTATION
DIVISION OF HIGHWAYS
GEOTECHNICAL ENGINEERING UNIT
SOIL AND ROCK LEGEND, TERMS, SYMBOLS, AND ABBREVIATIONS

SOIL DESCRIPTION

SOIL IS CONSIDERED TO BE THE UNCONSOLIDATED, SEMI-CONSOLIDATED, OR WEATHERED EARTH MATERIALS THAT CAN BE PENETRATED WITH A CONTINUOUS FLIGHT POWER AUGER, AND YIELD LESS THAN 100 BLOWS PER FOOT ACCORDING TO STANDARD PENETRATION TEST (AASHTO T206, ASTM D-1586). SOIL CLASSIFICATION IS BASED ON THE AASHTO SYSTEM. BASIC DESCRIPTIONS GENERALLY SHALL INCLUDE: CONSISTENCY, COLOR, TEXTURE, MOISTURE, AASHTO CLASSIFICATION, AND OTHER PERTINENT FACTORS SUCH AS MINERALOGICAL COMPOSITION, ANGULARITY, STRUCTURE, PLASTICITY, ETC. EXAMPLE:

VERY STIFF, GRAY, SILTY CLAY, MOIST WITH INTERBEDDED FINE SAND LAYERS, HIGHLY PLASTIC, A-7-6

SOIL LEGEND AND AASHTO CLASSIFICATION

GENERAL CLASS.	GRANULAR MATERIALS (≤ 35% PASSING #200)							SILT-CLAY MATERIALS (> 35% PASSING #200)				ORGANIC MATERIALS		
GROUP CLASS.	A-1		A-3	A-2				A-4	A-5	A-6	A-7	A-1, A-2, A-3	A-4, A-5, A-6, A-7	
	A-1-a	A-1-b		A-2-4	A-2-5	A-2-6	A-2-7				A-7-5, A-7-6			
SYMBOL														
% PASSING #10	50 MAX											GRANULAR SOILS	SILT-CLAY SOILS	MUCK, PEAT
#40	30 MAX	50 MAX	51 MIN											
#200	15 MAX	25 MAX	10 MAX	35 MAX	35 MAX	35 MAX	35 MAX	36 MIN	36 MIN	36 MIN	36 MIN			
LIQUID LIMIT				40 MAX	41 MIN	40 MAX	41 MIN	40 MAX	41 MIN	40 MAX	41 MIN	SOILS WITH LITTLE OR MODERATE AMOUNTS OF ORGANIC MATTER		HIGHLY ORGANIC SOILS
PLASTIC INDEX	6 MAX		NP	10 MAX	10 MAX	11 MIN	11 MIN	10 MAX	10 MAX	11 MIN	11 MIN			
GROUP INDEX	0		0	0		4 MAX		8 MAX	12 MAX	16 MAX	No MAX			
USUAL TYPES OF MAJOR MATERIALS	STONE FRAGS. GRAVEL, AND SAND		FINE SAND	SILTY OR CLAYEY GRAVEL AND SAND				SILTY SOILS		CLAYEY SOILS				
GEN. RATING AS A SUBGRADE	EXCELLENT TO GOOD							FAIR TO POOR				FAIR TO POOR	POOR	UNSUITABLE

PI OF A-7-5 SUBGROUP IS ≤ LL - 30 ; PI OF A-7-6 SUBGROUP IS > LL - 30

CONSISTENCY OR DENSENESS

PRIMARY SOIL TYPE	COMPACTNESS OR CONSISTENCY	RANGE OF STANDARD PENETRATION RESISTENCE (N-VALUE)	RANGE OF UNCONFINED COMPRESSIVE STRENGTH (TONS/FT²)
GENERALLY GRANULAR MATERIAL (NON-COHESIVE)	VERY LOOSE LOOSE MEDIUM DENSE DENSE VERY DENSE	<4 4 TO 10 10 TO 30 30 TO 50 >50	N/A
GENERALLY SILT-CLAY MATERIAL (COHESIVE)	VERY SOFT SOFT MEDIUM STIFF STIFF VERY STIFF HARD	<2 2 TO 4 4 TO 8 8 TO 15 15 TO 30 >30	<0.25 0.25 TO 0.50 0.5 TO 1.0 1 TO 2 2 TO 4 >4

TEXTURE OR GRAIN SIZE

U.S. STD. SIEVE SIZE	4	10	40	60	200	270
OPENING (MM)	4.76	2.00	0.42	0.25	0.075	0.053

BOULDER (BLDR.)	COBBLE (COB.)	GRAVEL (GR.)	COARSE SAND (CSE. SD.)	FINE SAND (F SD.)	SILT (SL.)	CLAY (CL.)

GRAIN SIZE (MM): 300 | 75 | 2.0 | 0.25 | 0.05 | 0.005
GRAIN SIZE (IN.): 12 | 3

SOIL MOISTURE - CORRELATION OF TERMS

SOIL MOISTURE SCALE (ATTERBERG LIMITS)	FIELD MOISTURE DESCRIPTION	GUIDE FOR FIELD MOISTURE DESCRIPTION
	- SATURATED - (SAT.)	USUALLY LIQUID; VERY WET, USUALLY FROM BELOW THE GROUND WATER TABLE
LL - LIQUID LIMIT PLASTIC RANGE (PI) PL - PLASTIC LIMIT	- WET - (W)	SEMISOLID; REQUIRES DRYING TO ATTAIN OPTIMUM MOISTURE
OM - OPTIMUM MOISTURE SL - SHRINKAGE LIMIT	- MOIST - (M)	SOLID; AT OR NEAR OPTIMUM MOISTURE
	- DRY - (D)	REQUIRES ADDITIONAL WATER TO ATTAIN OPTIMUM MOISTURE

PLASTICITY

	PLASTICITY INDEX (PI)	DRY STRENGTH
NONPLASTIC	0-5	VERY LOW
LOW PLASTICITY	6-15	SLIGHT
MED. PLASTICITY	16-25	MEDIUM
HIGH PLASTICITY	26 OR MORE	HIGH

COLOR

DESCRIPTIONS MAY INCLUDE COLOR OR COLOR COMBINATIONS (TAN, RED, YELLOW-BROWN, BLUE-GRAY). MODIFIERS SUCH AS LIGHT, DARK, STREAKED, ETC. ARE USED TO DESCRIBE APPEARANCE.

GRADATION

WELL GRADED - INDICATES A GOOD REPRESENTATION OF PARTICLE SIZES FROM FINE TO COARSE.
UNIFORM - INDICATES THAT SOIL PARTICLES ARE ALL APPROXIMATELY THE SAME SIZE. (ALSO POORLY GRADED)
GAP-GRADED - INDICATES A MIXTURE OF UNIFORM PARTICLES OF TWO OR MORE SIZES.

ANGULARITY OF GRAINS

THE ANGULARITY OR ROUNDNESS OF SOIL GRAINS IS DESIGNATED BY THE TERMS ANGULAR, SUBANGULAR, SUBROUNDED, OR ROUNDED.

MINERALOGICAL COMPOSITION

MINERAL NAMES SUCH AS QUARTZ, FELDSPAR, MICA, TALC, KAOLIN, ETC. ARE USED IN DESCRIPTIONS WHENEVER THEY ARE CONSIDERED OF SIGNIFICANCE.

COMPRESSIBILITY

SLIGHTLY COMPRESSIBLE	LIQUID LIMIT LESS THAN 31
MODERATELY COMPRESSIBLE	LIQUID LIMIT EQUAL TO 31-50
HIGHLY COMPRESSIBLE	LIQUID LIMIT GREATER THAN 50

PERCENTAGE OF MATERIAL

ORGANIC MATERIAL	GRANULAR SOILS	SILT - CLAY SOILS
TRACE OF ORGANIC MATTER	2 - 3%	3 - 5%
LITTLE ORGANIC MATTER	3 - 5%	5 - 12%
MODERATELY ORGANIC	5 - 10%	12 - 20%
HIGHLY ORGANIC	>10%	>20%

OTHER MATERIAL	
TRACE	1 - 10%
LITTLE	10 - 20%
SOME	20 - 35%
HIGHLY	35% AND ABOVE

GROUND WATER

- WATER LEVEL IN BORE HOLE IMMEDIATELY AFTER DRILLING
- STATIC WATER LEVEL AFTER 24 HOURS
- PW PERCHED WATER, SATURATED ZONE, OR WATER BEARING STRATA
- SPRING OR SEEP

MISCELLANEOUS SYMBOLS

- ROADWAY EMBANKMENT (RE) WITH SOIL DESCRIPTION
- SOIL SYMBOL
- ARTIFICIAL FILL (AF) OTHER THAN ROADWAY EMBANKMENT
- INFERRED SOIL BOUNDARY
- INFERRED ROCK LINE
- ALLUVIAL SOIL BOUNDARY
- 25/55 DIP & DIP DIRECTION OF ROCK STRUCTURES
- TEST BORING
- AUGER BORING
- CORE BORING
- MW MONITORING WELL
- PIEZOMETER INSTALLATION
- SLOPE INDICATOR INSTALLATION
- CONE PENETROMETER TEST
- SOUNDING ROD
- TEST BORING W/ CORE
- SPT N-VALUE
- 50/.1 SPT REFUSAL

ABBREVIATIONS

AR - AUGER REFUSAL
BT - BORING TERMINATED
CL. - CLAY
CPT - CONE PENETRATION TEST
CSE. - COARSE
DMT - DILATOMETER TEST
DPT - DYNAMIC PENETRATION TEST
e - VOID RATIO
F - FINE
FOSS. - FOSSILIFEROUS
FRAC. - FRACTURED, FRACTURES
FRAGS. - FRAGMENTS
HI. - HIGHLY
MED. - MEDIUM
MICA. - MICACEOUS
MOD. - MODERATELY
NP - NON PLASTIC
ORG. - ORGANIC
PMT - PRESSUREMETER TEST
SAP. - SAPROLITIC
SD. - SAND, SANDY
SL. - SILT, SILTY
SLI. - SLIGHTLY
TCR - TRICONE REFUSAL
w - MOISTURE CONTENT
V - VERY
VST - VANE SHEAR TEST
WEA. - WEATHERED
γ - UNIT WEIGHT
γ_d - DRY UNIT WEIGHT

SAMPLE ABBREVIATIONS
S - BULK
SS - SPLIT SPOON
ST - SHELBY TUBE
RS - ROCK
RT - RECOMPACTED TRIAXIAL
CBR - CALIFORNIA BEARING RATIO

EQUIPMENT USED ON SUBJECT PROJECT

DRILL UNITS:
- [ ] MOBILE B-__
- [ ] BK-51
- [ ] CME-45C
- [X] CME-550
- [ ] PORTABLE HOIST
- [ ] _____
- [ ] _____

ADVANCING TOOLS:
- [ ] CLAY BITS
- [ ] 6" CONTINUOUS FLIGHT AUGER
- [ ] 8" HOLLOW AUGERS
- [ ] HARD FACED FINGER BITS
- [ ] TUNG.-CARBIDE INSERTS
- [ ] CASING [ ] W/ ADVANCER
- [ ] TRICONE ____" STEEL TEETH
- [ ] TRICONE ____" TUNG.-CARB.
- [ ] CORE BIT
- [X] 3-1/4" HSA

HAMMER TYPE:
- [X] AUTOMATIC
- [ ] MANUAL

CORE SIZE:
- [ ] -B____
- [ ] -NQ____
- [ ] -H____

HAND TOOLS:
- [ ] POST HOLE DIGGER
- [ ] HAND AUGER
- [ ] SOUNDING ROD
- [ ] VANE SHEAR TEST
- [ ] _____

REVISED 08/23/00

PROJECT REFERENCE NO.	SHEET NO.
17BP.14.R.162	2A

NORTH CAROLINA DEPARTMENT OF TRANSPORTATION
DIVISION OF HIGHWAYS
GEOTECHNICAL ENGINEERING UNIT
SOIL AND ROCK LEGEND, TERMS, SYMBOLS, AND ABBREVIATIONS

ROCK DESCRIPTION

HARD ROCK IS NON-COASTAL PLAIN MATERIAL THAT IF TESTED, WOULD YIELD SPT REFUSAL. AN INFERRED ROCK LINE INDICATES THE LEVEL AT WHICH NON-COASTAL PLAIN MATERIAL WOULD YIELD SPT REFUSAL. SPT REFUSAL IS PENETRATION BY A SPLIT SPOON SAMPLER EQUAL TO OR LESS THAN 0.1 FOOT PER 60 BLOWS. IN NON-COASTAL PLAIN MATERIAL, THE TRANSITION BETWEEN SOIL AND ROCK IS OFTEN REPRESENTED BY A ZONE OF WEATHERED ROCK.
ROCK MATERIALS ARE TYPICALLY DIVIDED AS FOLLOWS:

WEATHERED ROCK (WR)	NON-COASTAL PLAIN MATERIAL THAT WOULD YIELD SPT N VALUES > 100 BLOWS PER FOOT IF TESTED.
CRYSTALLINE ROCK (CR)	FINE TO COARSE GRAIN IGNEOUS AND METAMORPHIC ROCK THAT WOULD YIELD SPT REFUSAL IF TESTED. ROCK TYPE INCLUDES GRANITE, GNEISS, GABBRO, SCHIST, ETC.
NON-CRYSTALLINE ROCK (NCR)	FINE TO COARSE GRAIN METAMORPHIC AND NON-COASTAL PLAIN SEDIMENTARY ROCK THAT WOULD YEILD SPT REFUSAL IF TESTED. ROCK TYPE INCLUDES PHYLLITE, SLATE, SANDSTONE, ETC.
COASTAL PLAIN SEDIMENTARY ROCK (CP)	COASTAL PLAIN SEDIMENTS CEMENTED INTO ROCK, BUT MAY NOT YIELD SPT REFUSAL. ROCK TYPE INCLUDES LIMESTONE, SANDSTONE, CEMENTED SHELL BEDS, ETC.

WEATHERING

FRESH	ROCK FRESH, CRYSTALS BRIGHT, FEW JOINTS MAY SHOW SLIGHT STAINING. ROCK RINGS UNDER HAMMER IF CRYSTALLINE.
VERY SLIGHT (V SLI.)	ROCK GENERALLY FRESH, JOINTS STAINED, SOME JOINTS MAY SHOW THIN CLAY COATINGS IF OPEN, CRYSTALS ON A BROKEN SPECIMEN FACE SHINE BRIGHTLY. ROCK RINGS UNDER HAMMER BLOWS IF OF A CRYSTALLINE NATURE.
SLIGHT (SLI.)	ROCK GENERALLY FRESH, JOINTS STAINED AND DISCOLORATION EXTENDS INTO ROCK UP TO 1 INCH. OPEN JOINTS MAY CONTAIN CLAY. IN GRANITOID ROCKS SOME OCCASIONAL FELDSPAR CRYSTALS ARE DULL AND DISCOLORED. CRYSTALLINE ROCKS RING UNDER HAMMER BLOWS.
MODERATE (MOD.)	SIGNIFICANT PORTIONS OF ROCK SHOW DISCOLORATION AND WEATHERING EFFECTS. IN GRANITOID ROCKS, MOST FELDSPARS ARE DULL AND DISCOLORED, SOME SHOW CLAY. ROCK HAS DULL SOUND UNDER HAMMER BLOWS AND SHOWS SIGNIFICANT LOSS OF STRENGTH AS COMPARED WITH FRESH ROCK.
MODERATELY SEVERE (MOD. SEV.)	ALL ROCK EXCEPT QUARTZ DISCOLORED OR STAINED. IN GRANITOID ROCKS, ALL FELDSPARS DULL AND DISCOLORED AND A MAJORITY SHOW KAOLINIZATION. ROCK SHOWS SEVERE LOSS OF STRENGTH AND CAN BE EXCAVATED WITH A GEOLOGIST'S PICK. ROCK GIVES "CLUNK" SOUND WHEN STRUCK. *IF TESTED, WOULD YIELD SPT REFUSAL*
SEVERE (SEV.)	ALL ROCK EXCEPT QUARTZ DISCOLORED OR STAINED. ROCK FABRIC CLEAR AND EVIDENT BUT REDUCED IN STRENGTH TO STRONG SOIL. IN GRANITOID ROCKS ALL FELDSPARS ARE KAOLINIZED TO SOME EXTENT. SOME FRAGMENTS OF STRONG ROCK USUALLY REMAIN. *IF TESTED, YIELDS SPT N VALUES > 100 BPF*
VERY SEVERE (V SEV.)	ALL ROCK EXCEPT QUARTZ DISCOLORED OR STAINED. ROCK FABRIC ELEMENTS ARE DISCERNIBLE BUT THE MASS IS EFFECTIVELY REDUCED TO SOIL STATUS, WITH ONLY FRAGMENTS OF STRONG ROCK REMAINING. SAPROLITE IS AN EXAMPLE OF ROCK WEATHERED TO A DEGREE SUCH THAT ONLY MINOR VESTIGES OF THE ORIGINAL ROCK FABRIC REMAIN. *IF TESTED, YIELDS SPT N VALUES < 100 BPF*
COMPLETE	ROCK REDUCED TO SOIL. ROCK FABRIC NOT DISCERNIBLE, OR DISCERNIBLE ONLY IN SMALL AND SCATTERED CONCENTRATIONS. QUARTZ MAY BE PRESENT AS DIKES OR STRINGERS. SAPROLITE IS ALSO AN EXAMPLE.

ROCK HARDNESS

VERY HARD	CANNOT BE SCRATCHED BY KNIFE OR SHARP PICK. BREAKING OF HAND SPECIMENS REQUIRES SEVERAL HARD BLOWS OF THE GEOLOGIST'S PICK.
HARD	CAN BE SCRATCHED BY KNIFE OR PICK ONLY WITH DIFFICULTY. HARD HAMMER BLOWS REQUIRED TO DETACH HAND SPECIMEN.
MODERATELY HARD	CAN BE SCRATCHED BY KNIFE OR PICK. GOUGES OR GROOVES TO 0.25 INCHES DEEP CAN BE EXCAVATED BY HARD BLOW OF A GEOLOGIST'S PICK. HAND SPECIMENS CAN BE DETACHED BY MODERATE BLOWS.
MEDIUM HARD	CAN BE GROOVED OR GOUGED 0.05 INCHES DEEP BY FIRM PRESSURE OF KNIFE OR PICK POINT. CAN BE EXCAVATED IN SMALL CHIPS TO PIECES 1 INCH MAXIMUM SIZE BY HARD BLOWS OF THE POINT OF A GEOLOGIST'S PICK.
SOFT	CAN BE GROVED OR GOUGED READILY BY KNIFE OR PICK. CAN BE EXCAVATED IN FRAGMENTS FROM CHIPS TO SEVERAL INCHES IN SIZE BY MODERATE BLOWS OF A PICK POINT. SMALL, THIN PIECES CAN BE BROKEN BY FINGER PRESSURE.
VERY SOFT	CAN BE CARVED WITH KNIFE. CAN BE EXCAVATED READILY WITH POINT OF PICK. PIECES 1 INCH OR MORE IN THICKNESS CAN BE BROKEN BY FINGER PRESSURE. CAN BE SCRATCHED READILY BY FINGERNAIL.

FRACTURE SPACING

TERM	SPACING
VERY WIDE	MORE THAN 10 FEET
WIDE	3 TO 10 FEET
MODERATELY CLOSE	1 TO 3 FEET
CLOSE	0.05 TO 1 FEET
VERY CLOSE	LESS THAN 0.05 FEET

BEDDING

TERM	THICKNESS
VERY THICKLY BEDDED	> 4 FEET
THICKLY BEDDED	1.5 - 4 FEET
THINLY BEDDED	0.05 - 1.5 FEET
VERY THINLY BEDDED	0.03 - 0.05 FEET
THICKLY LAMINATED	0.008 - 0.03 FEET
THINLY LAMINATED	< 0.008 FEET

INDURATION

FOR SEDIMENTARY ROCKS, INDURATION IS THE HARDENING OF THE MATERIAL BY CEMENTING, HEAT, PRESSURE, ETC.

FRIABLE	RUBBING WITH FINGER FREES NUMEROUS GRAINS; GENTLE BLOW BY HAMMER DISINTEGRATES SAMPLE.
MODERATELY INDURATED	GRAINS CAN BE SEPARATED FROM SAMPLE WITH STEEL PROBE; BREAKS EASILY WHEN HIT WITH HAMMER.
INDURATED	GRAINS ARE DIFFICULT TO SEPARATE WITH STEEL PROBE; DIFFICULT TO BREAK WITH HAMMER.
EXTREMELY INDURATED	SHARP HAMMER BLOWS REQUIRED TO BREAK SAMPLE; SAMPLE BREAKS across GRAINS.

TERMS AND DEFINITIONS

ALLUVIUM (ALLUV.) - SOILS THAT HAVE BEEN TRANSPORTED BY WATER.

AQUIFER - A WATER BEARING FORMATION OR STRATA.

ARENACEOUS - APPLIED TO ROCKS THAT HAVE BEEN DERIVED FROM SAND OR THAT CONTAIN SAND.

ARGILLACEOUS - APPLIED TO ALL ROCKS OR SUBSTANCES COMPOSED OF CLAY MINERALS, OR HAVING A NOTABLE PROPORTION OF CLAY IN THEIR COMPOSITION, AS SHALE, SLATE, ETC.

ARTESIAN - GROUND WATER THAT IS UNDER SUFFICIENT PRESSURE TO RISE ABOVE THE LEVEL AT WHICH IT IS ENCOUNTERED, BUT WHICH DOES NOT NECESSARILY RISE TO OR ABOVE THE GROUND SURFACE.

CALCAREOUS (CALC.) - SOILS THAT CONTAIN APPRECIABLE AMOUNTS OF CALCIUM CARBONATE.

COLLUVIUM - ROCK FRAGMENTS MIXED WITH SOIL DEPOSITED BY GRAVITY ON SLOPE OR AT BOTTOM OF SLOPE.

CORE RECOVERY (REC.) - TOTAL LENGTH OF ALL MATERIAL RECOVERED IN THE CORE BARREL DIVIDED BY TOTAL LENGTH OF CORE RUN AND EXPRESSED AS A PERCENTAGE.

DIKE - A TABULAR BODY OF IGNEOUS ROCK THAT CUTS ACROSS THE STRUCTURE OF ADJACENT ROCKS OR CUTS MASSIVE ROCK.

DIP - THE ANGLE AT WHICH A STRATUM OR ANY PLANAR FEATURE IS INCLINED FROM THE HORIZONTAL.

DIP DIRECTION (DIP AZIMUTH) - THE DIRECTION OR BEARING OF THE HORIZONTAL TRACE OF THE LINE OF DIP, MEASURED CLOCKWISE FROM NORTH.

FAULT - A FRACTURE OR FRACTURE ZONE ALONG WHICH THERE HAS BEEN DISPLACEMENT OF THE SIDES RELATIVE TO ONE ANOTHER PARALLEL TO THE FRACTURE.

FISSILE - A PROPERTY OF SPLITTING ALONG CLOSELY SPACED PARALLEL PLANES.

FLOAT - ROCK FRAGMENTS ON SURFACE NEAR THEIR ORIGINAL POSITION AND DISLODGED FROM PARENT MATERIAL.

FLOOD PLAIN (FP) - LAND BORDERING A STREAM, BUILT OF SEDIMENTS DEPOSITED BY THE STREAM.

FORMATION (FM.) - A MAPPABLE GEOLOGIC UNIT THAT CAN BE RECOGNIZED AND TRACED IN THE FIELD.

JOINT - FRACTURE IN ROCK ALONG WHICH NO APPRECIABLE MOVEMENT HAS OCCURRED.

LEDGE - A SHELF-LIKE RIDGE OR PROJECTION OF ROCK WHOSE THICKNESS IS SMALL COMPARED TO ITS LATERAL EXTENT.

LENS - A BODY OF SOIL OR ROCK THAT THINS OUT IN ONE OR MORE DIRECTIONS.

MOTTLED (MOT.) - IRREGULARLY MARKED WITH SPOTS OF DIFFERENT COLORS. MOTTLING IN SOILS USUALLY INDICATES POOR AERATION AND LACK OF GOOD DRAINAGE.

PERCHED WATER - WATER MAINTAINED ABOVE THE NORMAL GROUND WATER LEVEL BY THE PRESENCE OF AN INTERVENING IMPERVIOUS STRATUM.

RESIDUAL (RES.) SOIL - SOIL FORMED IN PLACE BY THE WEATHERING OF ROCK.

ROCK QUALITY DESIGNATION (RQD) - A MEASURE OF ROCK QUALITY DESCRIBED BY TOTAL LENGTH OF ROCK SEGMENTS EQUAL TO OR GREATER THAN 4 INCHES DIVIDED BY THE TOTAL LENGTH OF CORE RUN AND EXPRESSED AS A PERCENTAGE.

SAPROLITE (SAP.) - RESIDUAL SOIL THAT RETAINS THE RELIC STRUCTURE OR FABRIC OF THE PARENT ROCK.

SILL - AN INTRUSIVE BODY OF IGNEOUS ROCK OF APPROXIMATELY UNIFORM THICKNESS AND RELATIVELY THIN COMPARED WITH ITS LATERAL EXTENT, THAT HAS BEEN EMPLACED PARALLEL TO THE BEDDING OR SCHISTOSITY OF THE INTRUDED ROCKS.

SLICKENSIDE - POLISHED AND STRIATED SURFACE THAT RESULTS FROM FRICTION ALONG A FAULT OR SLIP PLANE.

STANDARD PENETRATION TEST (PENETRATION RESISTANCE) (SPT) - NUMBER OF BLOWS (N OR BPF) OF A 140 LB. HAMMER FALLING 30 INCHES REQUIRED TO PRODUCE A PENETRATION OF 1 FOOT INTO SOIL WITH A 2 INCH OUTSIDE DIAMETER SPLIT SPOON SAMPLER. SPT REFUSAL IS PENETRATION EQUAL TO OR LESS THAN 0.1 FOOT PER 60 BLOWS.

STRATA CORE RECOVERY (SREC.) - TOTAL LENGTH OF STRATA MATERIAL RECOVERED DIVIDED BY TOTAL LENGTH OF STRATUM AND EXPRESSED AS A PERCENTAGE.

STRATA ROCK QUALITY DESIGNATION (SRQD) - A MEASURE OF ROCK QUALITY DESCRIBED BY TOTAL LENGTH OF ROCK SEGMENTS WITHIN A STRATUM EQUAL TO OR GREATER THAN 4 INCHES DIVIDED BY THE TOTAL LENGTH OF STRATA AND EXPRESSED AS A PERCENTAGE.

TOPSOIL (TS.) - SURFACE SOILS USUALLY CONTAINING ORGANIC MATTER.

BENCH MARK: BL-2

ELEVATION: 1963.31 feet

NOTES:
Boring elevations determined by normal surveying techniques with reference to BL-2, Elev. 1963.31 feet.

REVISED 08/23/08

N

Date of Aerial Photograph: October 2015
Obtained from Google Earth

Boring Locations Bridge No. 550088 over Cowee Creek on SR 1472 (Snow Hill Rd.) Macon Co., North Carolina State Project No. 17BP.14.R.162	STV Engineers, Inc.	Scale: 1"= 40' (approx.) Date: August 2016 Project: 4017927-1008 SHEET 3

NCDOT GEOTECHNICAL ENGINEERING UNIT
BORELOG REPORT

WBS 17BP.14.R.162	**TIP** N/A	**COUNTY** Macon	**GEOLOGIST** J. Skytta, PE
SITE DESCRIPTION Bridge 550088 on SR 1472 (Snow Hill Road) over Cowee Creek			**GROUND WTR (ft)**
BORING NO. EB1-A	**STATION** 12+67	**OFFSET** 7 ft LT	**ALIGNMENT** -L-
COLLAR ELEV. 1,964.8 ft	**TOTAL DEPTH** 57.6 ft	**NORTHING** 684,308	**EASTING** 579,682
DRILL RIG/HAMMER EFF./DATE CME-55/93%/2-22-15		**DRILL METHOD** H.S. Augers	**HAMMER TYPE** Automatic
DRILLER AmeriDrill	**START DATE** 06/14/16	**COMP. DATE** 06/14/16	**SURFACE WATER DEPTH** N/A

GROUND WTR (ft)	
0 HR.	14.1
24 HR.	FIAD

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT (0 25 50 75 100)	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION (ELEV. (ft) / DEPTH (ft))
1965										
	1,963.8	1.0								1,964.8 GROUND SURFACE 0.0
			16	12	8	20	SS-1	M		1,964.0 **PAVEMENT** 0.8 — 5 inches asphalt on 4 inches stone
	1,961.3	3.5								**ROADWAY EMBANKMENT**
1960			5	2	2	4	SS-2	M		Very stiff to soft dark brown red slightly fine to coarse sandy clayey SILT, with rock pieces, some organics
	1,958.8	6.0								1,958.8 6.0
			WOH	WOH	WOH	0	SS-3	W		**RESIDUAL**
	1,956.3	8.5								Very loose tan silty fine to medium SAND
1955			WOH	WOH	WOH	0	SS-4	W		
	1,951.3	13.5								
1950			2	1	2	3	SS-5	Sat.		
	1,946.3	18.5								
1945			3	4	8	12	SS-6	W		
										1,942.8 22.0
	1,941.3	23.5								Loose to medium dense orange brown silty fine to coarse SAND
1940			1	2	2	4	SS-7	W		
	1,936.3	28.5								
1935			3	3	6	9	SS-8	W		
										1,932.8 32.0
	1,931.3	33.5								Medium dense brown white silty fine to coarse SAND
1930			4	5	6	11	SS-9	W		
										1,927.8 37.0
	1,926.3	38.5								Dense to medium dense yellow orange white brown silty fine to coarse SAND, with weathered rock pieces
1925			4	11	23	34	SS-10	M		
	1,921.3	43.5								
1920			6	10	16	26	SS-11	M		
	1,916.3	48.5								
1915			8	11	15	26	SS-12	M		
	1,911.3	53.5								
1910			12	34	66/0.4		SS-13	M		1,910.3 54.5
										WEATHERED ROCK
	1,907.2	57.6	50/0.0							1,907.2 Weathered rock sampled as tan white slightly silty fine to medium SAND, with weathered rock pieces 57.6
										Boring Terminated by Auger Refusal at Elevation 1,907.2 ft

NCDOT GEOTECHNICAL ENGINEERING UNIT
BORELOG REPORT

WBS 17BP.14.R.162	**TIP** N/A	**COUNTY** Macon	**GEOLOGIST** J. Skytta, PE
SITE DESCRIPTION Bridge 550088 on SR 1472 (Snow Hill Road) over Cowee Creek			**GROUND WTR (ft)**
BORING NO. EB1-B	**STATION** 12+60	**OFFSET** 6 ft RT	**ALIGNMENT** -L- — **0 HR.** 12.0
COLLAR ELEV. 1,964.8 ft	**TOTAL DEPTH** 52.3 ft	**NORTHING** 684,320	**EASTING** 579,682 — **24 HR.** FIAD
DRILL RIG/HAMMER EFF./DATE CME-55/93%/2-22-15		**DRILL METHOD** H.S. Augers	**HAMMER TYPE** Automatic
DRILLER AmeriDrill	**START DATE** 06/14/16	**COMP. DATE** 06/14/16	**SURFACE WATER DEPTH** N/A

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT (0 25 50 75 100)	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION (ELEV. ft / DEPTH ft)
1965										
	1,963.8	1.0								1,964.8 GROUND SURFACE 0.0
			6	4	3	7	SS-1	M		1,964.1 **PAVEMENT** 0.7 — 4 inches asphalt on 4 inches stone
	1,961.3	3.5								**ROADWAY EMBANKMENT**
1960			1	2	2	4	SS-2	M		Firm to soft brown red fine to coarse sandy clayey SILT, with rock pieces, some organics
	1,958.8	6.0								1,958.8 6.0
			WOH	WOH	1	1	SS-3	W		**RESIDUAL**
	1,956.3	8.5								Very loose to loose tan silty fine to coarse SAND
1955			WOH	1	2	3	SS-4	W		
	1,951.3	13.5								
1950			2	4	4	8	SS-5	M		
	1,946.3	18.5								1,947.8 17.0
1945			1	2	4	6	SS-6	M		Loose to medium dense orange silty fine to coarse SAND, micaceous
	1,941.3	23.5								
1940			3	6	7	13	SS-7	M		
	1,936.3	28.5								1,936.8 28.0
1935			3	5	6	11	SS-8	M		Medium dense orange yellow white brown silty fine to coarse SAND, with weathered rock pieces
	1,931.3	33.5								
1930			8	12	17	29	SS-9	M		
	1,926.3	38.5								
1925			6	11	15	26	SS-10	M		
	1,921.3	43.5								
1920			5	7	8	15	SS-11	M		
	1,916.3	48.5								1,917.8 47.0
1915			8	10	12	22	SS-12	M		Medium dense dark brown orange silty fine to coarse SAND, with weathered rock pieces
	1,912.5	52.3	30/0.0							1,912.5 52.3
										Boring Terminated by Auger Refusal at Elevation 1,912.5 ft

NCDOT BORE SINGLE DIV 14 BR 088.GPJ NC_DOT.GDT 9/19/16

NCDOT GEOTECHNICAL ENGINEERING UNIT
BORELOG REPORT

WBS 17BP.14.R.162	**TIP** N/A	**COUNTY** Macon	**GEOLOGIST** J. Skytta, PE
SITE DESCRIPTION Bridge 550088 on SR 1472 (Snow Hill Road) over Cowee Creek			**GROUND WTR (ft)**
BORING NO. EB2-A	**STATION** 13+31	**OFFSET** 9 ft LT	**ALIGNMENT** -L- / **0 HR.** 11.7
COLLAR ELEV. 1,964.3 ft	**TOTAL DEPTH** 52.5 ft	**NORTHING** 684,275	**EASTING** 579,741 / **24 HR.** FIAD
DRILL RIG/HAMMER EFF./DATE CME-55/93%/2-22-15		**DRILL METHOD** H.S. Augers	**HAMMER TYPE** Automatic
DRILLER AmeriDrill	**START DATE** 06/14/16	**COMP. DATE** 06/14/16	**SURFACE WATER DEPTH** N/A

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	BLOWS PER FOOT (0 25 50 75 100)	SAMP. NO.	MOI	LOG	SOIL AND ROCK DESCRIPTION (ELEV. (ft) / DEPTH (ft))
1965										
										1,964.3 GROUND SURFACE 0.0
	1,963.3	1.0								1,963.6 **PAVEMENT** 0.7
			5	7	10	17	SS-1	M		2 inches asphalt on 6 inches stone
1960	1,960.8	3.5								**ROADWAY EMBANKMENT**
			2	1	2	3	SS-2	W		Very stiff to soft brown red slightly fine to medium sandy clayey SILT
	1,958.3	6.0								1,958.3 6.0
			1	1	WOH	1	SS-3	W		**RESIDUAL**
1955	1,955.8	8.5								Very loose to loose olive gray silty fine to medium SAND
			WOH	WOH	1	1	SS-4	Sat.		
1950	1,950.8	13.5								
			12	5	5	10	SS-5	M		
										1,948.3 16.0
1945	1,945.8	18.5								Firm to stiff yellow orange slightly clayey fine to medium sandy SILT
			1	2	3	5	SS-6	M		
1940	1,940.8	23.5								
			WOH	3	5	8	SS-7	M		
1935	1,935.8	28.5								
			3	5	8	13	SS-8	M		
										1,932.3 32.0
1930	1,930.8	33.5								Loose to medium dense orange yellow white silty fine to coarse SAND
			3	4	5	9	SS-9	M		
1925	1,925.8	38.5								
			4	6	9	15	SS-10	M		
										1,922.3 42.0
1920	1,920.8	43.5								Loose dark brown white brown silty fine SAND, with weathered rock pieces
			3	3	4	7	SS-11	M		
										1,917.3 47.0
1915	1,915.8	48.5								
			23	16	10	26	SS-12	M		Medium dense dark brown white silty fine to coarse SAND, with weathered rock pieces
										1,911.8 52.5
										Boring Terminated by Auger Refusal at Elevation 1,911.8 ft

NCDOT GEOTECHNICAL ENGINEERING UNIT
BORELOG REPORT

WBS 17BP.14.R.162	**TIP** N/A	**COUNTY** Macon	**GEOLOGIST** J. Skytta, PE
SITE DESCRIPTION Bridge 550088 on SR 1472 (Snow Hill Road) over Cowee Creek			**GROUND WTR (ft)**
BORING NO. EB2-B	**STATION** 13+29	**OFFSET** 8 ft RT	**ALIGNMENT** -L- — **0 HR.** 11.2
COLLAR ELEV. 1,964.4 ft	**TOTAL DEPTH** 51.0 ft	**NORTHING** 684,290	**EASTING** 579,745 — **24 HR.** FIAD
DRILL RIG/HAMMER EFF./DATE CME-55/93%/2-22-15		**DRILL METHOD** H.S. Augers	**HAMMER TYPE** Automatic
DRILLER AmeriDrill	**START DATE** 06/14/16	**COMP. DATE** 06/14/16	**SURFACE WATER DEPTH** N/A

ELEV (ft)	DRIVE ELEV (ft)	DEPTH (ft)	BLOW COUNT 0.5ft	0.5ft	0.5ft	SAMP. NO.	MOI
1965							
	1,963.4	1.0					
			4	7	6	SS-1	M
1960	1,960.9	3.5					
			2	2	2	SS-2	M
	1,958.4	6.0					
			1	1	0	SS-3	W
1955	1,955.9	8.5					
			WOH	WOH	WOH	SS-4	Sat.
1950	1,950.9	13.5					
			2	4	5	SS-5	M
1945	1,945.9	18.5					
			3	4	5	SS-6	M
1940	1,940.9	23.5					
			3	4	7	SS-7	M
1935	1,935.9	28.5					
			4	7	10	SS-8	M
1930	1,930.9	33.5					
			4	6	10	SS-9	M
1925	1,925.9	38.5					
			6	8	12	SS-10	M
1920	1,920.9	43.5					
			9	26	28	SS-11	M
1915	1,915.9	48.5					
			19	62	38/0.2	SS-12	M
	1,913.4	51.0	50/0.0				

BLOWS PER FOOT (0, 25, 50, 75, 100)

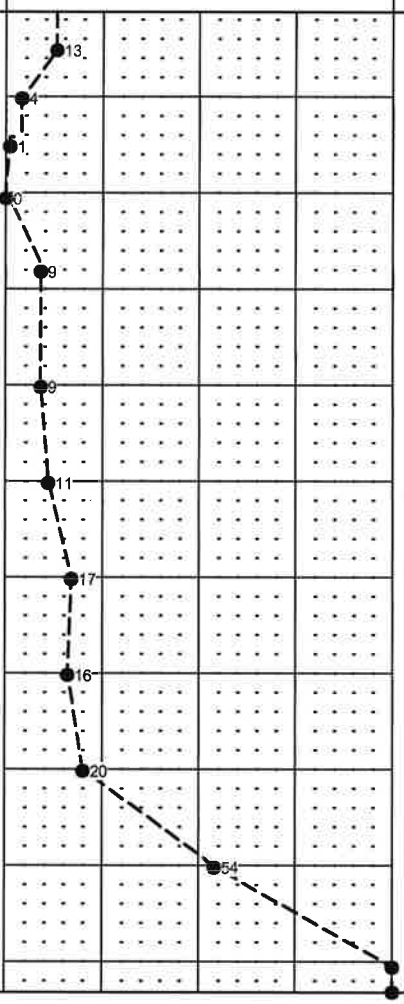

LOG

ELEV. (ft)	SOIL AND ROCK DESCRIPTION	DEPTH (ft)
1,964.4	GROUND SURFACE	0.0
1,963.7	**PAVEMENT** 5 inches asphalt on 3 inches stone	0.7
	ROADWAY EMBANKMENT Soft to very soft red brown fine to coarse sandy clayey SILT, with rock pieces, trace organics	
1,957.9	**RESIDUAL** Very loose olive green silty fine to medium SAND	6.5
1,951.9	Loose to medium dense orange brown slightly clayey silty fine to coarse SAND	12.5
1,937.4	Medium dense orange yellow white silty fine to coarse SAND	27.0
1,922.4	Very dense tan brown gray silty fine to coarse SAND, with weathered rock pieces	42.0
1,915.4	**WEATHERED ROCK** Weathered rock sampled as dark brown white silty fine SAND, with weathered rock pieces	49.0
1,913.4	Boring Terminated by Auger Refusal at Elevation 1,913.4 ft	51.0

NCDOT BORE SINGLE DIV 14 BR 088.GPJ NC_DOT.GDT 9/19/16
