Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

Jones Tract Subdivision
SR 1010, Johnston County,North Carolina
Steel Bridge Road & SR 1010

File Name : count 6
Site Code : 00033333
Start Date : 9/10/2015
Page No : 1

Groups Printed- Unshifted - Bank 1

	Steel Bridge Road					SR 1010					Steel Bridge Road					SR 1010					
Start Time					App. Total					App. Total					App. Total					App. Total	Int. Total
07:00 AM	9	0	15	0	24	0	43	23	0	66	0	0	0	0	0	18	77	0	0	95	185
07:15 AM	3	0	16	0	19	0	39	19	0	58	0	0	0	0	0	13	76	0	0	89	166
07:30 AM	8	0	10	0	18	0	49	11	0	60	0	0	0	0	0	11	93	0	0	104	182
07:45 AM	4	0	17	0	21	0	38	14	0	52	0	0	0	0	0	7	46	0	0	53	126
Total	24	0	58	0	82	0	169	67	0	236	0	0	0	0	0	49	292	0	0	341	659
08:00 AM	4	0	21	0	25	0	42	12	0	54	0	0	0	0	0	4	38	0	0	42	121
08:15 AM	6	0	22	0	28	0	50	11	0	61	0	0	0	0	0	8	49	0	0	57	146
08:30 AM	6	0	13	0	19	0	40	7	0	47	0	0	0	0	0	16	52	0	0	68	134
08:45 AM	1	0	4	0	5	0	13	5	0	18	0	0	0	0	0	11	49	0	0	60	83
Total	17	0	60	0	77	0	145	35	0	180	0	0	0	0	0	39	188	0	0	227	484
*** BREAK ***																					
04:00 PM	6	0	7	0	13	0	56	1	0	57	0	0	0	0	0	19	60	0	0	79	149
04:15 PM	11	0	9	0	20	0	41	6	0	47	0	0	0	0	0	20	52	0	0	72	139
04:30 PM	15	0	16	0	31	0	42	5	0	47	0	0	0	0	0	16	36	0	0	52	130
04:45 PM	10	0	14	0	24	1	55	12	0	68	0	0	0	0	0	18	44	0	0	62	154
Total	42	0	46	0	88	1	194	24	0	219	0	0	0	0	0	73	192	0	0	265	572
05:00 PM	12	0	11	0	23	1	65	7	0	73	0	0	0	0	0	12	63	0	0	75	171
05:15 PM	21	0	15	0	36	0	102	12	0	114	0	0	0	0	0	9	49	0	0	58	208
05:30 PM	10	0	18	0	28	0	75	9	0	84	0	0	0	0	0	10	51	0	0	61	173
05:45 PM	10	0	30	0	40	0	57	6	1	64	0	0	0	0	0	16	42	0	0	58	162
Total	53	0	74	0	127	1	299	34	1	335	0	0	0	0	0	47	205	0	0	252	714
Grand Total	136	0	238	0	374	2	807	160	1	970	0	0	0	0	0	208	877	0	0	1085	2429
Apprch %	36.4	0	63.6	0		0.2	83.2	16.5	0.1		0	0	0	0		19.2	80.8	0	0		
Total %	5.6	0	9.8	0	15.4	0.1	33.2	6.6	0	39.9	0	0	0	0	0	8.6	36.1	0	0	44.7	
Unshifted	136	0	238	0	374	2	807	160	1	970	0	0	0	0	0	208	877	0	0	1085	2429
% Unshifted	100	0	100	0	100	100	100	100	100	100	0	0	0	0	0	100	100	0	0	100	100
Bank 1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
% Bank 1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

Jones Tract Subdivision
SR 1010, Johnston County,North Carolina
Steel Bridge Road & SR 1010

File Name : count 6
Site Code : 00033333
Start Date : 9/10/2015
Page No : 2

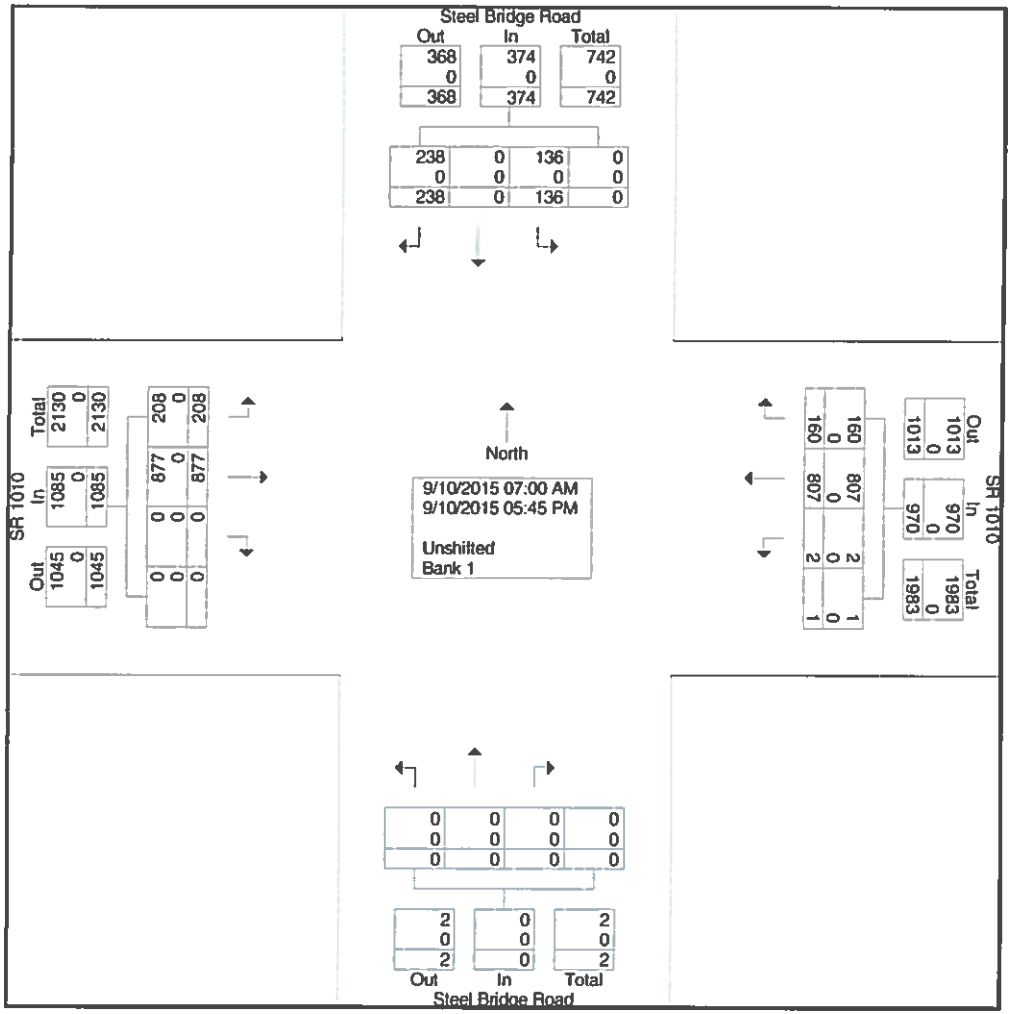

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

Jones Tract Subdivision
SR 1010, Johnston County,North Carolina
Steel Bridge Road & SR 1010

File Name : count 6
Site Code : 00033333
Start Date : 9/10/2015
Page No : 4

	Steel Bridge Road					SR 1010					Steel Bridge Road					SR 1010					
Start Time					App. Total					App. Total					App. Total					App. Total	Int. Total
Peak Hour Analysis From 07:00 AM to 11:45 AM - Peak 1 of 1																					
Peak Hour for Entire Intersection Begins at 07:00 AM																					
07:00 AM	9	0	15	0	24	0	43	23	0	66	0	0	0	0	0	18	77	0	0	95	185
07:15 AM	3	0	16	0	19	0	39	19	0	58	0	0	0	0	0	13	76	0	0	89	166
07:30 AM	8	0	10	0	18	0	49	11	0	60	0	0	0	0	0	11	93	0	0	104	182
07:45 AM	4	0	17	0	21	0	38	14	0	52	0	0	0	0	0	7	46	0	0	53	126
Total Volume	24	0	58	0	82	0	169	67	0	236	0	0	0	0	0	49	292	0	0	341	659
% App. Total	29.3	0	70.7	0		0	71.6	28.4	0		0	0	0	0		14.4	85.6	0	0		
PHF	.667	.000	.853	.000	.854	.000	.862	.728	.000	.894	.000	.000	.000	.000	.000	.681	.785	.000	.000	.820	.891

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

Jones Tract Subdivision
SR 1010, Johnston County,North Carolina
Steel Bridge Road & SR 1010

File Name : count 6
Site Code : 00033333
Start Date : 9/10/2015
Page No : 5

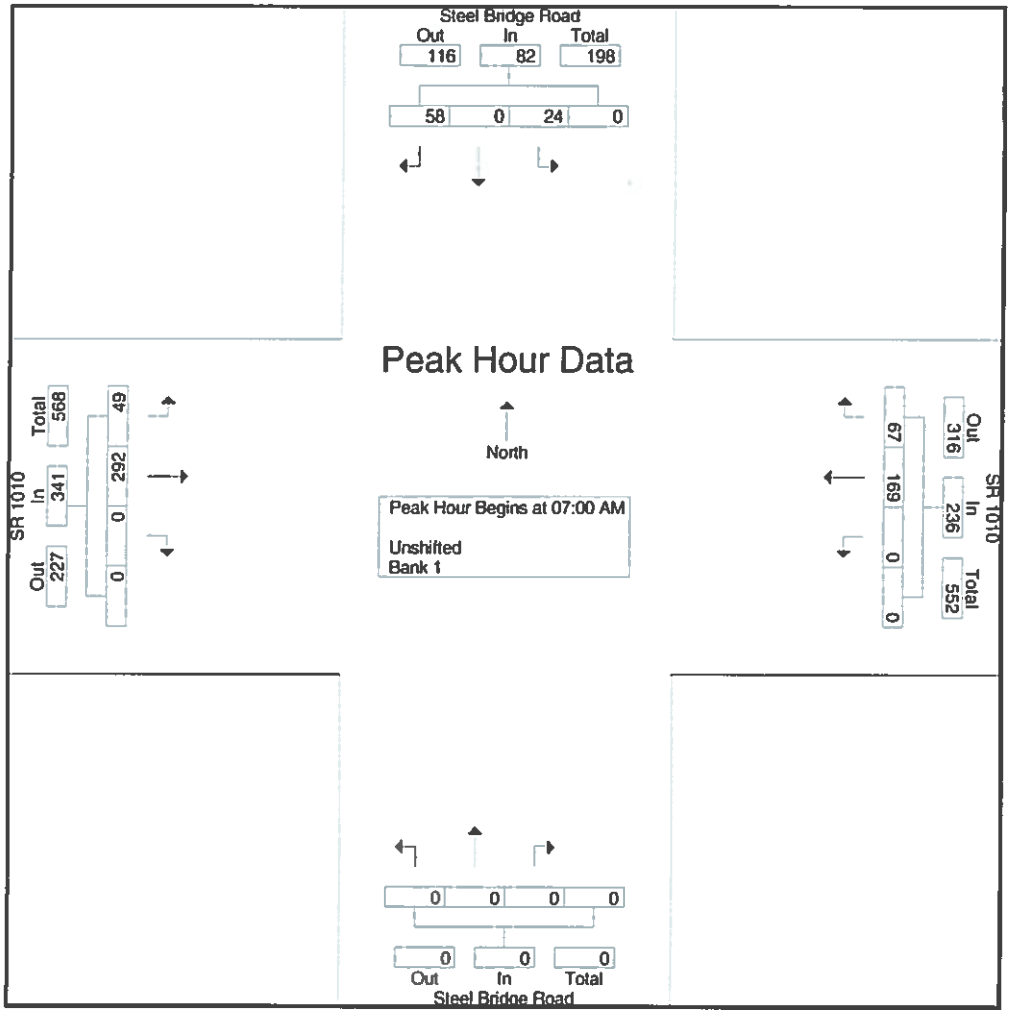

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

Jones Tract Subdivision
SR 1010, Johnston County,North Carolina
Steel Bridge Road & SR 1010

File Name : count 6
Site Code : 00033333
Start Date : 9/10/2015
Page No : 7

	Steel Bridge Road					SR 1010					Steel Bridge Road					SR 1010					
Start Time					App. Total					App. Total					App. Total					App. Total	Int. Total
Peak Hour Analysis From 12:00 PM to 05:45 PM - Peak 1 of 1																					
Peak Hour for Entire Intersection Begins at 05:00 PM																					
05:00 PM	12	0	11	0	23	1	65	7	0	73	0	0	0	0	0	12	63	0	0	75	171
05:15 PM	21	0	15	0	36	0	102	12	0	114	0	0	0	0	0	9	49	0	0	58	208
05:30 PM	10	0	18	0	28	0	75	9	0	84	0	0	0	0	0	10	51	0	0	61	173
05:45 PM	10	0	30	0	40	0	57	6	1	64	0	0	0	0	0	16	42	0	0	58	162
Total Volume	53	0	74	0	127	1	299	34	1	335	0	0	0	0	0	47	205	0	0	252	714
% App. Total	41.7	0	58.3	0		0.3	89.3	10.1	0.3		0	0	0	0		18.7	81.3	0	0		
PHF	.631	.000	.617	.000	.794	.250	.733	.708	.250	.735	.000	.000	.000	.000	.000	.734	.813	.000	.000	.840	.858

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

Jones Tract Subdivision
SR 1010, Johnston County,North Carolina
Steel Bridge Road & SR 1010

File Name : count 6
Site Code : 00033333
Start Date : 9/10/2015
Page No : 8

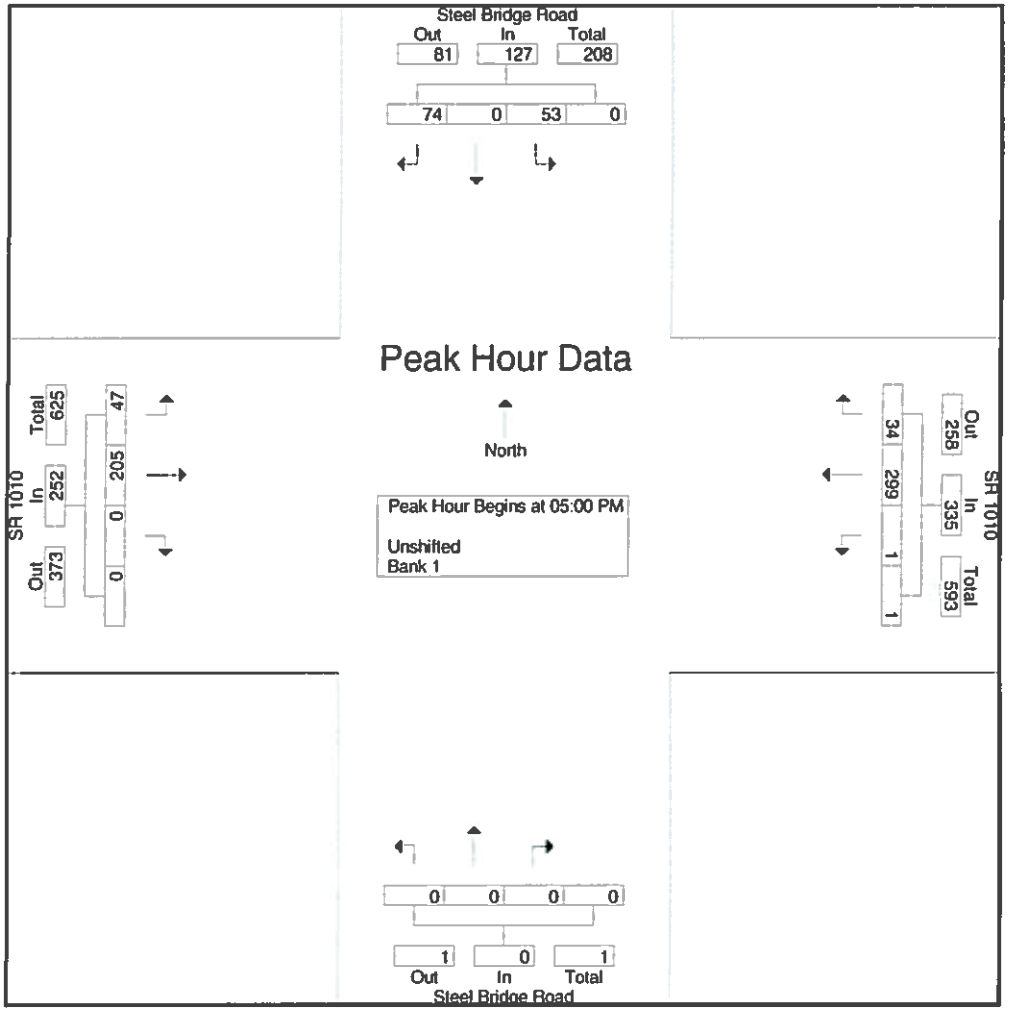

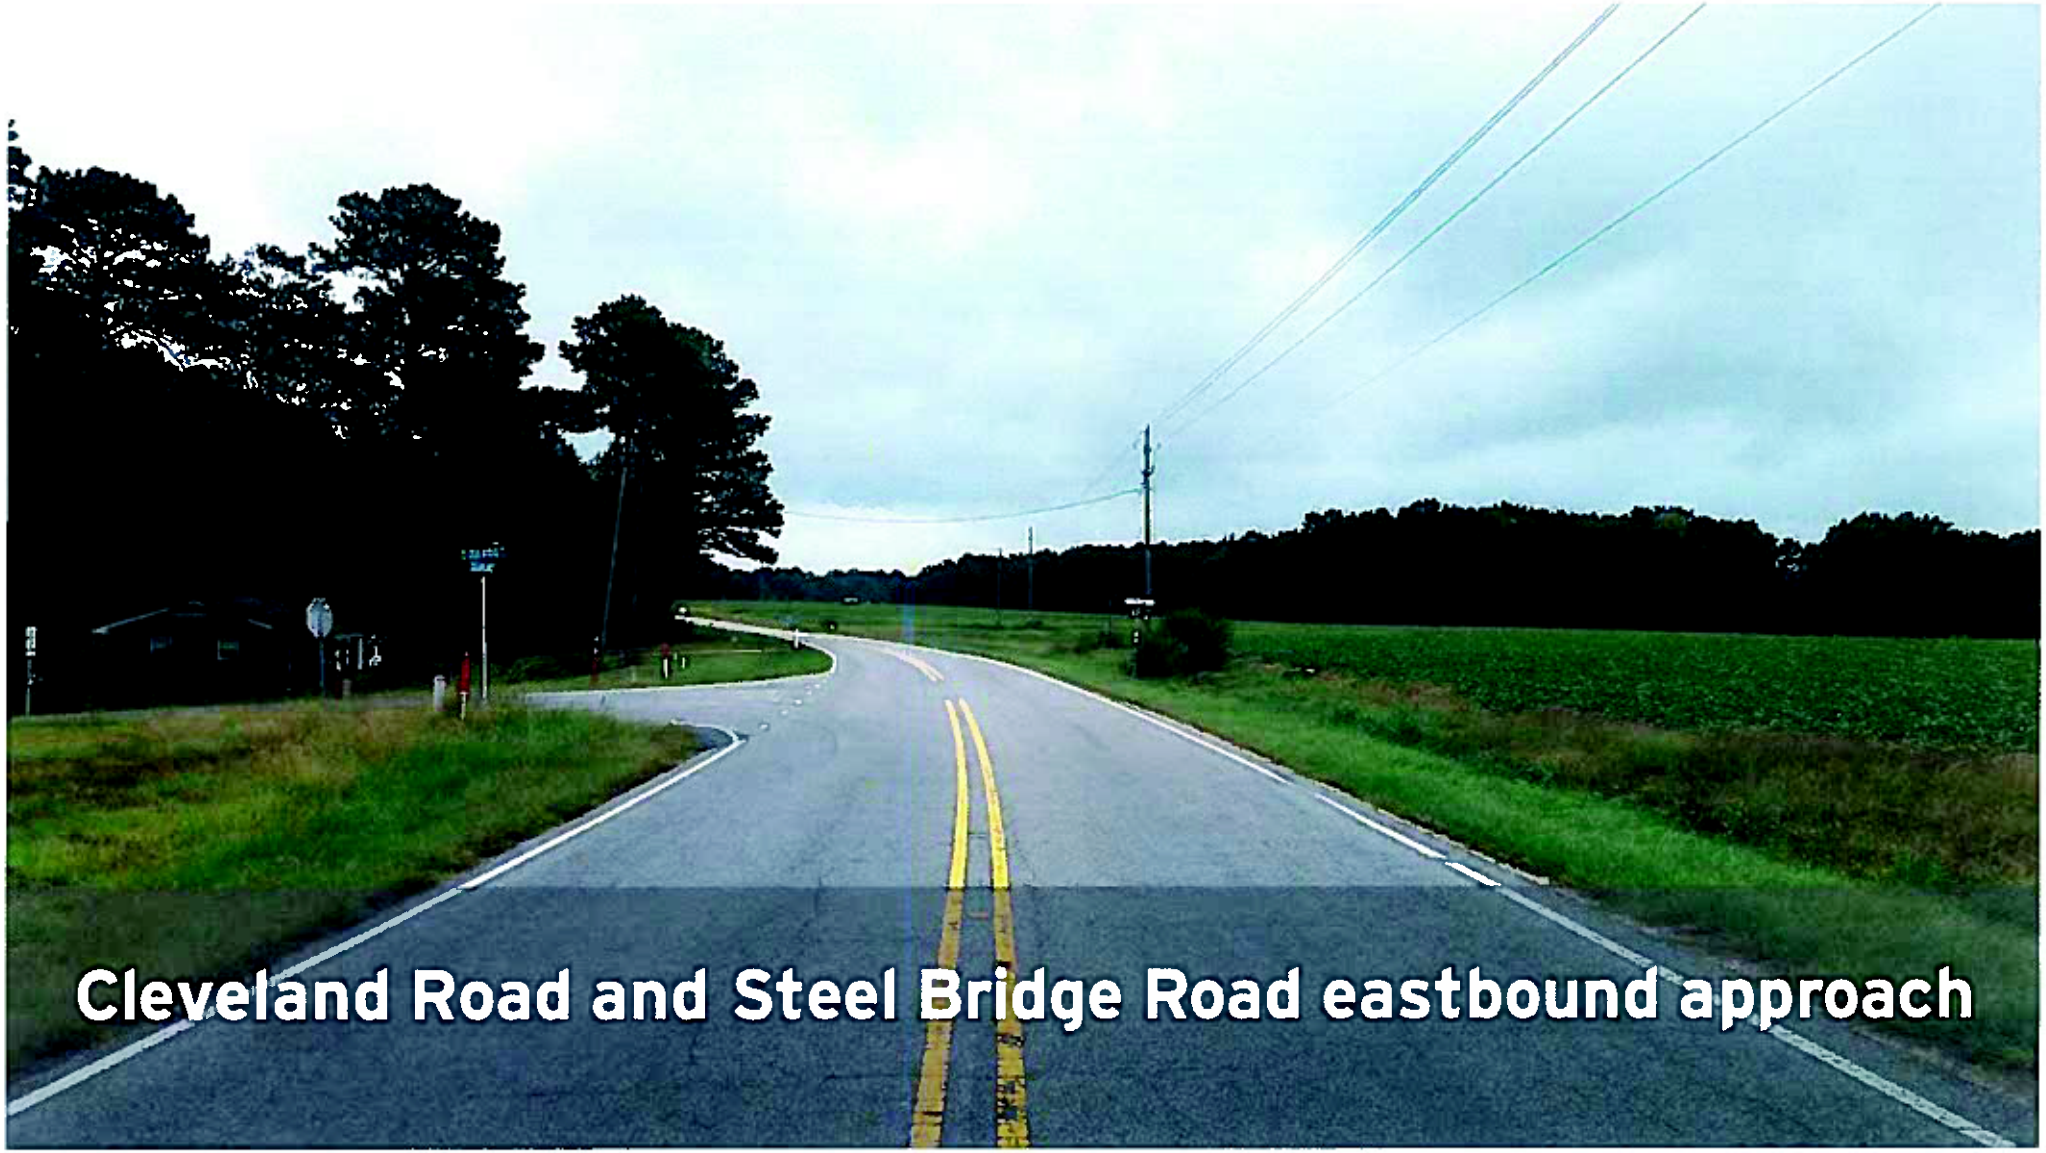
Cleveland Road and Steel Bridge Road eastbound approach

Cleveland Road and Steel Bridge Road westbound approach

Cleveland Road and Steel Bridge Road southbound approach
