Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

River Oakes Mixed Use Subdivision
NC 42, Johnston County,North Carolina
NC 42 & Govement Rosd

File Name : NC 40 - Govement Rd
Site Code : 00000006
Start Date : 5/19/2015
Page No : 1

Groups Printed- Unshifted - Bank 1

						NC 42					Govement Rd.					NC 42					
Start Time					App. Total					App. Total					App. Total					App. Total	Int. Total
07:00 AM	0	0	0	0	0	10	125	0	0	135	47	0	53	0	100	0	155	4	0	159	394
07:15 AM	0	0	0	0	0	13	117	0	0	130	36	0	54	0	90	0	166	10	0	176	396
07:30 AM	0	0	0	0	0	10	140	0	0	150	34	0	54	0	88	0	181	5	0	186	424
07:45 AM	1	0	1	0	2	7	119	0	0	126	42	0	33	0	75	0	188	6	0	194	397
Total	1	0	1	0	2	40	501	0	0	541	159	0	194	0	353	0	690	25	0	715	1611
08:00 AM	0	0	0	0	0	6	117	0	0	123	18	0	39	0	57	0	156	5	0	161	341
08:15 AM	0	0	0	0	0	5	128	0	0	133	18	0	34	0	52	0	177	6	0	183	368
08:30 AM	0	0	0	0	0	11	151	0	0	162	22	0	26	0	48	0	139	10	0	149	359
08:45 AM	0	0	0	0	0	11	145	0	0	156	17	0	22	0	39	0	185	9	0	194	389
Total	0	0	0	0	0	33	541	0	0	574	75	0	121	0	196	0	657	30	0	687	1457
*** BREAK ***																					
04:00 PM	0	0	0	0	0	30	170	0	0	200	14	0	19	0	33	0	179	16	0	195	428
04:15 PM	0	0	0	0	0	34	180	0	0	214	15	0	11	0	26	0	140	28	0	168	408
04:30 PM	0	0	0	0	0	37	205	0	0	242	17	0	23	0	40	0	154	26	0	180	462
04:45 PM	0	0	0	0	0	42	222	0	0	264	14	0	10	0	24	0	134	33	0	167	455
Total	0	0	0	0	0	143	777	0	0	920	60	0	63	0	123	0	607	103	0	710	1753
05:00 PM	0	0	0	0	0	41	196	0	0	237	18	0	22	0	40	0	163	37	0	200	477
05:15 PM	0	0	0	0	0	51	201	0	0	252	15	0	22	0	37	0	159	29	0	188	477
05:30 PM	0	0	0	0	0	51	200	0	0	251	10	0	20	0	30	0	157	22	0	179	460
05:45 PM	0	0	0	0	0	56	192	0	0	248	22	0	18	0	40	0	171	23	0	194	482
Total	0	0	0	0	0	199	789	0	0	988	65	0	82	0	147	0	650	111	0	761	1896
Grand Total	1	0	1	0	2	415	2608	0	0	3023	359	0	460	0	819	0	2604	269	0	2873	6717
Apprch %	50	0	50	0		13.7	86.3	0	0		43.8	0	56.2	0		0	90.6	9.4	0		
Total %	0	0	0	0	0	6.2	38.8	0	0	45	5.3	0	6.8	0	12.2	0	38.8	4	0	42.8	
Unshifted	1	0	1	0	2	415	2608	0	0	3023	359	0	460	0	819	0	2604	269	0	2873	6717
% Unshifted	100	0	100	0	100	100	100	0	0	100	100	0	100	0	100	0	100	100	0	100	100
Bank 1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
% Bank 1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

River Oakes Mixed Use Subdivision
NC 42, Johnston County,North Carolina
NC 42 & Govement Rosd

File Name : NC 40 - Govement Rd
Site Code : 00000006
Start Date : 5/19/2015
Page No : 2

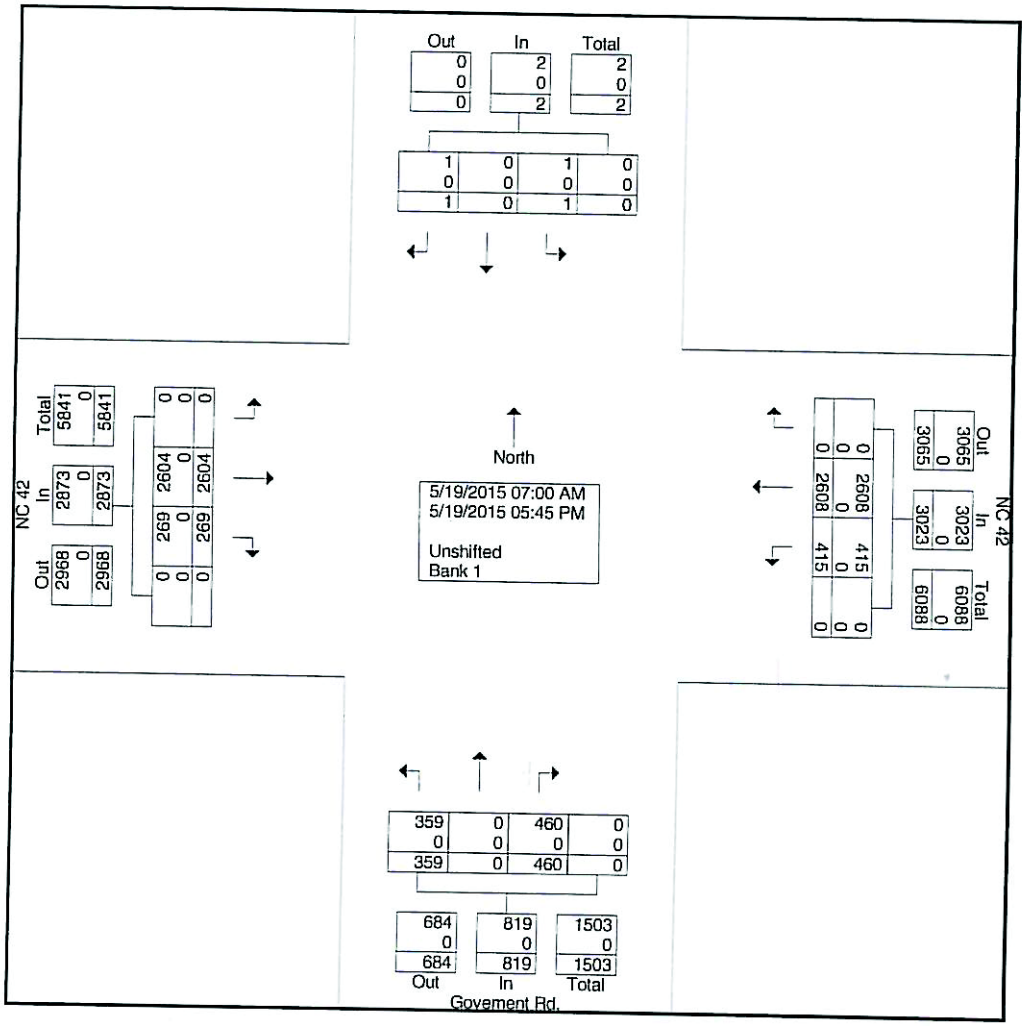

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

River Oakes Mixed Use Subdivision
NC 42, Johnston County,North Carolina
NC 42 & Govement Rosd

File Name : NC 40 - Govement Rd
Site Code : 00000006
Start Date : 5/19/2015
Page No : 4

						NC 42					Govement Rd.					NC 42					
Start Time					App. Total					App. Total					App. Total					App. Total	Int. Total
Peak Hour Analysis From 07:00 AM to 11:45 AM - Peak 1 of 1																					
Peak Hour for Entire Intersection Begins at 07:00 AM																					
07:00 AM	0	0	0	0	0	10	125	0	0	135	**47**	0	53	0	**100**	0	155	4	0	159	394
07:15 AM	0	0	0	0	0	**13**	117	0	0	130	36	0	**54**	0	90	0	166	**10**	0	176	396
07:30 AM	0	0	0	0	0	10	**140**	0	0	**150**	34	0	54	0	88	0	181	5	0	186	**424**
07:45 AM	**1**	0	**1**	0	**2**	7	119	0	0	126	42	0	33	0	75	0	**188**	6	0	**194**	397
Total Volume	1	0	1	0	2	40	501	0	0	541	159	0	194	0	353	0	690	25	0	715	1611
% App. Total	50	0	50	0		7.4	92.6	0	0		45	0	55	0		0	96.5	3.5	0		
PHF	.250	.000	.250	.000	.250	.769	.895	.000	.000	.902	.846	.000	.898	.000	.883	.000	.918	.625	.000	.921	.950

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

River Oakes Mixed Use Subdivision
NC 42, Johnston County,North Carolina
NC 42 & Govement Rosd

File Name : NC 40 - Govement Rd
Site Code : 00000006
Start Date : 5/19/2015
Page No : 5

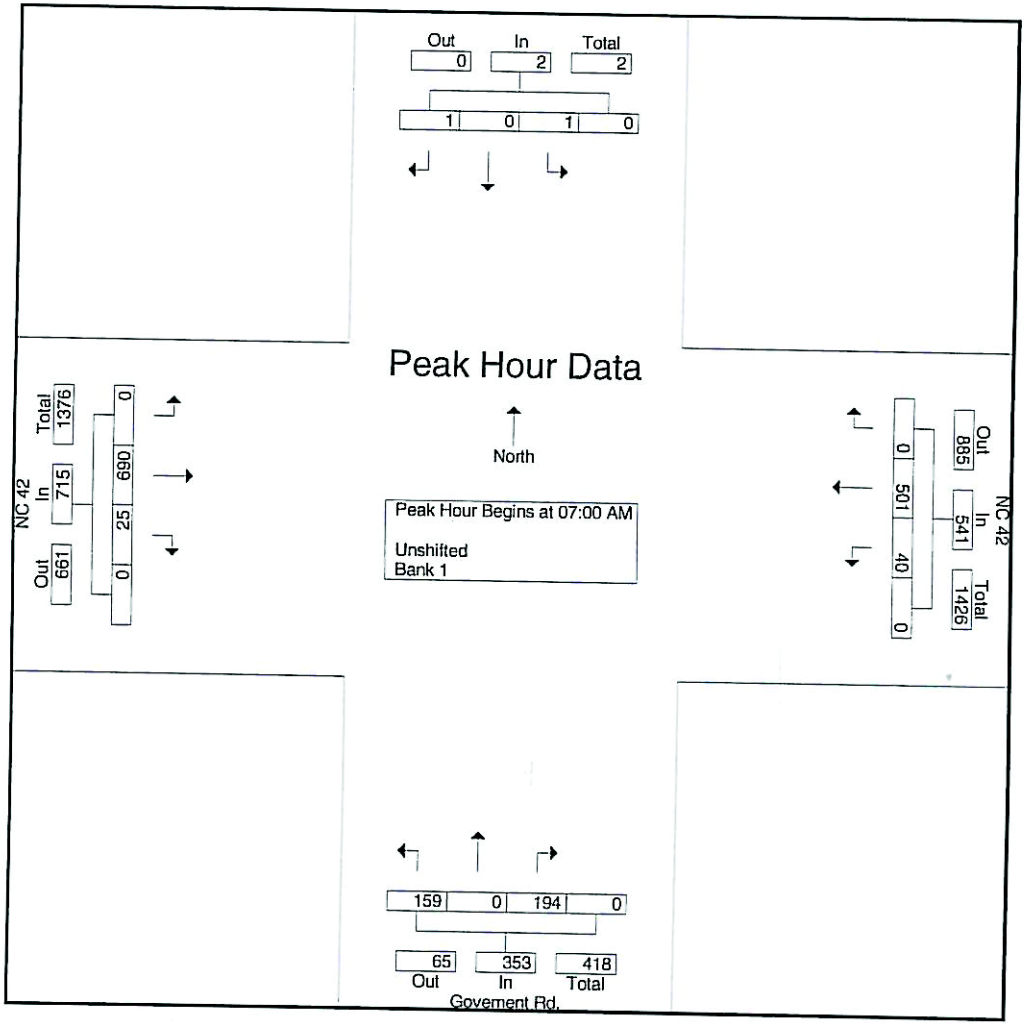

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

River Oakes Mixed Use Subdivision
NC 42, Johnston County,North Carolina
NC 42 & Govement Rosd

File Name : NC 40 - Govement Rd
Site Code : 00000006
Start Date : 5/19/2015
Page No : 7

						NC 42					Govement Rd.					NC 42					
Start Time					App. Total					App. Total					App. Total					App. Total	Int. Total
Peak Hour Analysis From 12:00 PM to 05:45 PM - Peak 1 of 1																					
Peak Hour for Entire Intersection Begins at 05:00 PM																					
05:00 PM	0	0	0	0	0	41	196	0	0	237	18	0	**22**	0	**40**	0	163	**37**	0	**200**	477
05:15 PM	0	0	0	0	0	51	**201**	0	0	**252**	15	0	22	0	37	0	159	29	0	188	477
05:30 PM	0	0	0	0	0	51	200	0	0	251	10	0	20	0	30	0	157	22	0	179	460
05:45 PM	0	0	0	0	0	**56**	192	0	0	248	**22**	0	18	0	40	0	**171**	23	0	194	**482**
Total Volume	0	0	0	0	0	199	789	0	0	988	65	0	82	0	147	0	650	111	0	761	1896
% App. Total	0	0	0	0		20.1	79.9	0	0		44.2	0	55.8	0		0	85.4	14.6	0		
PHF	.000	.000	.000	.000	.000	.888	.981	.000	.000	.980	.739	.000	.932	.000	.919	.000	.950	.750	.000	.951	.983

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

River Oakes Mixed Use Subdivision
NC 42, Johnston County,North Carolina
NC 42 & Govement Rosd

File Name : NC 40 - Govement Rd
Site Code : 00000006
Start Date : 5/19/2015
Page No : 8

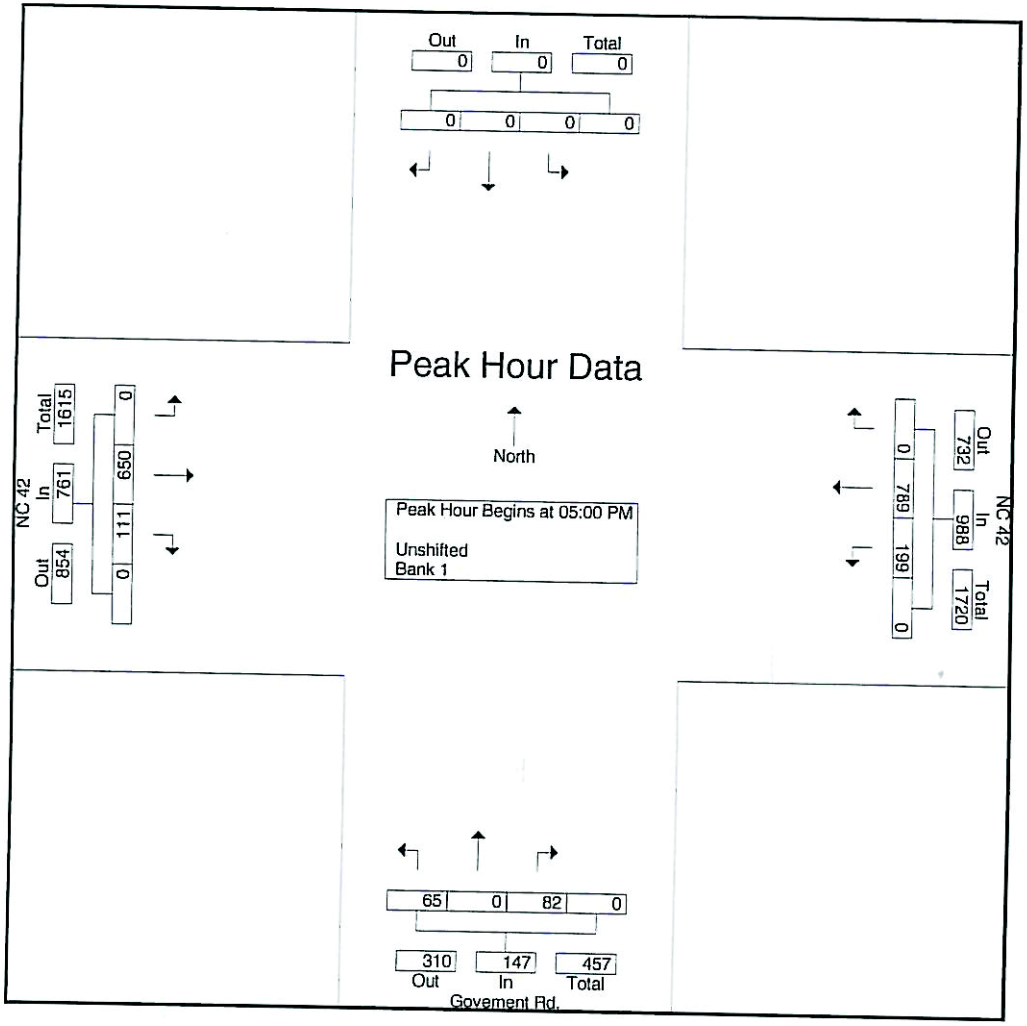

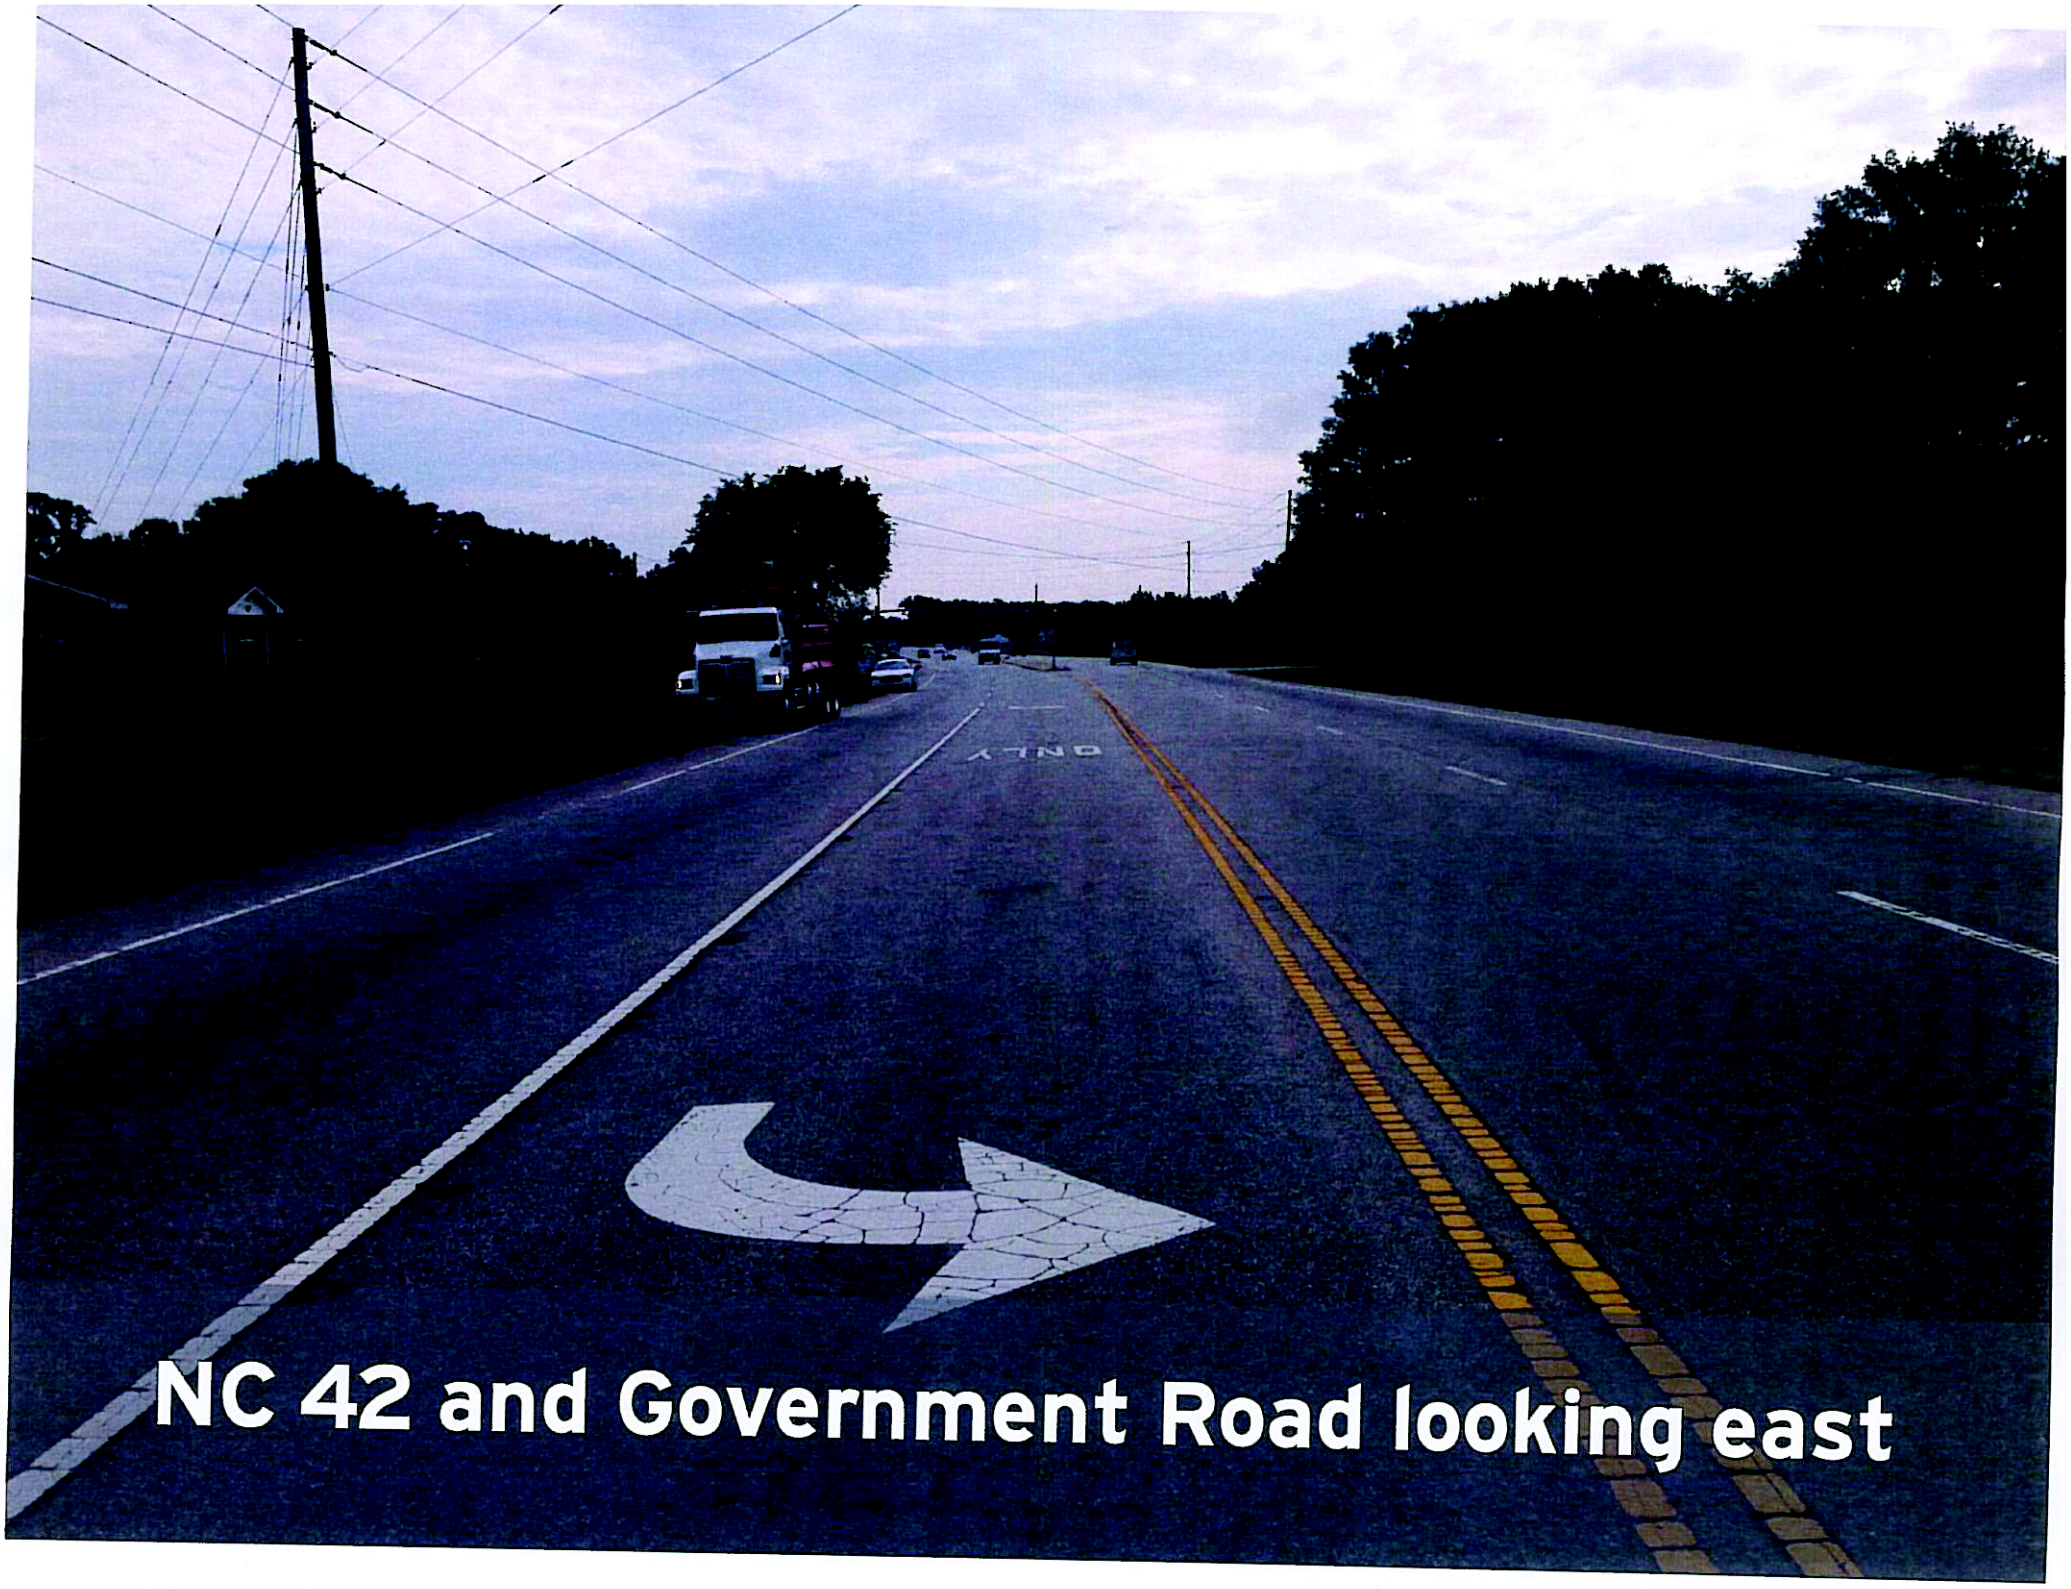
NC 42 and Government Road looking east

NC 42 and Government Road looking west

NC 42 and Government Road looking north
