Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

Portofino Subdivision, Wilders Township, Johnston County

File Name : PORTOFINO WEEK OF 9-22-14 - 5
Site Code : 00000003
Start Date : 9/18/2014
Page No : 1

Groups Printed- Unshifted - Bank 1

						NC 42					Portofino Dr.I					NC 42					
Start Time					App. Total					App. Total					App. Total					App. Total	Int. Total
07:00 AM	0	0	0	0	0	6	124	3	0	133	5	0	3	0	8	0	70	3	0	73	214
07:15 AM	0	0	0	0	0	2	116	0	0	118	3	0	5	0	8	0	89	0	0	89	215
07:30 AM	0	0	0	0	0	2	133	0	0	135	3	0	5	0	8	0	93	2	0	95	238
07:45 AM	0	0	0	0	0	7	143	0	0	150	2	0	4	0	6	0	83	8	0	91	247
Total	0	0	0	0	0	17	516	3	0	536	13	0	17	0	30	0	335	13	0	348	914
08:00 AM	0	0	0	0	0	4	113	0	0	117	6	0	4	0	10	0	60	4	0	64	191
08:15 AM	0	0	0	0	0	6	116	0	0	122	4	0	11	0	15	0	80	5	0	85	222
08:30 AM	0	0	0	0	0	5	115	0	0	120	4	0	15	0	19	0	70	2	0	72	211
08:45 AM	0	0	0	0	0	10	142	0	0	152	3	0	6	0	9	0	79	3	0	82	243
Total	0	0	0	0	0	25	486	0	0	511	17	0	36	0	53	0	289	14	0	303	867
Grand Total	0	0	0	0	0	42	1002	3	0	1047	30	0	53	0	83	0	624	27	0	651	1781
Apprch %	0	0	0	0		4	95.7	0.3	0		36.1	0	63.9	0		0	95.9	4.1	0		
Total %	0	0	0	0	0	2.4	56.3	0.2	0	58.8	1.7	0	3	0	4.7	0	35	1.5	0	36.6	
Unshifted	0	0	0	0	0	42	1002	3	0	1047	30	0	53	0	83	0	624	27	0	651	1781
% Unshifted	0	0	0	0	0	100	100	100	0	100	100	0	100	0	100	0	100	100	0	100	100
Bank 1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
% Bank 1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

Portofino Subdivision, Wilders Township, Johnston County

File Name : PORTOFINO WEEK OF 9-22-14 - 5
Site Code : 00000003
Start Date : 9/18/2014
Page No : 2

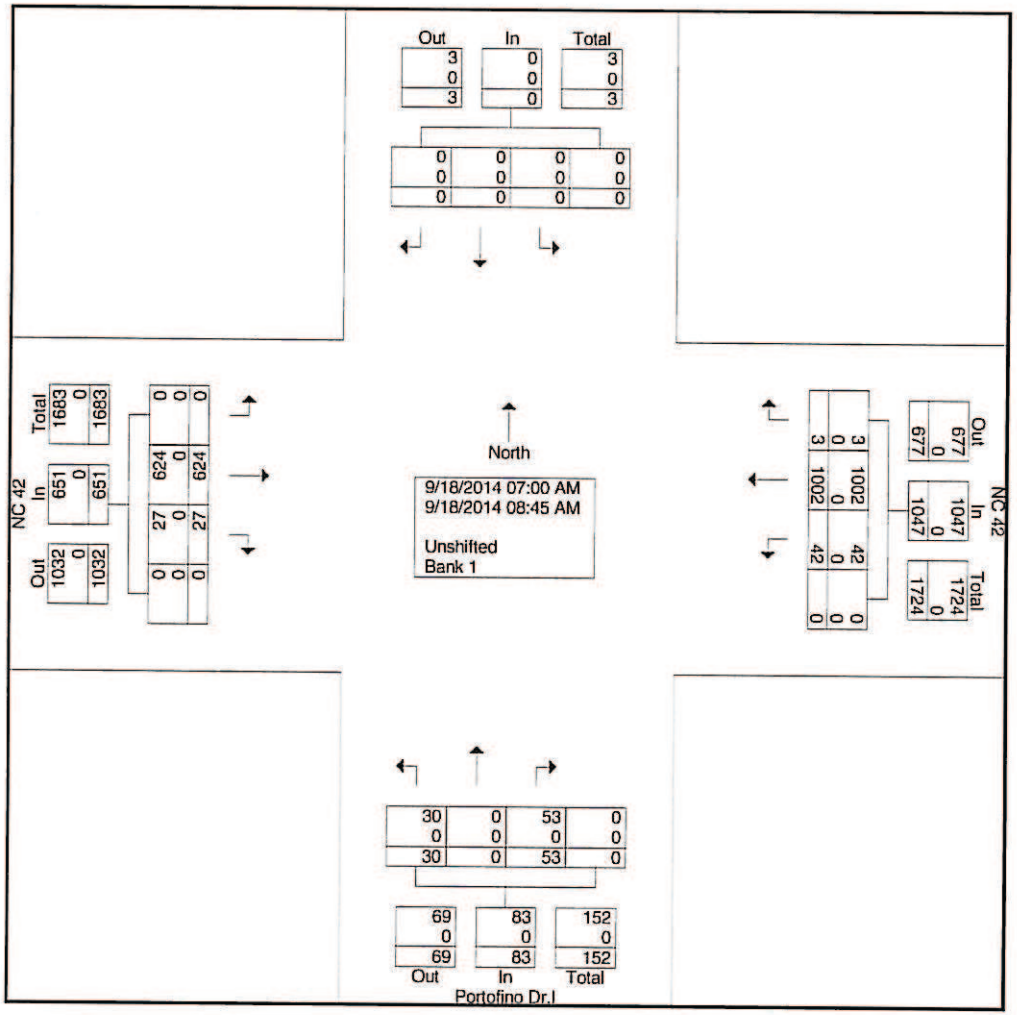

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

Portofino Subdivision, Wilders Township, Johnston County

File Name : PORTOFINO WEEK OF 9-22-14 - 5
Site Code : 00000003
Start Date : 9/18/2014
Page No : 4

						NC 42					Portofino Dr.I					NC 42					
Start Time					App. Total					App. Total					App. Total					App. Total	Int. Total
Peak Hour Analysis From 07:00 AM to 08:45 AM - Peak 1 of 1																					
Peak Hour for Each Approach Begins at:																					
	07:00 AM					07:00 AM					08:00 AM					07:00 AM					
+0 mins.	0	0	0	0	0	6	124	3	0	133	6	0	4	0	10	0	70	3	0	73	
+15 mins.	0	0	0	0	0	2	116	0	0	118	4	0	11	0	15	0	89	0	0	89	
+30 mins.	0	0	0	0	0	2	133	0	0	135	4	0	15	0	19	0	93	2	0	95	
+45 mins.	0	0	0	0	0	7	143	0	0	150	3	0	6	0	9	0	83	8	0	91	
Total Volume	0	0	0	0	0	17	516	3	0	536	17	0	36	0	53	0	335	13	0	348	
% App. Total	0	0	0	0		3.2	96.3	0.6	0		32.1	0	67.9	0		0	96.3	3.7	0		
PHF	.000	.000	.000	.000	.000	.607	.902	.250	.000	.893	.708	.000	.600	.000	.697	.000	.901	.406	.000	.916	

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

Portofino Subdivision, Wilders Township, Johnston County

File Name : PORTOFINO WEEK OF 9-22-14 - 5
Site Code : 00000003
Start Date : 9/18/2014
Page No : 5

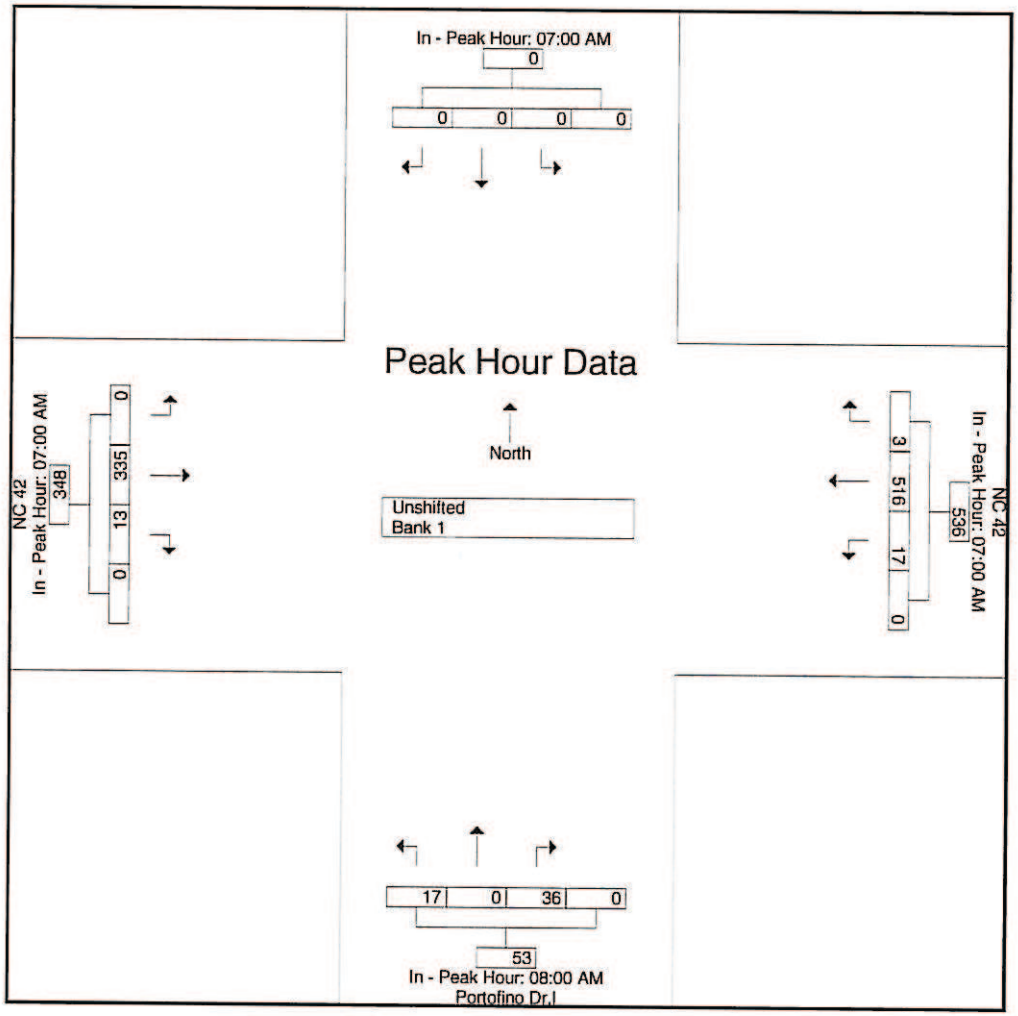

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

Portofino Subdivision, Wilders Township, Johnston County

File Name : PORTOFINO WEEK OF 9-22-14 - 6
Site Code : 00000003
Start Date : 9/18/2014
Page No : 1

Groups Printed- Unshifted - Bank 1

						NC 42					Portofino Drive					NC 42					
Start Time					App. Total					App. Total					App. Total					App. Total	Int. Total
04:00 PM	0	0	0	0	0	10	86	0	0	96	5	0	8	0	13	0	104	1	0	105	214
04:15 PM	0	0	0	0	0	12	83	0	0	95	6	0	6	0	12	0	142	6	0	148	255
04:30 PM	0	0	0	0	0	5	105	0	0	110	6	0	3	0	9	0	123	6	0	129	248
04:45 PM	0	0	0	0	0	7	107	0	0	114	4	0	5	0	9	0	143	9	0	152	275
Total	0	0	0	0	0	34	381	0	0	415	21	0	22	0	43	0	512	22	0	534	992
05:00 PM	0	0	0	0	0	6	105	0	0	111	13	0	3	0	16	0	149	4	0	153	280
05:15 PM	0	0	0	0	0	9	123	0	0	132	0	0	4	0	4	0	167	3	0	170	306
05:30 PM	0	0	0	0	0	6	145	0	0	151	4	0	8	0	12	0	154	8	0	162	325
05:45 PM	0	0	0	0	0	8	134	0	0	142	5	0	3	0	8	0	144	6	0	150	300
Total	0	0	0	0	0	29	507	0	0	536	22	0	18	0	40	0	614	21	0	635	1211
Grand Total	0	0	0	0	0	63	888	0	0	951	43	0	40	0	83	0	1126	43	0	1169	2203
Apprch %	0	0	0	0		6.6	93.4	0	0		51.8	0	48.2	0		0	96.3	3.7	0		
Total %	0	0	0	0	0	2.9	40.3	0	0	43.2	2	0	1.8	0	3.8	0	51.1	2	0	53.1	
Unshifted	0	0	0	0	0	63	888	0	0	951	43	0	40	0	83	0	1126	43	0	1169	2203
% Unshifted	0	0	0	0	0	100	100	0	0	100	100	0	100	0	100	0	100	100	0	100	100
Bank 1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
% Bank 1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

Portofino Subdivision, Wilders Township, Johnston County

File Name : PORTOFINO WEEK OF 9-22-14 - 6
Site Code : 00000003
Start Date : 9/18/2014
Page No : 2

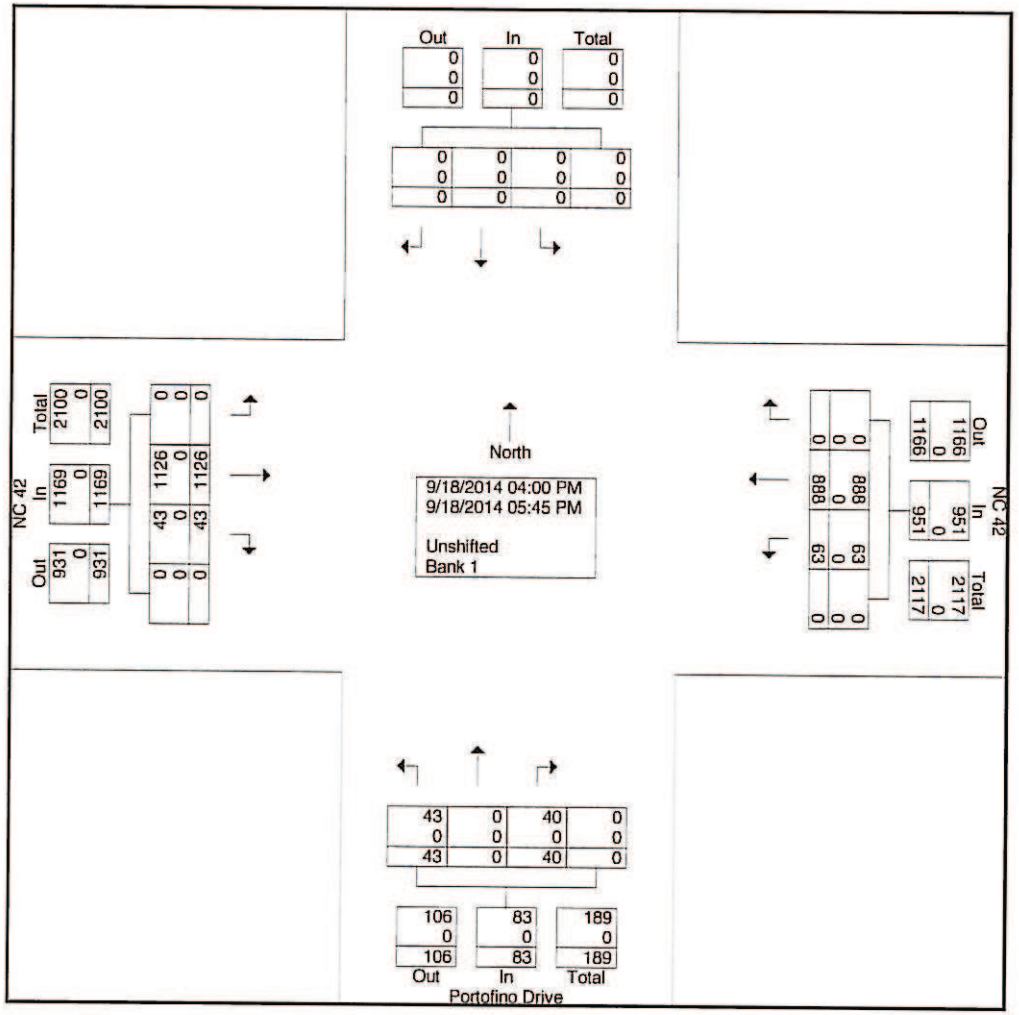

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

Portofino Subdivision, Wilders Township, Johnston County

File Name : PORTOFINO WEEK OF 9-22-14 - 6
Site Code : 00000003
Start Date : 9/18/2014
Page No : 4

						NC 42					Portofino Drive					NC 42					
Start Time					App. Total					App. Total					App. Total					App. Total	Int. Total
Peak Hour Analysis From 04:00 PM to 05:45 PM - Peak 1 of 1																					
Peak Hour for Each Approach Begins at:																					
	04:00 PM					05:00 PM					04:15 PM					04:45 PM					
+0 mins.	0	0	0	0	0	6	105	0	0	111	6	0	6	0	12	0	143	9	0	152	
+15 mins.	0	0	0	0	0	9	123	0	0	132	6	0	3	0	9	0	149	4	0	153	
+30 mins.	0	0	0	0	0	6	145	0	0	151	4	0	5	0	9	0	167	3	0	170	
+45 mins.	0	0	0	0	0	8	134	0	0	142	13	0	3	0	16	0	154	8	0	162	
Total Volume	0	0	0	0	0	29	507	0	0	536	29	0	17	0	46	0	613	24	0	637	
% App. Total	0	0	0	0		5.4	94.6	0	0		63	0	37	0		0	96.2	3.8	0		
PHF	.000	.000	.000	.000	.000	.806	.874	.000	.000	.887	.558	.000	.708	.000	.719	.000	.918	.667	.000	.937	

Wetherill Engineering Inc.

559 Jones Frankin Road, Suite 164
Raleigh NC 27606

Portofino Subdivision, Wilders Township, Johnston County

File Name : PORTOFINO WEEK OF 9-22-14 - 6
Site Code : 00000003
Start Date : 9/18/2014
Page No : 5

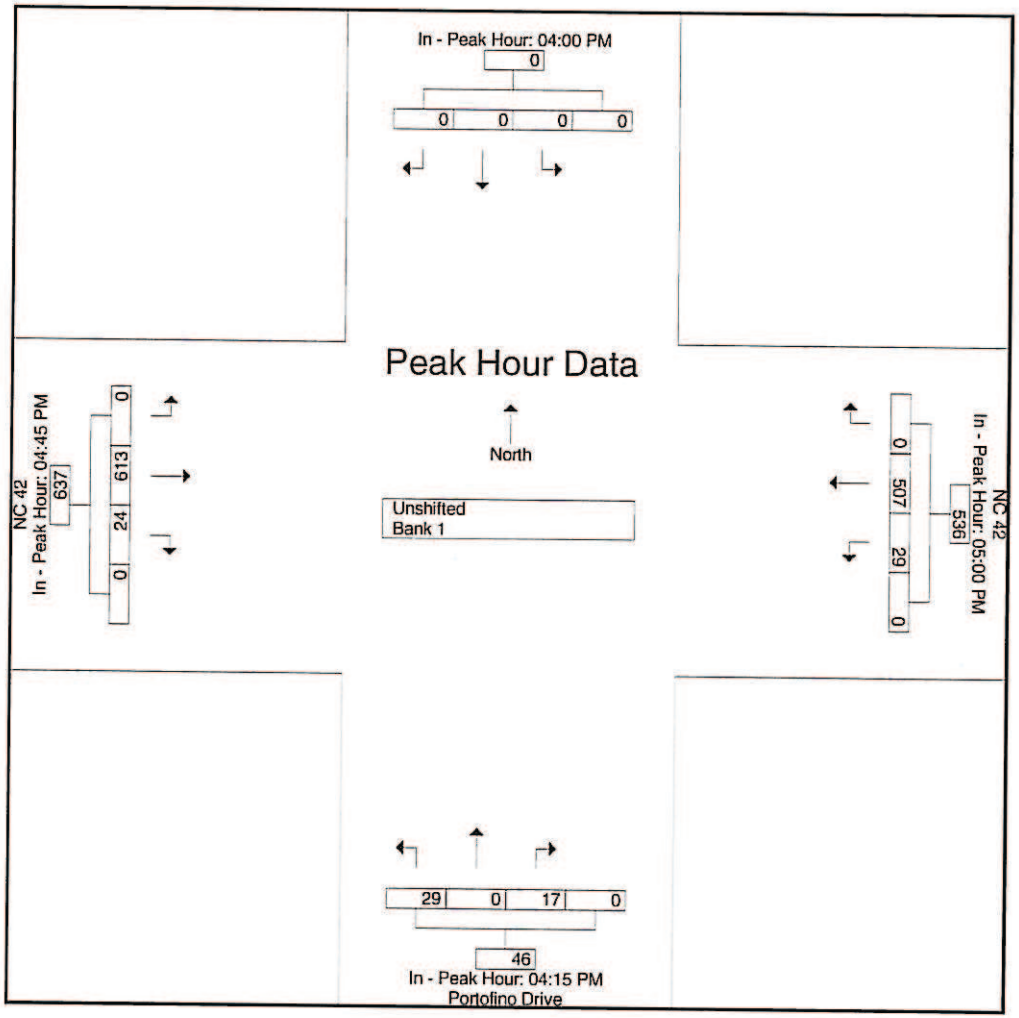

NC 42 eastbound approach to Portofino Drive

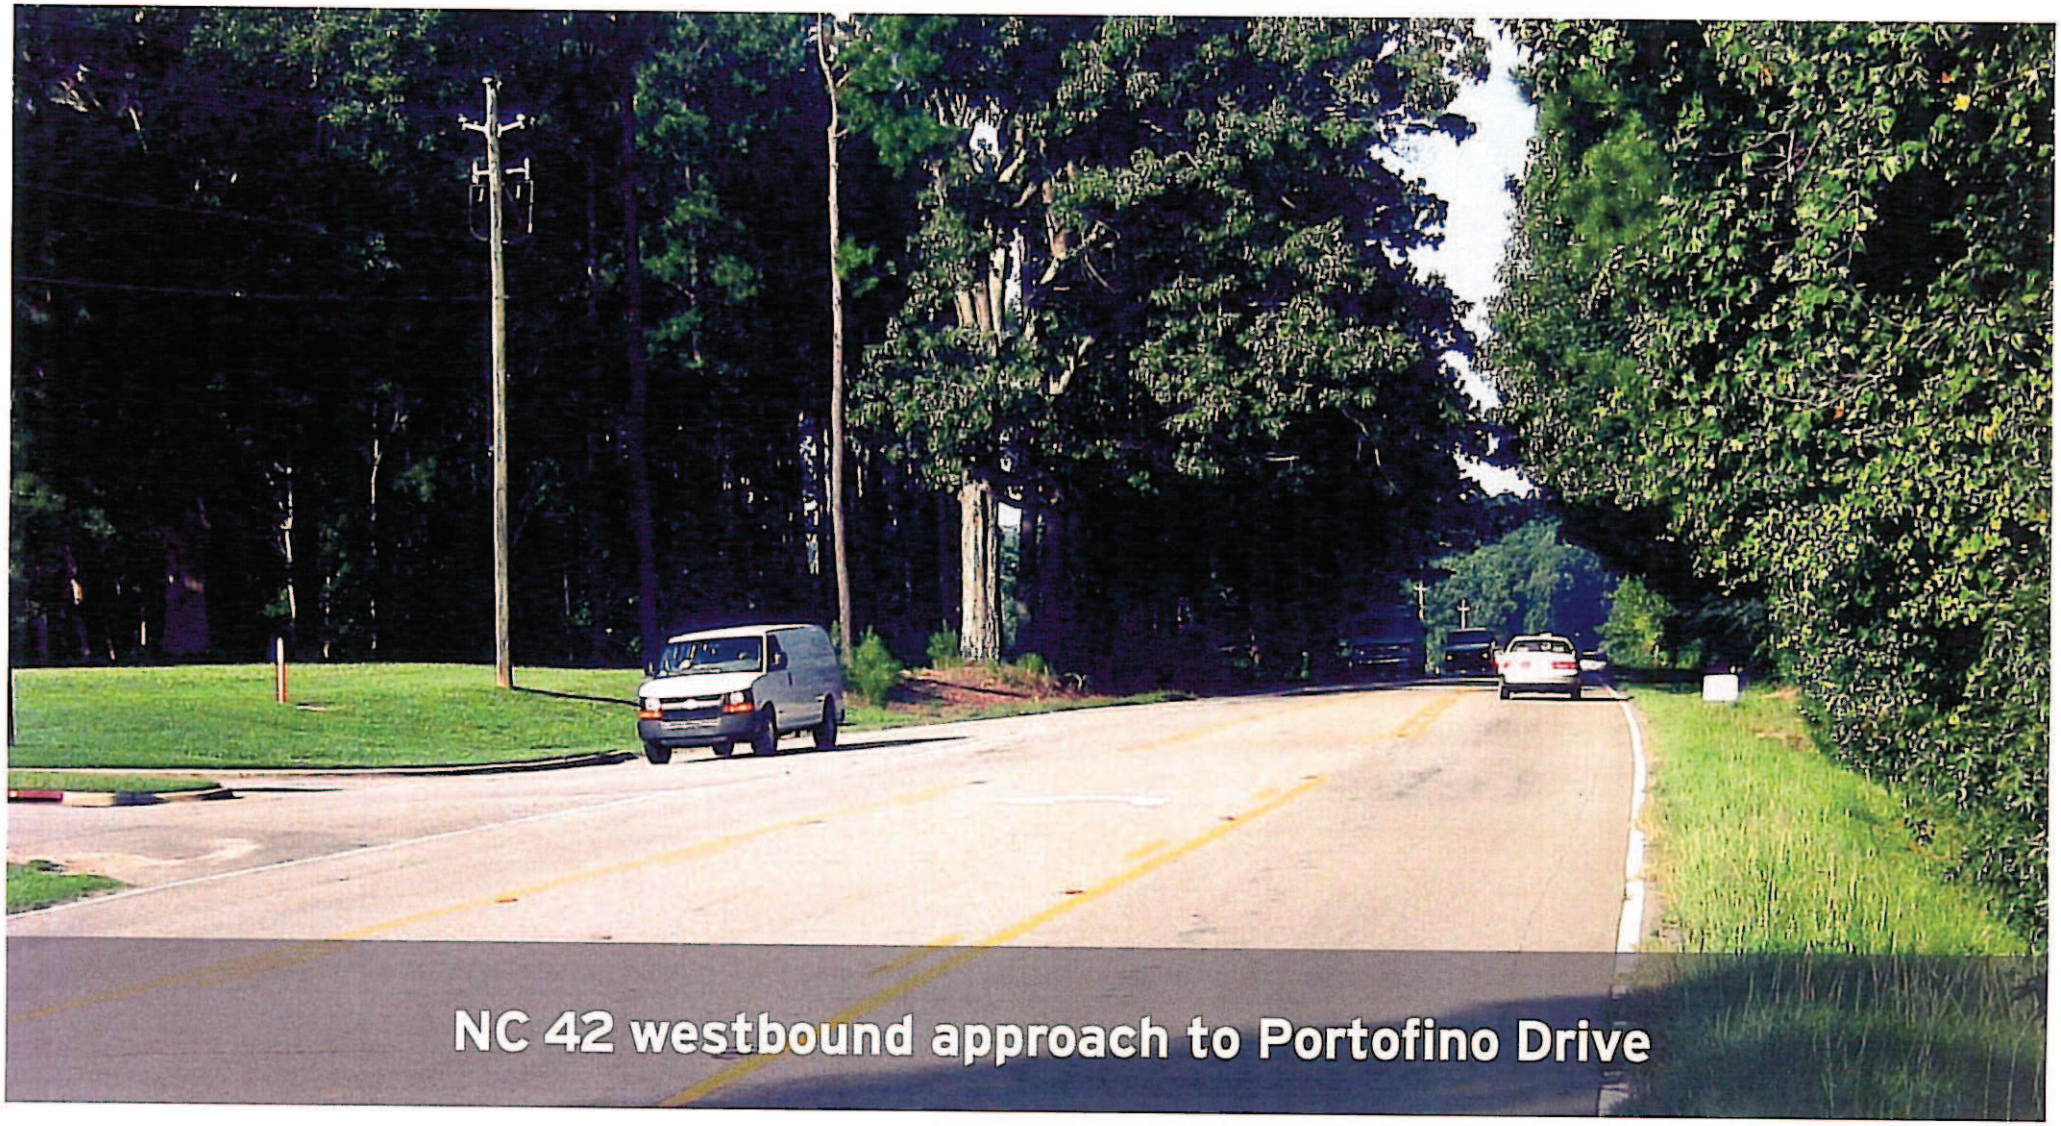

NC 42 westbound approach to Portofino Drive

Portofino Drive northbound approach to NC 42
