

Field Scoping Meetings 2015


THE GOAL:

- 114 Projects to FSM in 6 Months

THE CHALLENGE:

- Twice the number of Projects
- Half the Time
- Transitioning an In-House Process to a Consultant Driven Process

TRI- Managed Bridge Process

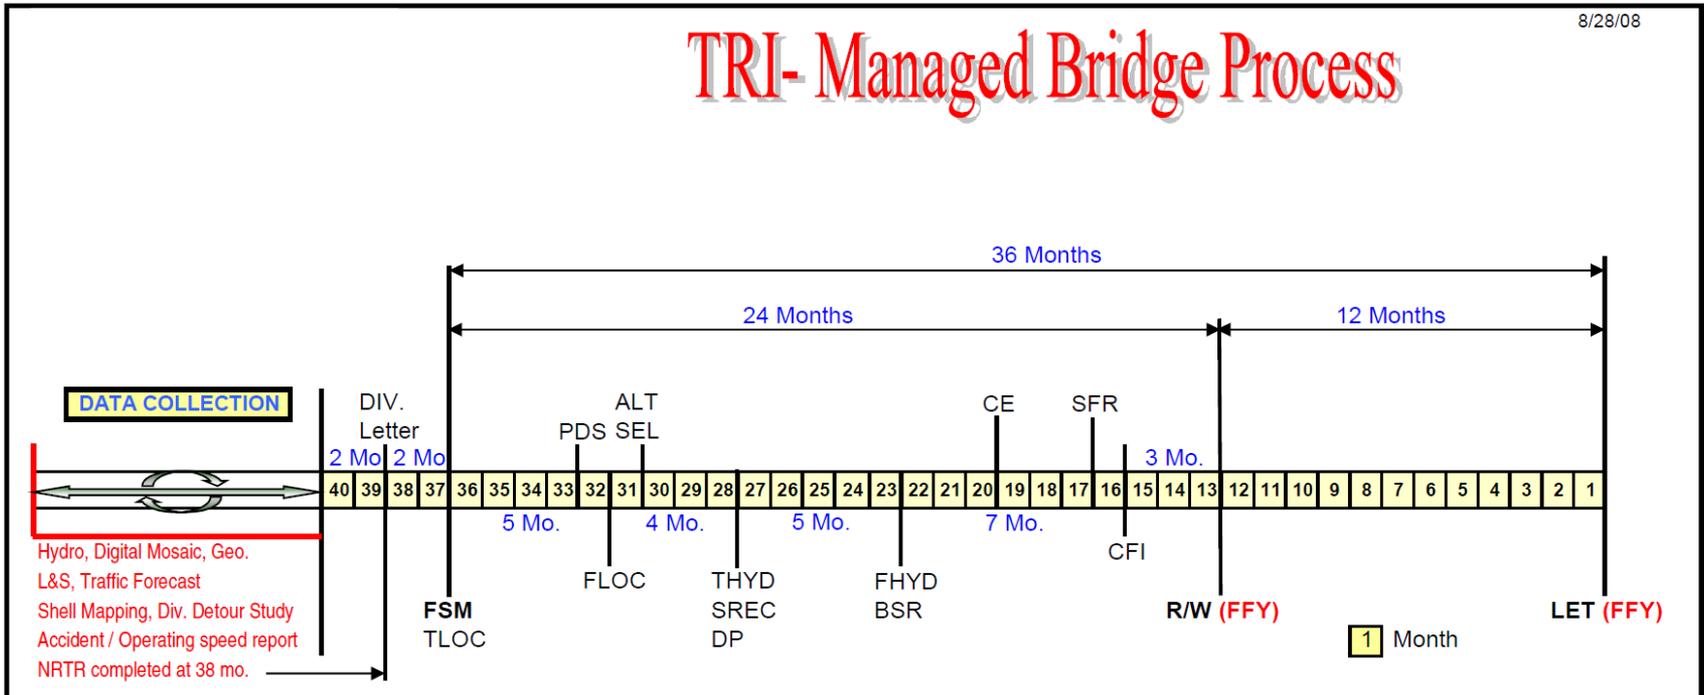

4.5 to 5.5- Years from Funding to Let

Purpose of Field Scoping Meeting as it was designed:

- Division Led Meeting*
- Alternatives Discussion or Decision
- Constructability Discussion
- Consistency in Decision Making
- Efficiency by processing in mass*
- Set Project Schedule

Eastern Region

Week	Week Of	Group #'s	Div	Total Projects	PDEA PE
1	6-Apr	A	1	9	McInnis
2	13-Apr	B,D	2	11	Cox
3	20-Apr	C	2	9	Cox
4	27-Apr	E, F	3	9	Yamamoto
5	4-May	G	3	7	Yamamoto
6	11-May	H, B-4937	4	9	McInnis
7	18-May	I	6	5	Cox

Central Region

Week	Week Of	Group #'s	Div	Total Projects	PDEA PE
1	6-Apr	J, B-4654	5	5	Weaver/ Robinson
2	13-Apr	K, B-5356	7	3	Walls
3	20-Apr	K	8	3	Walls
4	27-Apr	J, B-5148, B-4626	9	4	Weaver/ Robinson
5	4-May				
6	11-May				
7	18-May				

Western Region

Week	Week Of	Group #'s	Div	Total Projects	PDEA PE
1	6-Apr	L, M	10	6	Oberhausen
2	13-Apr	R,S	12	7	Conforti
3	20-Apr	T,U	13	8	Oberhausen
4	27-Apr	V	14	4	Oberhausen
5	4-May	N, O, P, Q	11	18	Kluchar
6	11-May				
7	18-May				

Schedule of Field Scoping Meetings

Example for FSM's of Week 1

Requests:

Schools
 EMS
 Historic Resources Screening
 SOS Internal
 SOS External
 Traffic (if needed)

Due

Line & Grade Drawings
 Final Draft CIA
 FSM Worksheet Filled Distributed

Scope, Negotions & NTP

Natural Systems

.wex files
 NS FSM Checklist

Completed

FSM Minutes
 FSM Worksheets

OCTOBER	NOVEMBER	DECEMBER	JANUARY	FEBRUARY	MARCH	APRIL	MAY	JUNE
---------	----------	----------	---------	----------	-------	-------	-----	------

Training

Due

Draft CIA
 EMS
 Schools
 Division Input
 Architectural Screening Results

Due

Archaeological Screening

Field Trips Complete

FSM Week 1

NRTR Complete

Maps:

Quad Map
 Vicinity Map
 Study Area (aerial)

Notice To Proceed (NTP)

End of Day 2

1. Quad Map
2. Study Area
3. Vicinity Map

End of Week 1 (Requests Sent)

EMS Request Form
Schools Request Form
Historic Resources Screening
 Archaeological
 Architectural
SOS Internal E-mail
SOS External

Due 1 Month from Request

EMS
Schools
Historic Architectural Screening

Due 2 Months from Request

Archaeological Screening

Due 12 Weeks Prior to FSM

First Draft of CIA
Field Trips complete
EMS & Schools Input Received
Division Input Received

Due 8 Weeks prior to FSM

Division Input
Approved .wex files (wetland files)
Final Draft

Due 1 Week prior to FSM


Line and Grade Drawings
FSM Worksheet Filled Out


Deliverables Prior to FSM

What Happens after the FSM?

- 1 week - Completed Minutes and FSM Worksheet
- 1 month – Set remainder of Schedule for Project based on:
 - Remaining Issues to work through
 - Moratoriums
 - Constructability Issues
 - Local Needs – harvest season, local events, school schedule, etc.
- Work toward Alternate Selection if necessary
- Alternate Selection Sets the Design in Motion
 - From Alt Select to Let is 30 months
- Reaching Alternate Selection is critical to keeping the schedule.

TRI- Managed Bridge Process

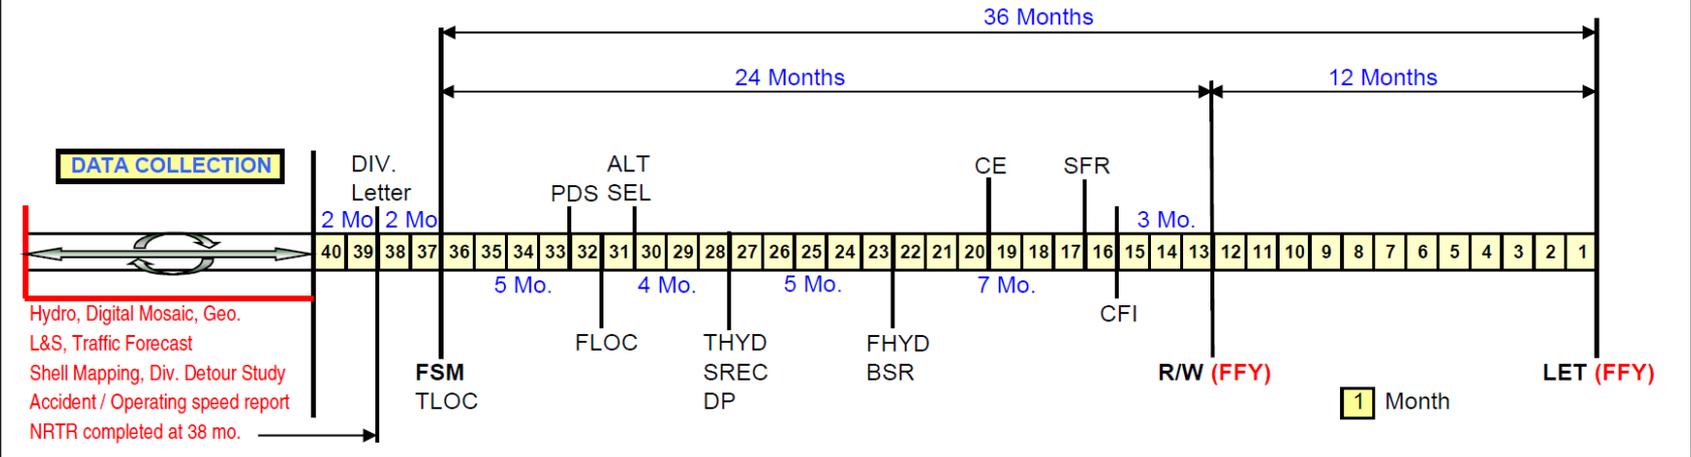



Questions?
