[State Fiscal Year] Project: ITR.RDA093 SMO (STaRS Networks) DO NOT DEL

S	Hi	Description	Duratn	(B)ElSchFi
		SMO (STaRS Networks) DO NO	**503.0 DAY**	
		Data Collection (PLANNING)	11.0 MON	05/28/2021
		Request Digital Mosaic (TMOS)		**07/01/2020**
		PE Funding Approved (PFA)		**07/01/2020**
		Survey Request to Location (TLOC)		**07/01/2020**
		Begin Data Collection (BDC)		**08/03/2020**
		Req. Prel. Hydro Report (REQ_PREHYD)		**08/03/2020**
		Environmental Input Request (EIR)		**09/01/2020**
		Request Traffic Forecast (REQ_TFC)		**09/01/2020**
		Project Scoping Meeting (PSM)		**09/01/2020**
		Receive Digital Mosaic (FMOS)		**11/02/2020**
		Public Meeting (PM)		**12/01/2020**
		Preliminary Hydro Report (PHYD)		**12/01/2020**
		Traffic Forecast Completed (TFC)		**03/01/2021**
		Request Traffic Capacity (REQ_CAP)		**03/01/2021**
		Archaeology Screening (ARCH_SCRN)		**03/29/2021**
		Historic Survey & Elig. (HIST)		**03/29/2021**
		Capacity Analysis (CAPA)		**05/28/2021**
		Natural Resources Technical Report	12.0 MON	08/31/2021
		Delineate Wetlands & Streams (DEL_W		**01/04/2021**
		Biological Conclusion (BIOCL)		**08/31/2021**
		Natural Resources Tech. Report (NRTR)		**08/31/2021**
		Verif. of Wetlands & Streams (VERWET)		**08/31/2021**
		Preliminary Design Development	10.0 MON	03/01/2022
		Plan Sheets from Location (FLOC)		**05/03/2021**
		Prel. Design Est (PD_EST)		**11/01/2021**
		Preliminary Design Submittal (PDS)		**11/01/2021**
		Req GEO Alt Eval (REQ_GEOEVAL		**11/01/2021**
		Req. Hist. Architect Effects (REQ_HAE)		**11/01/2021**
		Request Air & Noise (REQ_A&N)		**11/01/2021**
		GEO Alt Eval (GEOEVAL)		**03/01/2022**
		Human Environment Reports	5.0 MON	04/01/2022
		Historic Architecture Effects (HAE)		**02/02/2022**
		Community Impact Assess. (CIA)		**03/02/2022**
		Indirect & Cumulative Effects (ICE_SCR		**03/02/2022**
		Community Char. Report (CCR)		**03/02/2022**
		Traffic Noise Analysis (TNA)		**04/01/2022**
		Air Quality Analysis (AQ)		**04/01/2022**
		Document Development	3.0 MON	06/30/2022
		CE Approved (CE)		**06/30/2022**
		R/W Plans Development	12.0 MON	10/20/2022
		Preliminary Line & Grade (15% HYD)		**11/22/2021**
		Distribute Plans (DP)		**02/21/2022**
		Req. Final Pav't Design (REQ_PAV'T)		**02/21/2022**
		Prel. Util. Analysis & Routing (PUARR)		**03/21/2022**
		HES LDA INFO (HLDA)		**04/21/2022**
		T+E Species Review-consultation (T&E		**05/20/2022**
		Final Pavement Design (PAVEMENT)		**06/20/2022**
		Location and Design Approval (LADA)		**06/20/2022**
		Traffic Control Plans (TCP)		**06/20/2022**
		Slope Recommendations (SLREC)		**06/20/2022**
		Roadway Foundation Recm'ds (RDY_RE		**06/20/2022**
		Structure Foundation Recm'ds (SFR)		**06/20/2022**
		Construction Estimate (CONST_EST)		**07/20/2022**
		Final PUE's (PUE)		**07/20/2022**
		Utility Estimate (UTL_EST)		**07/20/2022**
		RW Estimate (RW_EST)		**07/20/2022**
		Combined Field Inspection (CFI)		**08/22/2022**
		Util. Analysis & Routing (UARR)		**09/20/2022**
		Traffic Staging Concept (TSC)		**09/21/2022**
		R/W Plans Complete (RPC)		**10/20/2022**
		Hydraulic Design	4.0 MON	06/20/2022
		To Hydraulics (THYD)		**02/21/2022**
		Hydro Recommendations (FHYD)		**06/20/2022**
		Plan & Permit Review	3.0 MON	09/20/2022
		Plan/Permit Consistency Review (PPCR		**08/22/2022**
		Permit Dwgs to Natural Systems (PDNE		**09/20/2022**
		Stormwater Mgm't Plan Complete (SMP		**09/20/2022**
		R/W PIVOT (DO NOT DELETE)		10/21/2022
		R/W Acquisition	11.0 MON	09/20/2023
		R/W Acquisition Begins (R/W)		**10/21/2022**
		R/W Certification (R/WCERT)		**09/20/2023**
		Utility Relocation	11.0 MON	09/20/2023
		Utility Parcel Acquisition (UPA)		**04/21/2023**
		Utility Certification (UC)		**09/20/2023**
		LET PIVOT (DO NOT DELETE)		10/20/2022
		Utility Plans Development	8.0 MON	06/20/2023
		Utility Environ. Permit Dwg (UEP_DWG)		**12/21/2022**
		Utility Agreement Plans (UTI_AGRM'T)		**06/20/2023**
		Environmental Permit Submittals	3.0 MON	01/20/2023
		Submit Individual Permit (SUB_IP)		**10/21/2022**
		Submit NW Permit (SUB_NWP)		**10/21/2022**
		Sub. Riparian Buffer Auth (SUB_BUFAU		**01/20/2023**
		Final Plans Development	10.0 MON	08/18/2023
		Sub. UtiL. Agrm't Package (SUB_UTLAP		**02/21/2023**
		Erosion Control Plans (ECP)		**08/11/2023**
		Cable Routing Plans (CABLE RT_PLN)		**08/11/2023**
		Sig. Design & Elec. Detail (S&E_PLN)		**08/11/2023**
		Final Plans to Design (FPD)		**08/11/2023**
		TCP to Design (TCPD)		**08/11/2023**
		Obtain UtiL. Agrm't Package (UTLAP)		**08/11/2023**
		Utility by Others Plans (UOP)		**08/11/2023**
		Utility Construction Plans (UCP)		**08/11/2023**
		Signing & Pav't. Marking Pln. (SIGN_DE		**08/11/2023**
		Roadway Plans to Cont & Prop (RPCP)		**08/18/2023**
		Obtain Permits	10.0 WK	10/27/2023
		Construction Consultation (CONST_CO		**08/21/2023**
		Obtain Riparian Buffer Auth (BUFAUTH)		**09/29/2023**
		Obtain 401 Permit (401)		**10/27/2023**
		Obtain 404 Permit (404)		**10/27/2023**
		Contract Advertisement	4.0 WK	11/21/2023
		Raleigh Letting (LET)		**11/21/2023**

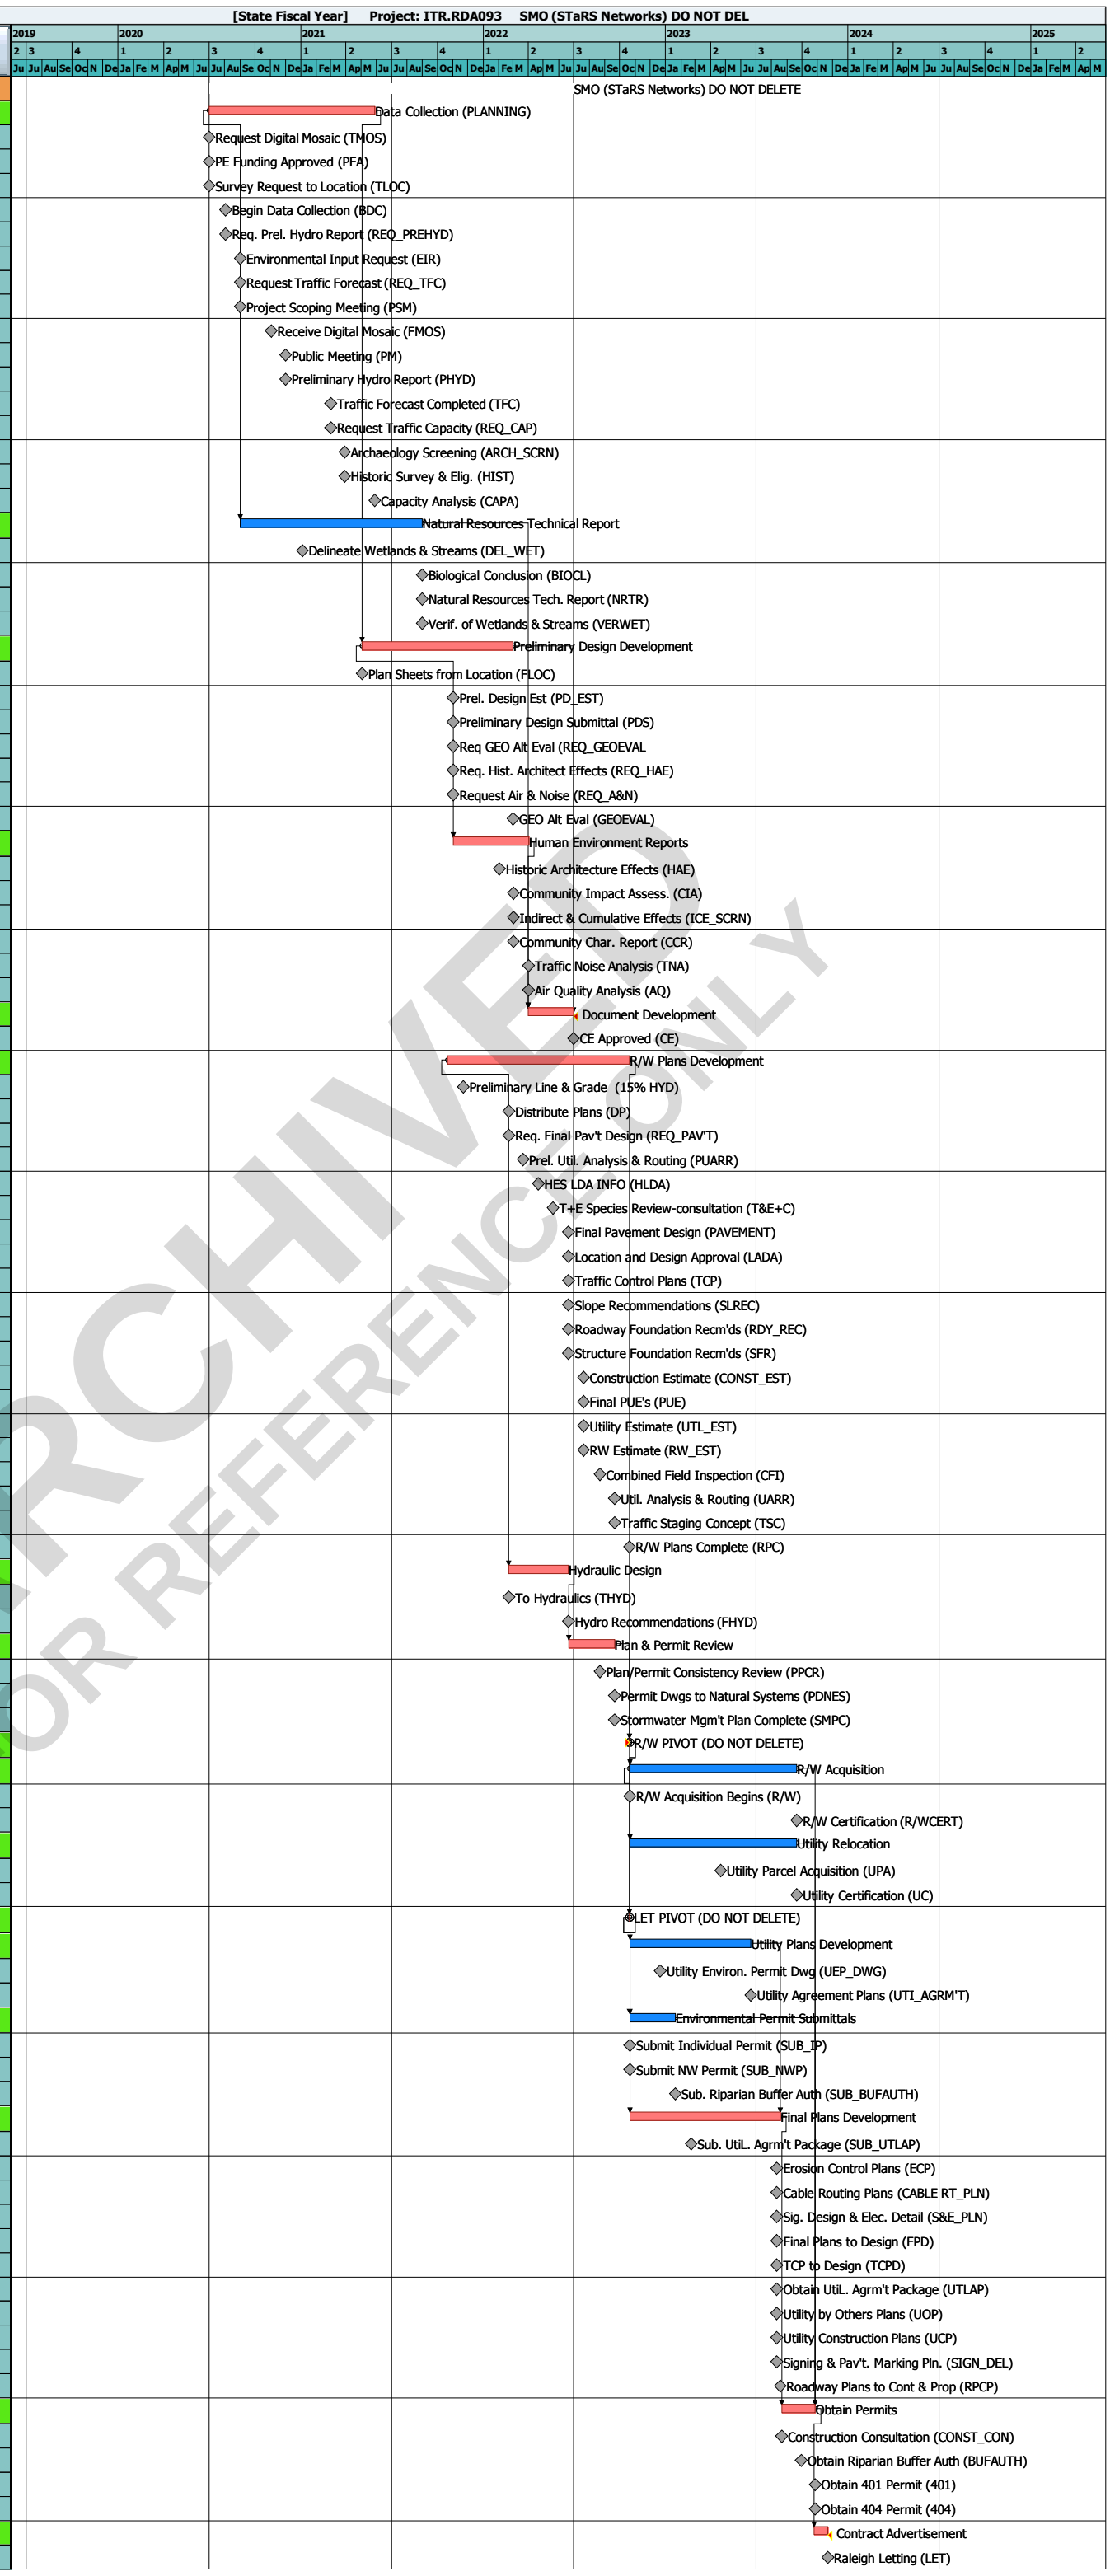

ARCHIVED
FOR REFERENCE ONLY
