[State Fiscal Year] Project: ITR.RDA093 SMO (STaRS Networks) DO NOT DEL

S	Hi	Description	Duratn	(B)ElSchFi
		SMO (STaRS Networks) DO NO	**,711.0 DAY**	
		Mapping	10.0 MON	08/31/2020
		PE Funding Approved (PFA)		11/01/2019
		Request Digital Ortho (TORT)		12/02/2019
		Request Digital Mosaic (TMOS)		12/02/2019
		Receive Digital Mosaic (FMOS)		04/01/2020
		Receive Digital Ortho (FORT)		08/31/2020
		Data Collection (PLANNING)	12.0 MON	03/31/2021
		Begin Data Collection (BDC)		04/01/2020
		Start of Study Letter (SOSL)		06/01/2020
		Internal Scoping Meeting (ISM)		06/01/2020
		Merger Screening Meeting (MSM)		07/01/2020
		Request CCR/Scr. ICE (REQ_CCR/SICE)		07/01/2020
		Community Char. Report (CCR)		03/01/2021
		Scoping Meeting Est (SM_EST)		03/01/2021
		Identify Conceptual Alternatives (ALT)		03/31/2021
		External Scoping Meeting (ESM)		03/31/2021
		Traffic & Capacity (Estimate)	12.0 MON	05/28/2021
		Req. Traffic Estimate (REQ_TRFE)		06/01/2020
		Traffic Estimate Complete (TRFE)		01/28/2021
		Req. Cap. Analysis (REQ_ICAP)		01/28/2021
		Capacity Analysis (CAP)		05/28/2021
		Purpose/Need & Alternatives (CP1 & CP	13.0 MON	04/29/2022
		Req GEO Alt Eval (REQ_GEOEVAL)		04/01/2021
		Public Meeting (PM)		06/01/2021
		Alternatives Screening Meeting (ASM)		07/01/2021
		Indirect & Cumulative Effects (ICE_SCR		08/30/2021
		Prel. GEO Recommendations (PGEO)		09/01/2021
		CP2 Est (CP2_EST)		03/29/2022
		Concurrence Point 1 (CP1)		03/29/2022
		CP1 Meeting (CP1M)		03/29/2022
		Concurrence Point 2 (CP2)		03/29/2022
		CP2 Meeting (CP2M)		03/29/2022
		RW Estimate (RW_EST)		04/29/2022
		Utility Estimate (UTL_EST)		04/29/2022
		Plan ITS DEV (ITS_DEV)		04/29/2022
		Alt. Development Functional Design	22.0 MON	04/28/2023
		GEO Alt Eval (GEOEVAL)		12/01/2021
		Archaeology Screening (ARCH_SCRN)		01/03/2022
		Req. Prel. Hydro Report (REQ_PREHYD)		02/01/2022
		Environmental Input Request (EIR)		02/01/2022
		Public Meeting (PM)		07/28/2022
		Historic Survey & Elig. (HIST)		01/30/2023
		Req. Hist. Architect Effects (REQ_HAE)		02/28/2023
		Request Air & Noise (REQ_A&N)		02/28/2023
		Functional Design Submittal (FDS)		02/28/2023
		Functional Design Est (FD_EST)		03/28/2023
		Traffic Estimate & Capacity (Update)	6.0 MON	10/31/2022
		Req. Update Traffic Estimate (REQ_UTR		05/02/2022
		Req. Update Cap. Analysis (REQ_UCAP)		09/02/2022
		Updated Traffic Estimate Comp. (UTRAF		09/02/2022
		Updated Capacity Analysis Comp. (UCA		10/31/2022
		Natural Resources Technical Report	12.0 MON	04/28/2023
		Delineate Wetlands & Streams (DEL_W		09/02/2022
		Verif. of Wetlands & Streams (VERWET)		04/28/2023
		Natural Resources Tech. Report (NRTR)		04/28/2023
		Biological Conclusion (BIOCL)		04/28/2023
		Human Environment Reports	4.0 MON	08/31/2023
		Community Impact Assess. (CIA)		06/01/2023
		Historic Architecture Effects (HAE)		06/30/2023
		Traffic Noise Analysis (TNA)		08/31/2023
		Air Quality Analysis (AQ)		08/31/2023
		Design & Const Impact Meeting (CP2A)	6.0 MON	12/29/2023
		Preliminary Hydro Report (PHYD)		07/03/2023
		Bridge Length Field Meeting (BLFM)		10/03/2023
		Concurrence Point 2A (CP2A)		12/29/2023
		CP2A Meeting (CP2AM)		12/29/2023
		CP2A Est (CP2A_EST)		12/29/2023
		Draft Environmental Document	9.0 MON	08/02/2024
		ICE Land Use Assessment (LUSA)		04/02/2024
		Draft EIS Approved (DEIS)		08/02/2024
		Public Hearing & Merger Application	5.0 MON	01/02/2025
		Corridor Public Hearing Rev Mtg (CPHR		08/05/2024
		Merger Permit Application (MPA)		10/07/2024
		Corridor Design Public Hearing (CDPH)		01/02/2025
		Alt. Select. & Min (CP3 & CP4A)	6.0 MON	06/30/2025
		Post Hearing Meeting (PHM)		02/03/2025
		Concurrence Point 3 (CP3)		05/01/2025
		CP3 Meeting (CP3M)		05/01/2025
		Concurrence Point 4A (CP4A)		05/01/2025
		CP4A Meeting (CP4AM)		05/01/2025
		Req. Comprehen. Arch. Survey (REQ_C		05/01/2025
		CP3 Est (CP3_EST)		06/30/2025
		CP4A EST (CP4A_EST)		06/30/2025
		Final Environmental Document	14.0 MON	08/31/2026
		Comprehensive Arch. Survey (C_ARCHS		07/01/2025
		Section 7 Consultation (SECT7)		07/01/2025
		Cultural Resources MOA (CR_MOA)		01/02/2026
		Final EIS Approved (FEIS)		07/31/2026
		ROD Approved (ROD)		08/31/2026
		Data Collection (DESIGN)	10.0 MON	03/09/2026
		PE Funding Design (PE_DSN)		05/12/2025
		Survey Request to Location (TLOC)		05/12/2025
		Req. Update Traffic Forecast (REQ_UTR		05/12/2025
		Updated Traffic Forecast Comp. (UTRAF		10/13/2025
		Req. Update Cap. Analysis (REQ_UCAP)		10/13/2025
		Updated Capacity Analysis Comp. (UCA		12/12/2025
		Plan Sheets from Location (FLOC)		03/09/2026
		Public Hearing	12.0 MON	05/08/2026
		Design Public Hearing Review Mtg (DP		12/12/2025
		Design Public Hearing (DPH)		03/09/2026
		Post Hearing Meeting (PHM)		05/08/2026
		Preliminary R/W Plans	10.0 MON	01/08/2027
		Req. Final Pav't Design (REQ_PAV'T)		03/10/2026
		Preliminary Line & Grade (15% HYD)		06/10/2026
		Distribute Plans (DP)		09/08/2026
		Request Design Noise Report (RDNR)		09/08/2026
		Draft Bridge Survey Reports (DBSR)		09/10/2026
		Prel. Util. Analysis & Routing (PUARR)		01/08/2027
		Hydraulic Design (CP4B)	8.0 MON	05/10/2027
		To Hydraulics (THYD)		09/11/2026
		Bridge Survey Reports (BSR)		11/12/2026
		Concurrence Point 4B (CP4B)		02/10/2027
		Hydro Recommendations (FHYD)		05/10/2027
		Preliminary Structure Design	4.0 MON	01/08/2027
		Structure Recommendations (STRREC)		09/11/2026
		Prel. Bridge General Drawings (PGD'S)		01/08/2027
		Final R/W Plans	10.0 MON	11/09/2027
		Final Pavement Design (PAVEMENT)		01/11/2027
		Traffic Staging Concept (TSC)		01/11/2027
		Slope Recommendations (SLREC)		02/11/2027
		Design Noise Report (DNR)		03/11/2027
		Roadway Foundation Recm'ds (RDY_RE		05/10/2027
		HES LDA INFO (HLDA)		06/09/2027
		Structure Foundation Recm'ds (SFR)		06/09/2027
		Location and Design Approval (LADA)		07/09/2027
		Final PUE's (PUE)		07/09/2027
		RW Estimate (RW_EST)		07/09/2027
		Utility Estimate (UTL_EST)		07/09/2027
		R/W Consultation (R/WCONS)		07/09/2027
		Final Design Field Inspection (FDFI)		08/09/2027
		Util. Analysis & Routing (UARR)		10/11/2027
		R/W Plans Complete (RPC)		11/09/2027
		Construction Estimate (CONST_EST)		11/09/2027
		R/W PIVOT (DO NOT DELETE)		11/09/2027
		R/W Acquisition	22.0 MON	09/07/2029
		R/W Acquisition Begins (R/W)		11/10/2027
		R/W Certification (R/WCERT)		09/07/2029
		Utility Relocation	22.0 MON	09/07/2029
		Utility Parcel Acquisition (UPA)		05/10/2028
		Utility Certification (UC)		09/07/2029
		LET PIVOT (DO NOT DELETE)		05/10/2027
		Utility Plans Development	20.0 MON	01/10/2029
		Utility Environ. Permit Dwg (UEP_DWG)		05/10/2028
		Utility Agreement Plans (UTI_AGRM'T)		01/10/2029
		Hydraulic Permits (CP4C)	6.0 MON	03/10/2028
		Submit HYD MOA Permit (SUB_HYDMO		10/13/2027
		Submit CLOMR Permit (SUB_CLOMR)		10/13/2027
		Concurrence Point 4C (CP4C)		03/10/2028
		Plan & Permit Review	5.0 MON	07/11/2028
		T+E Species Review-consultation (T&E		04/17/2028
		Plan/Permit Consistency Review (PPCR		06/12/2028
		Permit Dwgs to Natural Systems (PDNE		07/11/2028
		Stormwater Mgm't Plan Complete (SMP		07/11/2028
		Environmental Permit Submittals	5.0 MON	12/11/2028
		Submit NW Permit (SUB_NWP)		07/12/2028
		Submit Individual Permit (SUB_IP)		07/12/2028
		Sub. Riparian Buffer Auth (SUB_BUFAU		12/11/2028
		Submit Util. Environ. Permit (SUB_UEP		12/11/2028
		Final Plans Development	22.0 MON	07/10/2029
		Traffic Control Plans (TCP)		09/13/2027
		Final Pavement Design Review (PAV_R		09/13/2027
		13 month Estimate (13M_EST)		08/14/2028
		Pre-Let Field Inspection (PLFI)		01/10/2029
		Sub. Util. Agrm't Package (SUB_UTLAP		02/12/2029
		Utility Construction Plans (UCP)		07/02/2029
		Utility by Others Plans (UOP)		07/02/2029
		Obtain Util. Agrm't Package (UTLAP)		07/02/2029
		Final Plans to Design (FPD)		07/02/2029
		TCP to Design (TCPD)		07/02/2029
		Sig. Design & Elec. Detail (S&E_PLN)		07/02/2029
		Cable Routing Plans (CABLE RT_PLN)		07/02/2029
		Erosion Control Plans (ECP)		07/02/2029
		Signing & Pav't. Marking Pln. (SIGN_DE		07/02/2029
		Roadway Plans to Cont & Prop (RPCP)		07/10/2029
		Structure Plans to Plan checking (STRP		07/10/2029
		Obtain Permits	10.0 WK	09/18/2029
		Struct. Plans to Contract Office (SPCP)		07/24/2029
		Construction Consultation (CONST_CO		08/20/2029
		Obtain HYD MOA Permit (HYD_MOA)		08/21/2029
		Obtain CLOMR Permit (CLOMR)		08/21/2029
		Obtain Riparian Buffer Auth (BUFAUTH)		08/21/2029
		Obtain Util. Environ. Permit (UEP)		08/21/2029
		Obtain 401 Permit (401)		09/18/2029
		Obtain 404 Permit (404)		09/18/2029
		Contract Advertisement	4.0 WK	10/16/2029
		Raleigh Letting (LET)		10/16/2029

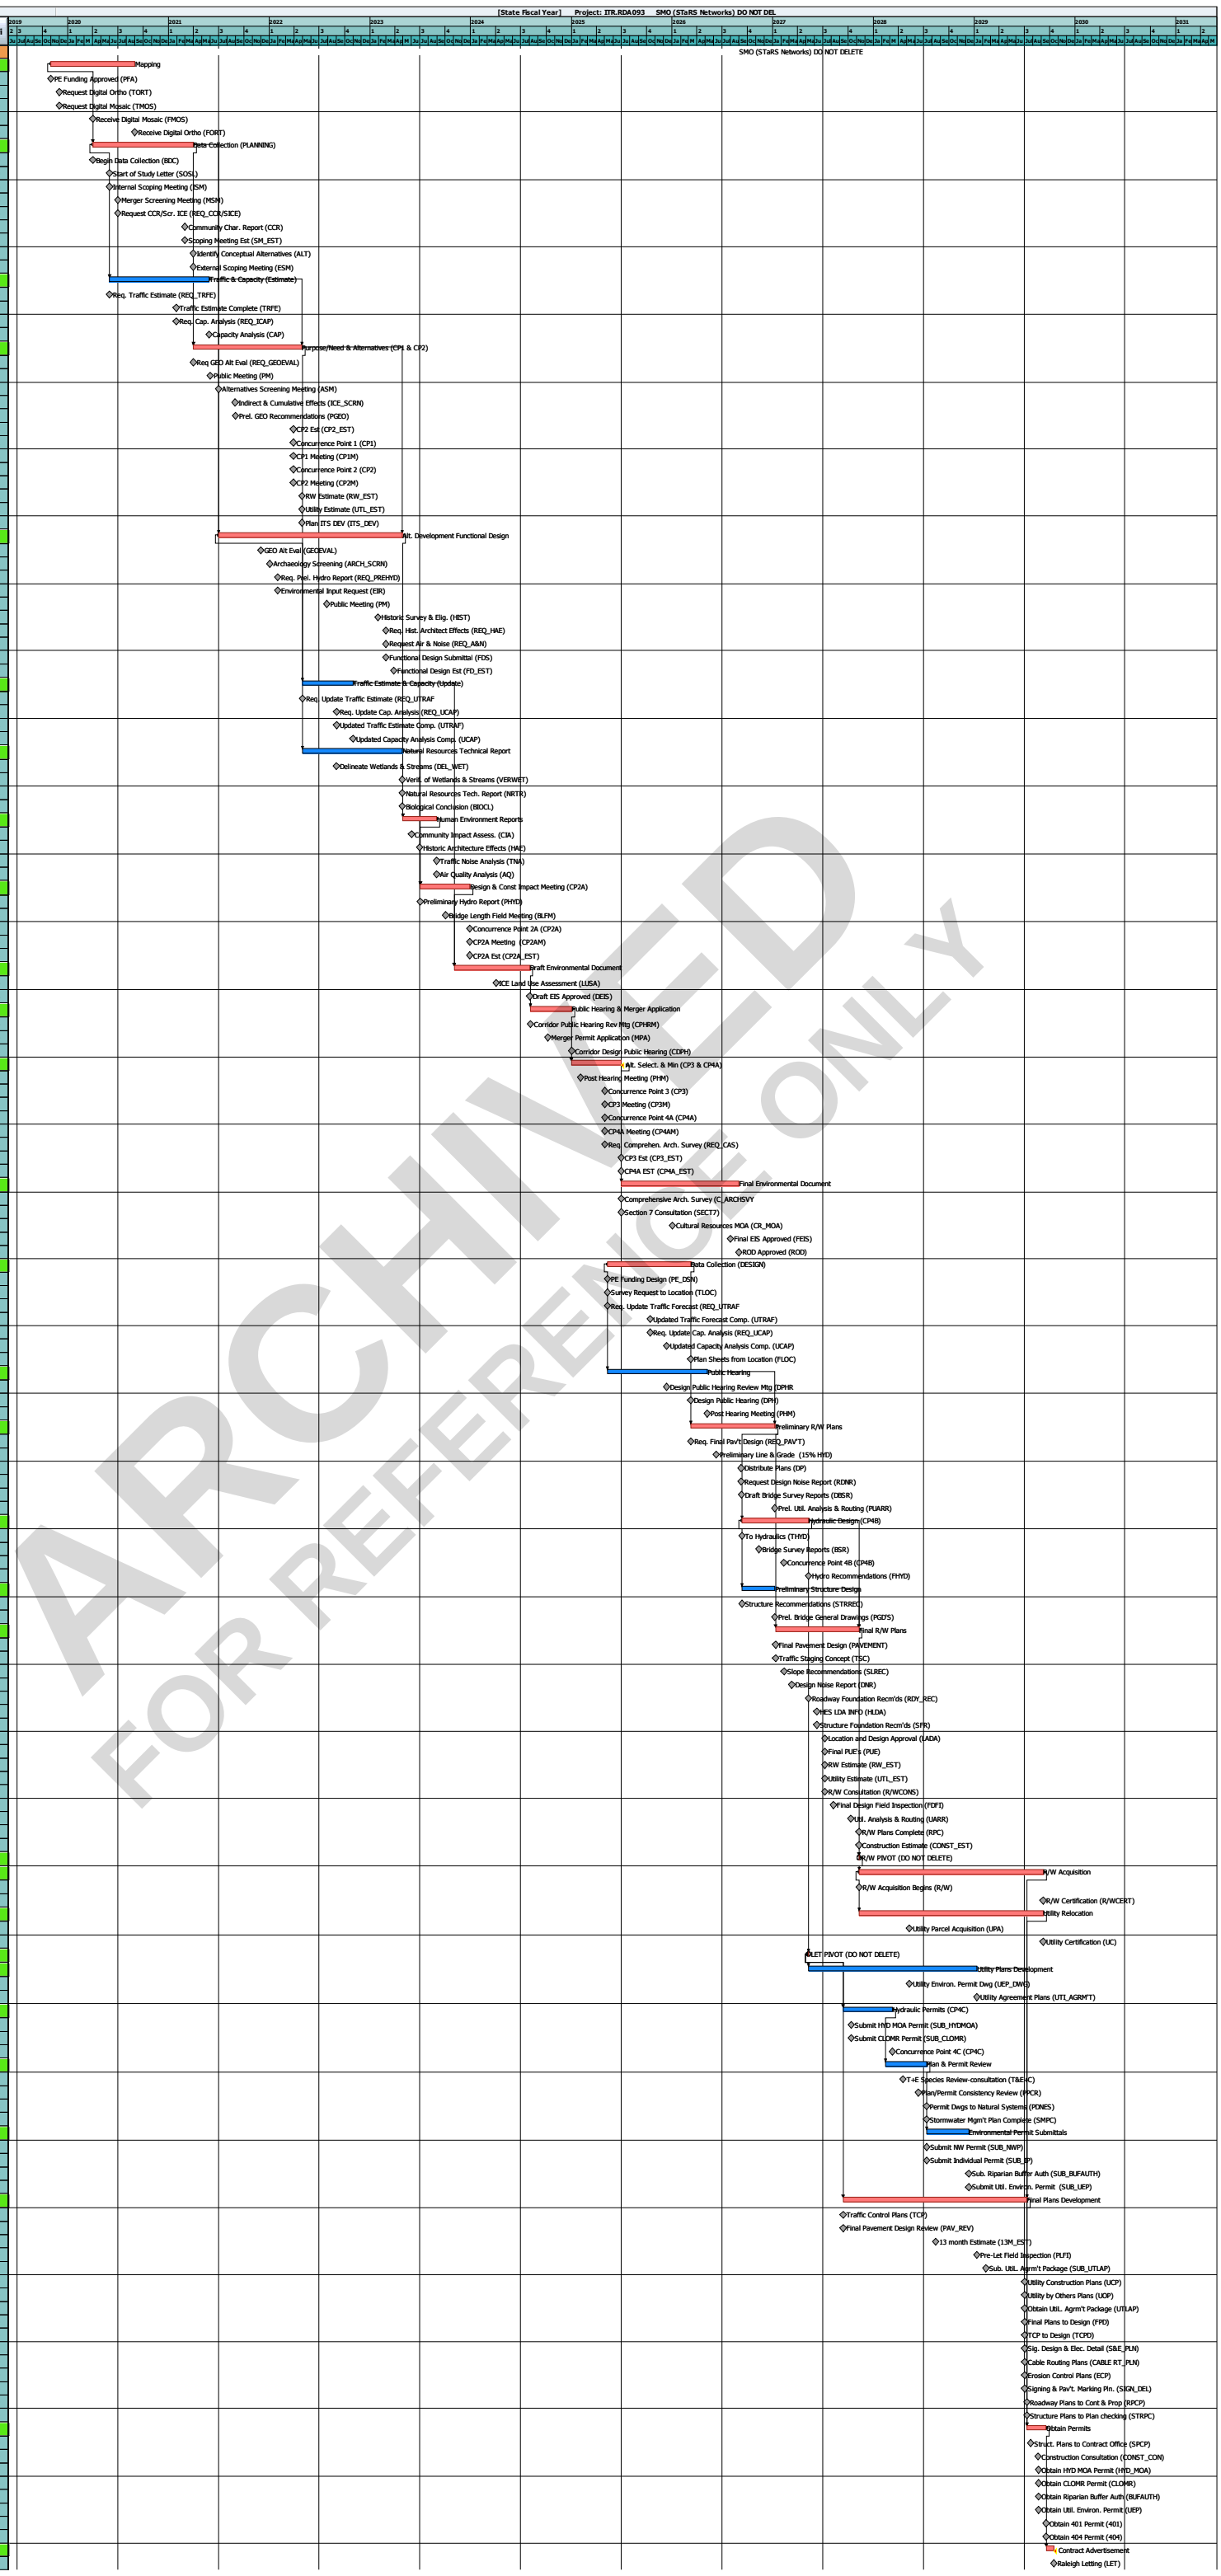

ARCHIVED FOR REFERENCE ONLY

NEW LOCATION
