[State Fiscal Year] Project: ITR.RDA093 SMO (STaRS Networks) DO NOT DEL

S	Hi	Description	Duratn	(B)ElSchFi
		SMO (STaRS Networks) DO NO	**,234.0 DAY**	
		Final Surveys	12.0 MON	06/26/2023
		PE Funding Approved (PFA)		06/27/2022
		Request Digital Mosaic (TMOS)		07/27/2022
		Survey Request to Location (TLOC)		07/27/2022
		Receive Digital Mosaic (FMOS)		11/28/2022
		Plan Sheets from Location (FLOC)		06/26/2023
		Data Collection (PLANNING)	15.0 MON	02/27/2024
		Begin Data Collection (BDC)		11/28/2022
		Req. Prel. Geotech. Input (REQ_PGEO)		01/30/2023
		Request Crash Data (REQ_CRD)		01/30/2023
		Request CCR/Scr. ICE (REQ_CCR/SICE)		01/30/2023
		Internal Scoping Meeting (ISM)		01/30/2023
		Merger Screening Meeting (MSM)		02/28/2023
		Start of Study Letter (SOSL)		02/28/2023
		Public Meeting (PM)		04/28/2023
		Environmental Input Request (EIR)		05/30/2023
		Prel. GEO Recommendations (PGEO)		08/28/2023
		Receive Crash Data (CRDA)		08/28/2023
		Community Char. Report (CCR)		08/28/2023
		Scoping Meeting Est (SM_EST)		08/28/2023
		Archaeology Screening (ARCH_SCRN)		08/28/2023
		Indirect & Cumulative Effects (ICE_SCR		11/27/2023
		External Scoping Meeting (ESM)		02/27/2024
		Historic Survey & Elig. (HIST)		02/27/2024
		Req. Comprehen. Arch. Survey (REQ_C		02/27/2024
		Traffic & Capacity	10.0 MON	11/27/2023
		Request Traffic Forecast (REQ_TFC)		01/30/2023
		Traffic Forecast Completed (TFC)		07/27/2023
		Req. Cap. Analysis (REQ_ICAP)		07/27/2023
		Capacity Analysis (CAP)		11/27/2023
		Natural Resources Technical Report	12.0 MON	05/24/2024
		Delineate Wetlands & Streams (DEL_W		10/02/2023
		Natural Resources Tech. Report (NRTR)		05/24/2024
		Biological Conclusion (BIOCL)		05/24/2024
		Verif. of Wetlands & Streams (VERWET)		05/24/2024
		Alternatives Analysis (CP1 & CP2)	9.0 MON	04/26/2024
		Identify Conceptual Alternatives (ALT)		10/30/2023
		Concurrence Point 1 (CP1)		04/26/2024
		CP1 Meeting (CP1M)		04/26/2024
		Concurrence Point 2 (CP2)		04/26/2024
		CP2 Meeting (CP2M)		04/26/2024
		CP2 Est (CP2_EST)		04/26/2024
		Plan ITS DEV (ITS_DEV)		04/26/2024
		Preliminary Design	8.0 MON	12/27/2024
		Req. Prel. Hydro Report (REQ_PREHYD)		04/29/2024
		Req. Hist. Architect Effects (REQ_HAE)		04/29/2024
		Req GEO Alt Eval (REQ_GEOEVAL)		04/29/2024
		GEO Alt Eval (GEOEVAL)		10/28/2024
		Request Air & Noise (REQ_A&N)		12/27/2024
		Preliminary Design Submittal (PDS)		12/27/2024
		Prel. Design Est (PD_EST)		12/27/2024
		RW Estimate (RW_EST)		12/27/2024
		Utility Estimate (UTL_EST)		12/27/2024
		Human Environment Reports	5.0 MON	05/27/2025
		Historic Architecture Effects (HAE)		01/30/2025
		Air Quality Analysis (AQ)		05/27/2025
		Community Impact Assess. (CIA)		05/27/2025
		Traffic Noise Analysis (TNA)		05/27/2025
		Design & Const Impact Meeting (CP2A)	6.0 MON	06/27/2025
		Preliminary Hydro Report (PHYD)		12/30/2024
		Bridge Length Field Meeting (BLFM)		03/31/2025
		Concurrence Point 2A (CP2A)		06/27/2025
		CP2A Meeting (CP2AM)		06/27/2025
		CP2A Est (CP2A_EST)		06/27/2025
		Draft Environmental Document	9.0 MON	11/26/2025
		EA Approved (EA)		11/26/2025
		Public Hearing & Merger Application	5.0 MON	04/27/2026
		Design Public Hearing Review Mtg (DP		01/02/2026
		Merger Permit Application (MPA)		02/27/2026
		Design Public Hearing (DPH)		04/27/2026
		Alt. Select. & Min (CP3 & CP4A)	6.0 MON	10/27/2026
		Post Hearing Meeting (PHM)		06/29/2026
		Concurrence Point 3 (CP3)		09/28/2026
		CP3 Meeting (CP3M)		09/28/2026
		Concurrence Point 4A (CP4A)		09/28/2026
		CP4A Meeting (CP4AM)		09/28/2026
		CP3 Est (CP3_EST)		10/27/2026
		CP4A EST (CP4A_EST)		10/27/2026
		Final Environmental Document	8.0 MON	05/28/2027
		Comprehensive Arch. Survey (C_ARCHS		09/29/2026
		Section 7 Consultation (SECT7)		09/29/2026
		Cultural Resources MOA (CR_MOA)		05/28/2027
✔		FONSI Approved (FONSI)		05/28/2027
		Preliminary R/W Plans	12.0 MON	12/15/2026
		PE Funding Design (PE_DSN)		12/16/2025
		Preliminary Line & Grade (15% HYD)		04/16/2026
		Req. Final Pav't Design (REQ_PAV'T)		05/15/2026
		Draft Bridge Survey Reports (DBSR)		06/16/2026
		Distribute Plans (DP)		07/15/2026
		Request Design Noise Report (RDNR)		07/15/2026
		Prel. Util. Analysis & Routing (PUARR)		12/15/2026
		Hydraulic Design (CP4B)	8.0 MON	03/16/2027
		To Hydraulics (THYD)		07/17/2026
		Bridge Survey Reports (BSR)		09/17/2026
		Concurrence Point 4B (CP4B)		11/17/2026
		Hydro Recommendations (FHYD)		03/16/2027
		Preliminary Structure Design	4.0 MON	11/16/2026
		Structure Recommendations (STRREC)		07/17/2026
		Prel. Bridge General Drawings (PGD'S)		11/16/2026
		Final R/W Plans	10.0 MON	10/15/2027
		Traffic Staging Concept (TSC)		12/16/2026
		Slope Recommendations (SLREC)		12/16/2026
		Design Noise Report (DNR)		01/19/2027
		Roadway Foundation Recm'ds (RDY_RE		02/15/2027
		Final Pavement Design (PAVEMENT)		03/16/2027
		Structure Foundation Recm'ds (SFR)		04/15/2027
		HES LDA INFO (HLDA)		05/17/2027
		Location and Design Approval (LADA)		06/15/2027
		Final PUE's (PUE)		06/15/2027
		RW Estimate (RW_EST)		06/15/2027
		Utility Estimate (UTL_EST)		06/15/2027
		R/W Consultation (R/WCONS)		06/15/2027
		Combined Field Inspection (CFI)		07/15/2027
		Util. Analysis & Routing (UARR)		09/15/2027
		R/W Plans Complete (RPC)		10/15/2027
		Construction Estimate (CONST_EST)		10/15/2027
		R/W PIVOT (DO NOT DELETE)		10/15/2027
		R/W Acquisition	22.0 MON	08/15/2029
		R/W Acquisition Begins (R/W)		10/18/2027
		R/W Certification (R/WCERT)		08/15/2029
		Utility Relocation	22.0 MON	08/15/2029
		Utility Parcel Acquisition (UPA)		04/18/2028
		Utility Certification (UC)		08/15/2029
		LET PIVOT (DO NOT DELETE)		03/29/2027
		Utility Plans Development	20.0 MON	11/29/2028
		Utility Environ. Permit Dwg (UEP_DWG)		02/29/2028
		Utility Agreement Plans (UTI_AGRM'T)		11/29/2028
		Hydraulic Permits (CP4C)	6.0 MON	02/29/2028
		Submit HYD MOA Permit (SUB_HYDMO		09/30/2027
		Submit CLOMR Permit (SUB_CLOMR)		09/30/2027
		Concurrence Point 4C (CP4C)		02/29/2028
		Plan & Permit Review	5.0 MON	06/30/2028
		T+E Species Review-consultation (T&E		04/03/2028
		Plan/Permit Consistency Review (PPCR		05/30/2028
		Permit Dwgs to Natural Systems (PDNE		06/30/2028
		Stormwater Mgm't Plan Complete (SMP		06/30/2028
		Environmental Permit Submittals	5.0 MON	12/01/2028
		Submit Individual Permit (SUB_IP)		07/03/2028
		Submit NW Permit (SUB_NWP)		07/03/2028
		Sub. Riparian Buffer Auth (SUB_BUFA U		12/01/2028
		Submit Util. Environ. Permit (SUB_UEP		12/01/2028
		Final Plans Development	20.0 MON	06/29/2029
		Final Pavement Design Review (PAV_R		11/01/2027
		Traffic Control Plans (TCP)		11/01/2027
		13 month Estimate (13M_EST)		10/02/2028
		Sub. Util. Agrm't Package (SUB_UTLAP		01/29/2029
		Utility Construction Plans (UCP)		06/22/2029
		Utility by Others Plans (UOP)		06/22/2029
		Obtain Util. Agrm't Package (UTLAP)		06/22/2029
		Final Plans to Design (FPD)		06/22/2029
		TCP to Design (TCPD)		06/22/2029
		Sig. Design & Elec. Detail (S&E_PLN)		06/22/2029
		Cable Routing Plans (CABLE RT_PLN)		06/22/2029
		Erosion Control Plans (ECP)		06/22/2029
		Signing & Pav't. Marking Pln. (SIGN_DE		06/22/2029
		Roadway Plans to Cont & Prop (RPCP)		06/29/2029
		Structure Plans to Plan checking (STRP		06/29/2029
		Obtain Permits	10.0 WK	09/07/2029
		Struct. Plans to Contract Office (SPCP)		07/13/2029
		Construction Consultation (CONST_CO		08/07/2029
		Obtain HYD MOA Permit (HYD_MOA)		08/10/2029
		Obtain CLOMR Permit (CLOMR)		08/10/2029
		Obtain Riparian Buffer Auth (BUFAUTH)		08/10/2029
		Obtain Util. Environ. Permit (UEP)		08/10/2029
		Obtain 401 Permit (401)		09/07/2029
		Obtain 404 Permit (404)		09/07/2029
		Contract Advertisement	4.0 WK	10/16/2029
		Raleigh Letting (LET)		10/16/2029

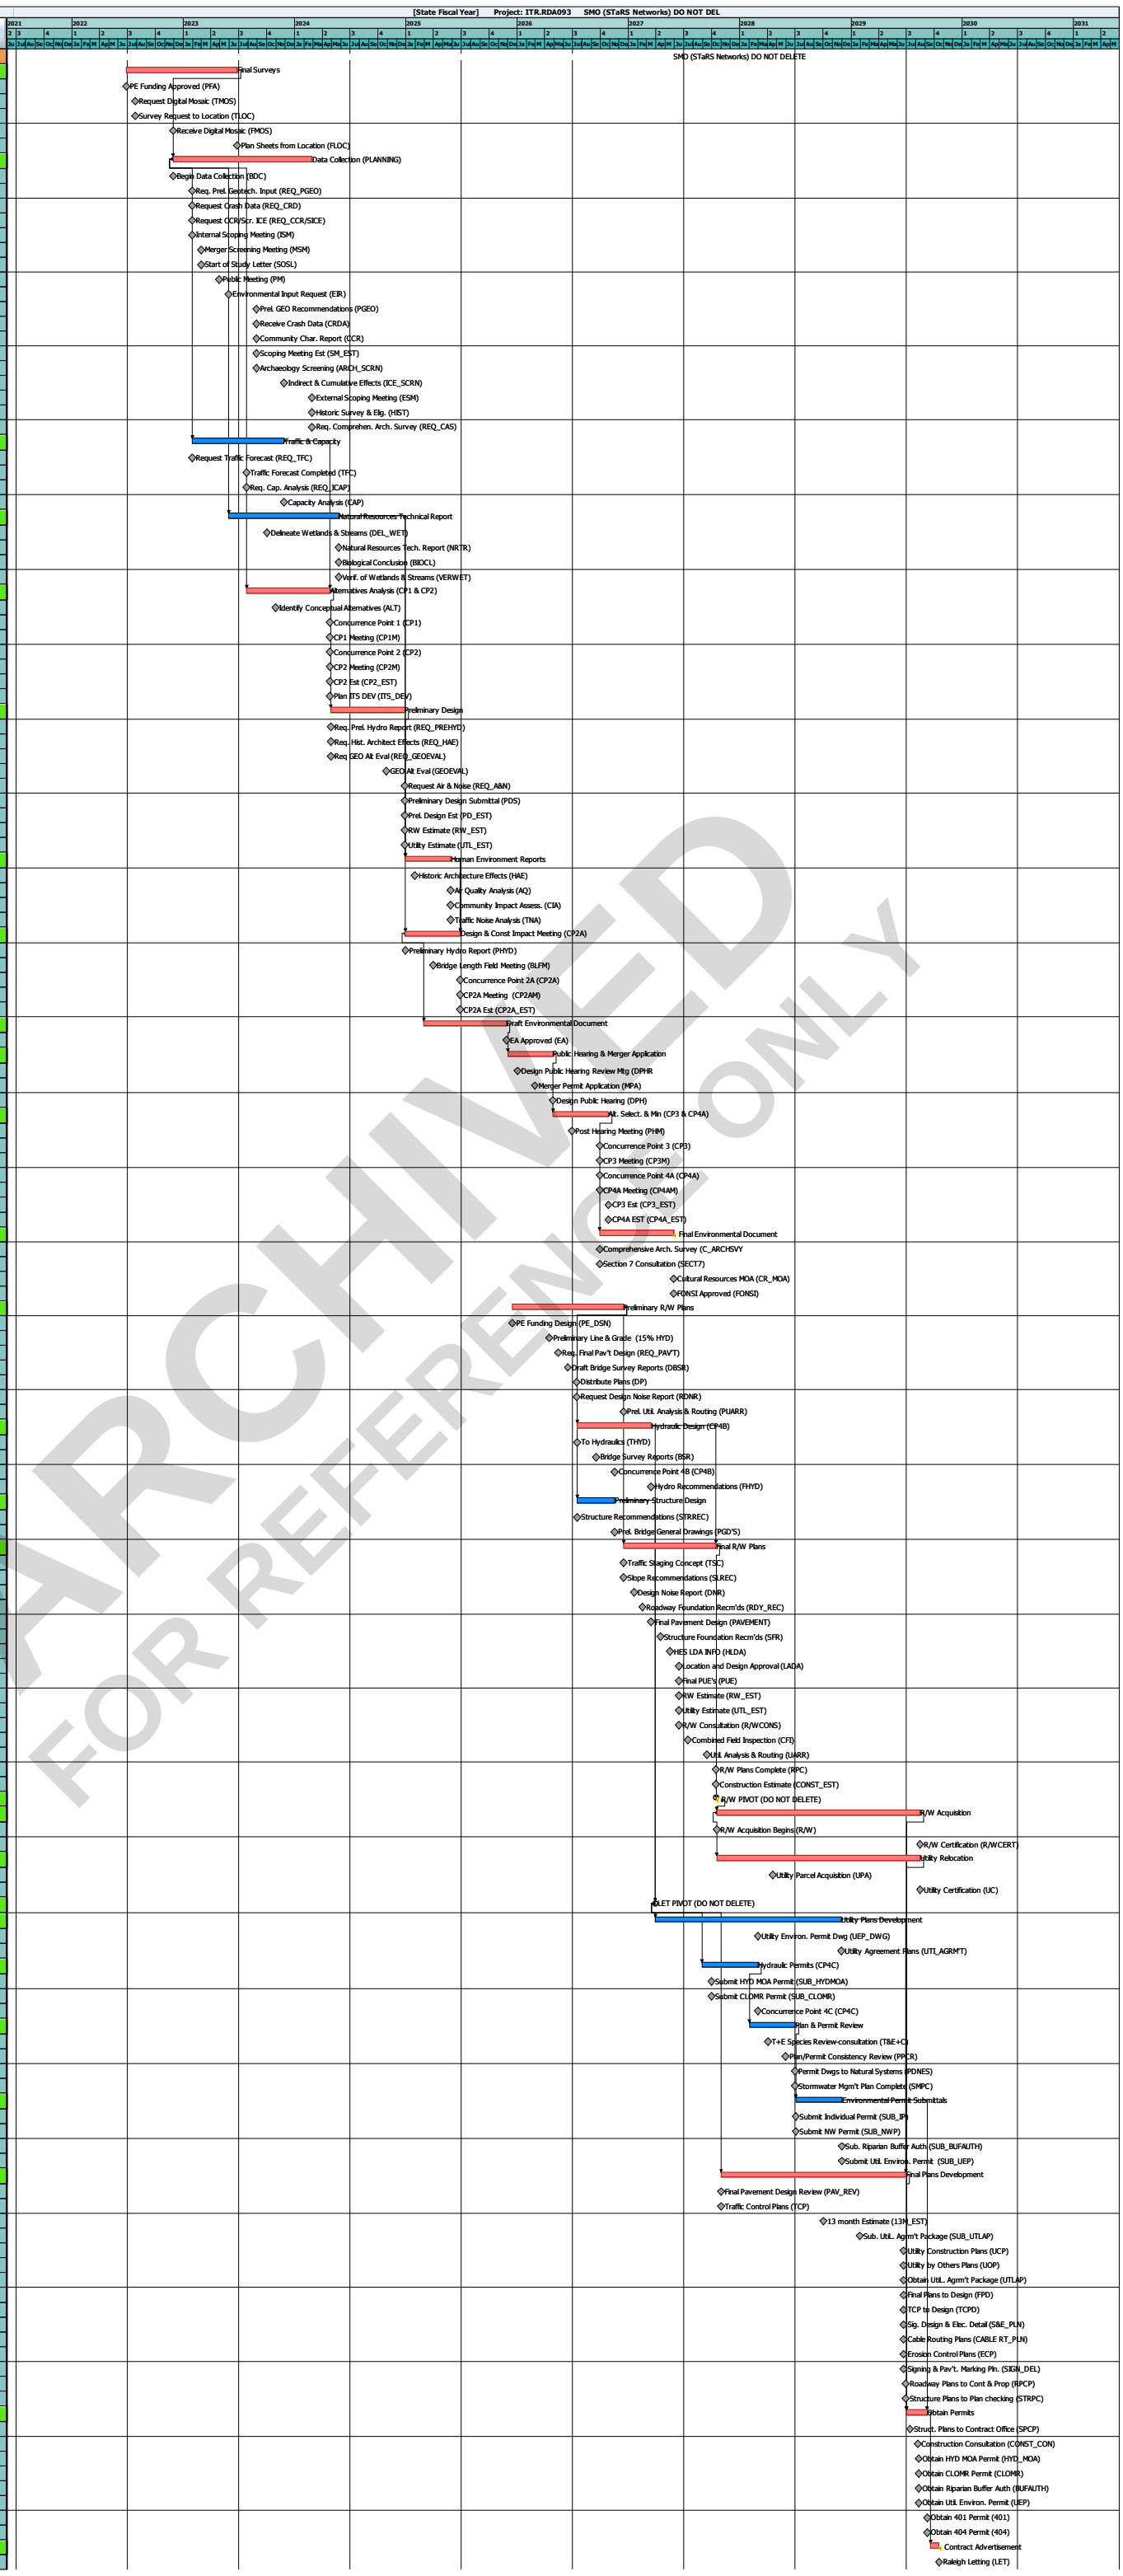

ARCHIVED FOR REFERENCE ONLY
