



STATE OF NORTH CAROLINA
DEPARTMENT OF TRANSPORTATION

ROY COOPER
GOVERNOR

JAMES H. TROGDON, III
SECRETARY

January 27, 2017

ADDENDUM # 1

To: Plan Holders

DS
wa

From: Wanda H. Austin, P.E.
Division 14 Project Team Lead

RE: **Revision of Plan Title Sheet
Revision of Contract Time and Liquidated Damages
Inclusion of ICT 1**

Contract ID: DN00548
County: Haywood
Letting Date: February 14, 2017

The above contract has experienced the following revisions:

1. Replace the existing plan Title Sheet with the revised plan Title Sheet (see attachment).
2. On page **G-7**, under **Contract Time and Liquidated Damages**, revise the last sentence of the last paragraph to read:

These liquidated damages will not be cumulative with any liquidated damages which may become chargeable under Intermediate Contract Time Number 1 and Intermediate Contract Time Number 2.

3. On page **G-7**, between **Contract Time and Liquidated Damages** and **Intermediate Contract Time Number 2 And Liquidated Damages**, insert the following language:

INTERMEDIATE CONTRACT TIME NUMBER 1 AND LIQUIDATED DAMAGES:
(7-1-95) (Rev. 2-21-12) 108 SPI G13 A

Except for that work required under the Project Special Provisions entitled *Planting, Reforestation* and/or *Permanent Vegetation Establishment*, included elsewhere in this proposal, the Contractor will be required to complete all work included in this contract and shall place and maintain traffic on same.

The date of availability for this intermediate contract time is **April 3, 2017**.

The completion date for this intermediate contract time is **June 2, 2017**.


The liquidated damages for this intermediate contract time are **Five Hundred Dollars (\$ 500.00)** per calendar day.

Upon apparent completion of all the work required to be completed by this intermediate date, a final inspection will be held in accordance with Article 105-17 and upon acceptance, the Department will assume responsibility for the maintenance of all work except *Planting, Reforestation* and/or *Permanent Vegetation Establishment*. The Contractor will be responsible for and shall make corrections of all damages to the completed roadway caused by his planting operations, whether occurring prior to or after placing traffic through the project.

These revisions do not change bid items or the associated quantities.

Please access ebs addenda files on Bid Express®.

Please insert this letter into the addendum section of the proposal and sign the verification. Thank you for your attention to this matter.

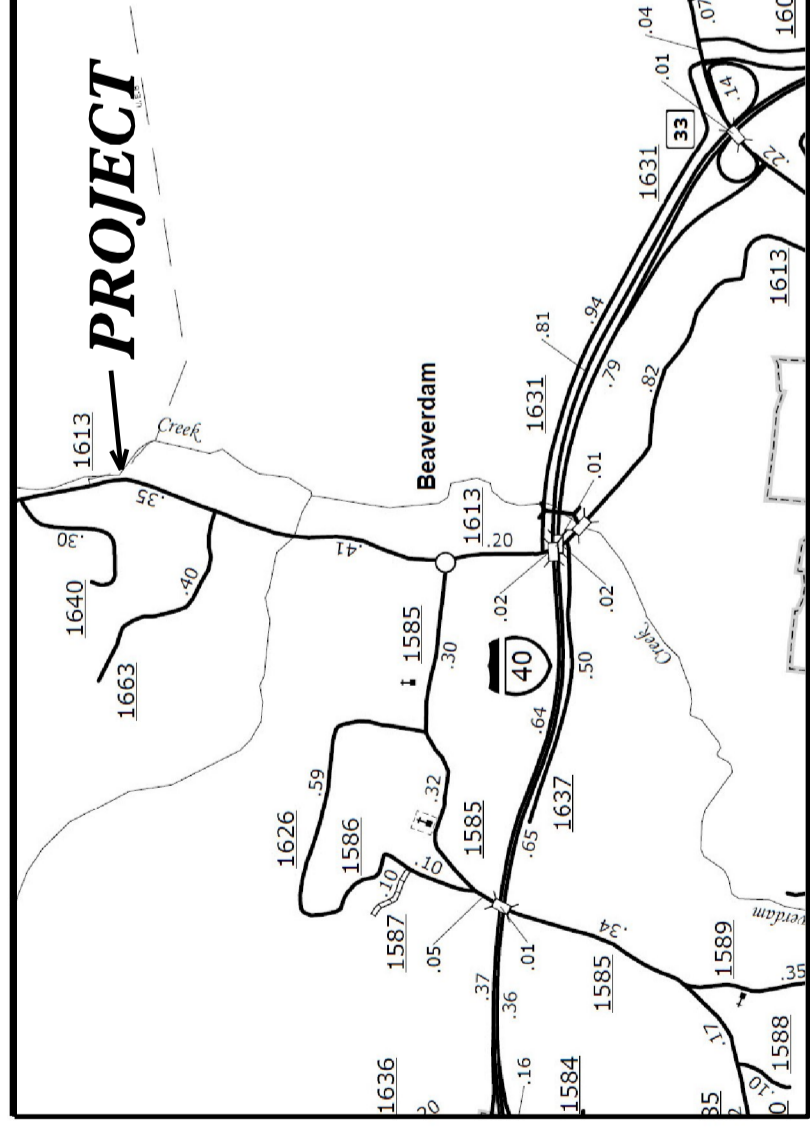

VICINITY MAP

STATE OF NORTH CAROLINA
DIVISION OF HIGHWAYS

HAYWOOD COUNTY

LOCATION: SR 1613 - BEAVERDAM ROAD

FROM: 0.1 Mile North of SR 1663


TO: 0.17 Mile South of SR 1640

TYPE OF WORK: GRADING, TRAFFIC CONTROL, EROSION CONTROL

STATE	STATE PROJECT REFERENCE NO.	SHEET NO.	TOTAL SHEETS
N.C.	W-5601GP	1	
STATE PROJ. NO.	F.A. PROJ. NO.	DESCRIPTION	
50138.1.119	HSIP-1613(009)	PE	
50138.3.199	HSIP-1613(009)	CONST.	



DOCUMENT NOT CONSIDERED FINAL
UNLESS ALL SIGNATURES COMPLETED

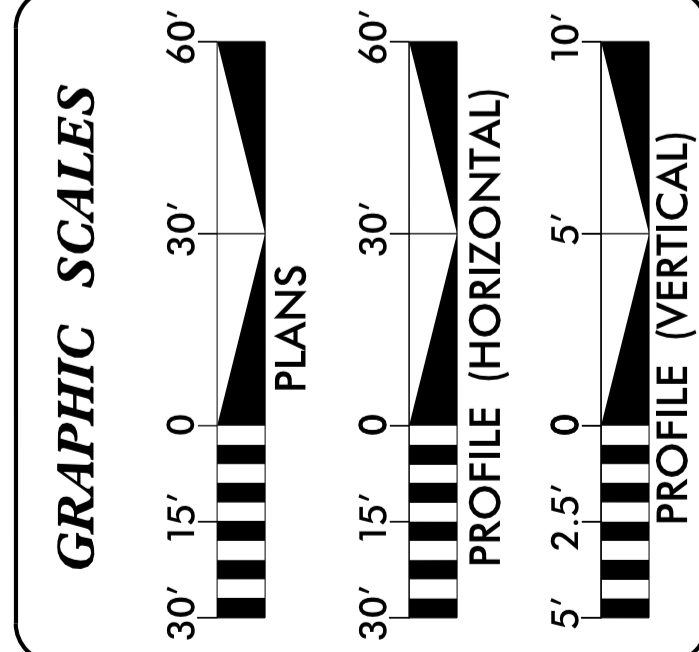

DESIGN DATA

AADT	=	200(2015)
ADT	=	
K	=	%
D	=	%
T	=	% *
V	=	40 MPH
* TTST	=	DUAL
FUNC CLASS	=	LOCAL

PROJECT LENGTH

LENGTH OF TIP PROJECT NO. W-5601GP = 0.092 mi.

Prepared in the Office of:
DIVISION OF HIGHWAYS
1000 Birch Ridge Dr., Raleigh N.C., 27610

2012 STANDARD SPECIFICATIONS


RIGHT OF WAY DATE:	JONATHAN WOODARD, PE PROJECT ENGINEER
LETTING DATE:	MARK HILL, PE PROJECT DESIGN ENGINEER
	02/14/2017

HYDRAULICS ENGINEER

SIGNATURE: _____ P.E.

ROADWAY DESIGN ENGINEER

SIGNATURE: _____ P.E.

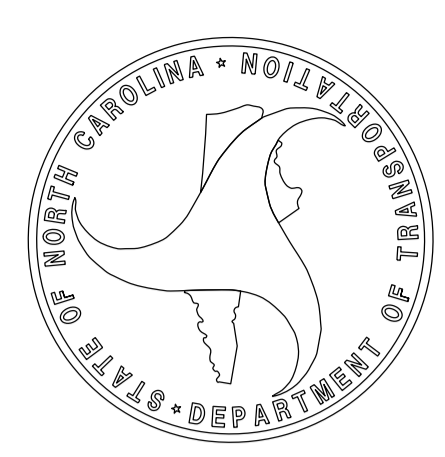

TIP PROJECT: W-5601GP

CONTRACT: DN00548
