


ID	WBS	Discipline Code	Task Code	SAP MLSN	Task Name	% Complete	Duration	Start	
1	1		2		<b>Project Initiation (Stg 1)</b>	0%	5 days?	Mon 6/14/21	
2	1.1	MLSN	MLSN		Develop STIP	0%	0 days	Mon 6/14/21	
3	1.2	EN	1EN1		Initiate Environmental Analysis	0%	1 day?	Mon 6/14/21	
4	1.3	MLSN	MLSN		Draft STIP	0%	1 day?	Mon 6/14/21	
5	1.4	PH	1PH2		Compile Aerial Photography & Mapping	0%	1 day?	Tue 6/15/21	
6	1.5	VM	1VM1		Initiate CR-RAVE and CLEAR Activities	0%	1 day?	Tue 6/15/21	
7	1.6	UT	1UT2		Initiate Utility Investigations	0%	1 day?	Tue 6/15/21	
8	1.7	PI	1PI1		Initiate Public Engagement Tasks	0%	1 day?	Tue 6/15/21	
9	1.8	CG	1CG1		Review Project Scoping	0%	1 day?	Wed 6/16/21	
10	1.9	LS	1LS1		Provide Photogrammetric Control & Initiate Survey	0%	1 day?	Wed 6/16/21	
11	1.10	GT	1GT1		Complete Geotechnical & GeoEnvironmental Screening	0%	1 day?	Wed 6/16/21	
12	1.11	EP	1EP1		Initiate Environmental Review	0%	1 day?	Wed 6/16/21	
13	1.12	FS	1FS3		Complete Project Scoping Report	0%	1 day?	Thu 6/17/21	
14	1.13	PM			Request Preliminary Engineering Funds	0%	1 day?	Fri 6/18/21	
15	1.14	MLSN	MLSN	M0965	NTP	0%	0 days	Thu 6/17/21	
16	2		2		<b>Alignment Defined (Stg 2)</b>	0%	6 days?	Fri 6/18/21	
17	2.1	LS	2LS1		Complete Final Surveys	0%	1 day?	Fri 6/18/21	
18	2.2	LS	2LS2		Complete SUE Level A & ROW Advance Acquisition Surveys	0%	1 day?	Fri 6/18/21	
19	2.3	RD	2RD1		Complete Design Recommendation Plan Set	0%	1 day?	Mon 6/21/21	
20	2.4	HY	2HY1		Develop Preliminary Hydraulic Recommendations	0%	1 day?	Fri 6/18/21	
21	2.5	HY	2HY2		Complete Drainage Design for Field Inspection	0%	1 day?	Tue 6/22/21	
22	2.6	GT	2GT1		Prepare GeoEnvironmental Phase I Report	0%	1 day?	Fri 6/18/21	
23	2.7	GT	2GT2		Conduct Subsurface Investigations & Provide Roadway Recor	0%	1 day?	Fri 6/18/21	
24	2.8	GT	2GT3		Complete Pavement & Subgrade Investigation and Recomme	0%	1 day?	Fri 6/18/21	
25	2.9	PD	2PD1		Complete Pavement Design	0%	1 day?	Fri 6/18/21	
26	2.10	ST	2ST1		Initiate Structures Design	0%	1 day?	Tue 6/22/21	
27	2.11	ST	2ST2		Develop Preliminary General Drawings	0%	1 day?	Wed 6/23/21	
28	2.12	EN	2EN1		Advance Natural Environment Tasks	0%	1 day?	Fri 6/18/21	
29	2.13	EN	2EN2		Advance Human Environment Tasks	0%	1 day?	Fri 6/18/21	
30	2.14	EP	2EP1		Prepare Environmental Document	0%	1 day?	Mon 6/21/21	
31	2.15	TM	2TM1		Complete Traffic Analysis	0%	1 day?	Fri 6/18/21	
32	2.16	TM	2TM2		Initiate Transportation Management Plan	0%	1 day?	Mon 6/21/21	
33	2.17	TO	2TO1		Initiate Transportation Operations Plan (if a Significant Projec	0%	1 day?	Mon 6/21/21	
34	2.18	RR	2RR1		Initiate Railroad Review	0%	1 day?	Fri 6/18/21	
35	2.19	RW	2RW1		Initiate Advance Acquisition ROW Tasks	0%	1 day?	Tue 6/22/21	
36	2.20	RW	2RW2		Prepare ROW Cost Estimate	0%	1 day?	Fri 6/18/21	
37	2.21	PM			Request ROW Funds	0%	1 day?	Mon 6/21/21	
38	2.22	UT	2UT1		Initiate Utility Coordination	0%	1 day?	Fri 6/18/21	
39	2.23	UT	2UT2		Prepare Utility Relocation and Construction Estimates	0%	1 day?	Fri 6/18/21	
40	2.24	PM			Request Utility Funds	0%	1 day?	Mon 6/21/21	
41	2.25	SG	2SG1		Initiate Signal and ITS Design	0%	1 day?	Tue 6/22/21	
42	2.26	TS	2TS1		Complete Safety Analysis & Operational Review	0%	1 day?	Fri 6/18/21	
43	2.27	SD	2SD1		Initiate Signing and Delineation Design	0%	1 day?	Tue 6/22/21	
44	2.28	IM	2IM1		Verify Complete Streets	0%	1 day?	Tue 6/22/21	
45	2.29	RE	2RE1		Initiate Erosion and Sediment Control Plans	0%	1 day?	Tue 6/22/21	
46	2.30	PI	2PI1		Continue Public Engagement	0%	1 day?	Fri 6/18/21	
47	2.31	CG	2CG1		Assist with Public Engagement	0%	1 day?	Mon 6/21/21	
48	2.32	VM	2VM1		Complete CR-RAVE Studies/Reviews and CLEAR Activities	0%	1 day?	Fri 6/18/21	
49	2.33	CS	2CS1		Prepare Initial Design Estimates	0%	1 day?	Thu 6/24/21	
50	2.34	RD	2RD2		Prepare for Field Inspection	0%	1 day?	Fri 6/25/21	
51	2.35	MLSN	MLSN	M1006 & #	Field Inspection & Environ. Document Complete	0%	0 days	Fri 6/25/21	

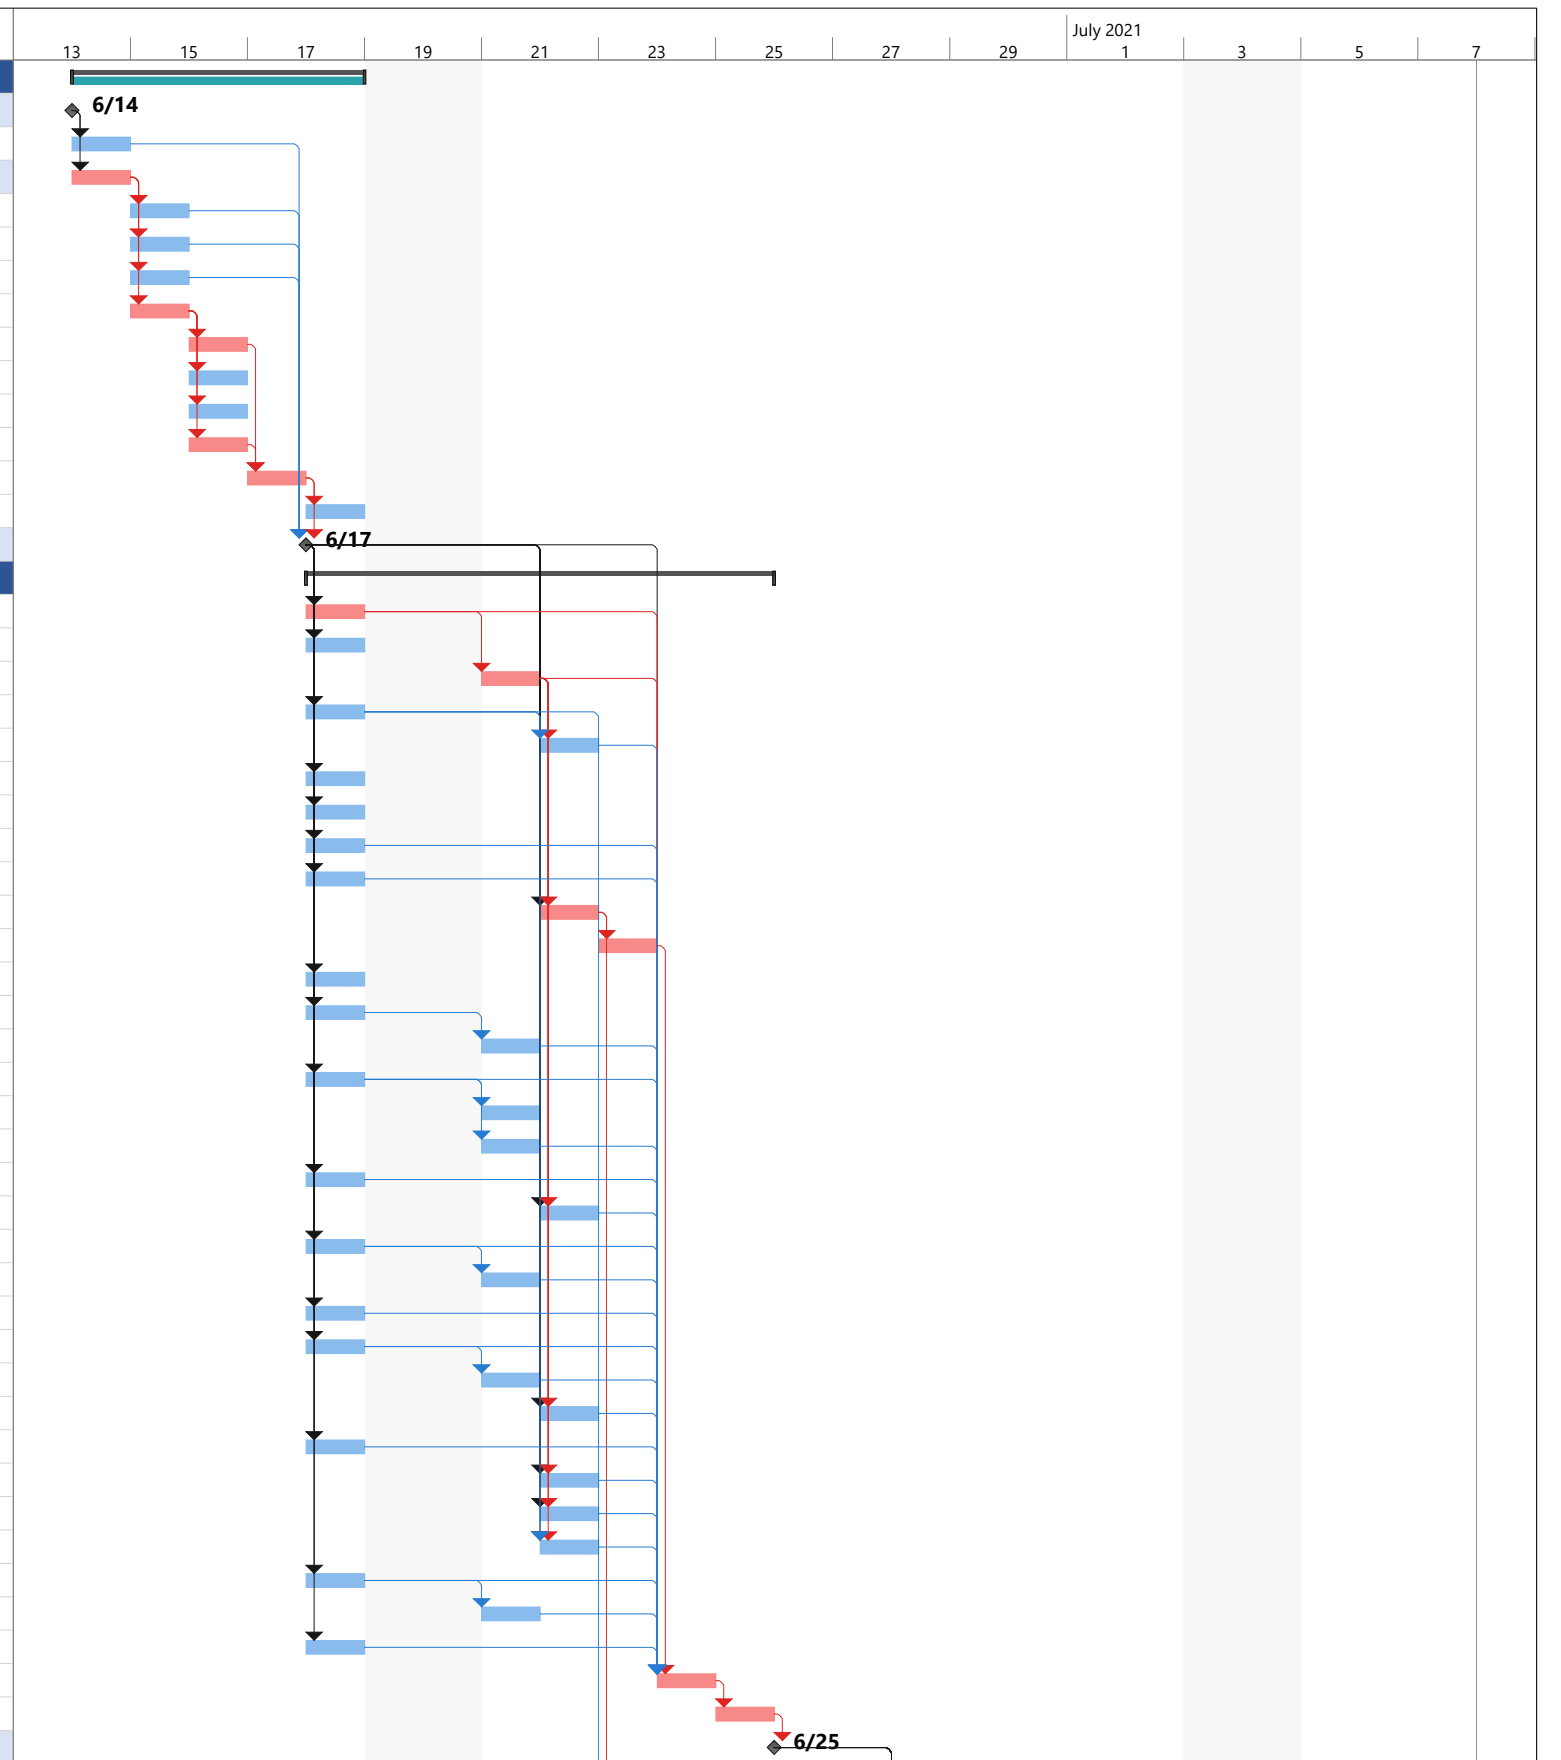

Project: NCDOT PDN 2 Schedu  
Date: Wed 6/9/21

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress	

ID	WBS	Discipline Code	Task Code	SAP MLSN	Task Name	% Complete	Duration	Start	July 2021													
									13	15	17	19	21	23	25	27	29	1	3	5	7	
52	3		3		<b>Plan-in-Hand (Stg 3)</b>	0%	6 days?	Wed 6/23/21														
53	3.1	RD	3RD1		Complete Roadway Design	0%	1 day?	Mon 6/28/21														
54	3.2	PD	3PD1		Verify Pavement Design	0%	1 day?	Mon 6/28/21														
55	3.3	LS	3LS1		Complete Additional Surveys and Initiate ROW Acquisition Su	0%	1 day?	Mon 6/28/21														
56	3.4	TM	3TM1		Complete Transportation Management Plan	0%	1 day?	Mon 6/28/21														
57	3.5	TO	3TO1		Advance Transportation Operations Plan (if a Significant Proj)	0%	1 day?	Mon 6/28/21														
58	3.6	SS	3SS1		Initiate Signal System Timing (if not a Significant Project)	0%	1 day?	Tue 6/29/21														
59	3.7	EP	3EP1		Complete Right-of-Way Consultation	0%	1 day?	Mon 6/28/21														
60	3.8	RW	3RW1		Prepare ROW Cost Estimate	0%	1 day?	Mon 6/28/21														
61	3.9	RW	3RW2		Complete ROW Authorization Package	0%	1 day?	Tue 6/29/21														
62	3.10	UT	3UT1		Advance Utility Coordination	0%	1 day?	Mon 6/28/21														
63	3.11	UT	3UT2		Prepare Utility Relocation and Construction Estimates	0%	1 day?	Mon 6/28/21														
64	3.12	GT	3GT1		Prepare GeoEnvironmental Phase II Report	0%	1 day?	Mon 6/28/21														
65	3.13	GT	3GT2		Conduct Subsurface Investigations & Provide Structures Recc	0%	1 day?	Wed 6/23/21														
66	3.14	ST	3ST1		Complete Structures Design	0%	1 day?	Mon 6/28/21														
67	3.15	SG	3SG1		Complete Signal and ITS Design	0%	1 day?	Mon 6/28/21														
68	3.16	SD	3SD1		Complete Signing and Delineation Design	0%	1 day?	Mon 6/28/21														
69	3.17	HY	3HY1		Complete Hydraulic Design	0%	1 day?	Mon 6/28/21														
70	3.18	RR	3RR1		Complete Railroad Design & Agreements	0%	1 day?	Mon 6/28/21														
71	3.19	RE	3RE1		Complete Erosion and Sediment Control Plans	0%	1 day?	Mon 6/28/21														
72	3.20	EN	3EN1		Complete Permit, Commitments, and Design Noise Report or	0%	1 day?	Mon 6/28/21														
73	3.21	EN	3EN2		Determine Final Noise Abatement	0%	1 day?	Tue 6/29/21														
74	3.22	VM	3VM1		Incorporate CR-RAVE Outcomes and Complete CLEAR Activiti	0%	1 day?	Mon 6/28/21														
75	3.23	CS	3CS1		Prepare Plan-in-Hand Estimates	0%	1 day?	Wed 6/30/21														
76	3.24	MLSN	MLSN	M1007	<b>Design Complete &amp; All Permit Applications Submitted</b>	0%	0 days	Wed 6/30/21														
77	4		4		<b>Plans, Specifications, and Estimates (Stage 4)</b>	0%	5 days?	Thu 7/1/21														
78	4.1	RW	4RW1		<b>Complete ROW Acquisitions and Relocations</b>	0%	1 day?	Thu 7/1/21														
79	4.1.1	RW	4RW1		Request ROW Certification	0%	1 day?	Thu 7/1/21														
80	4.2	GT	4GT1		Prepare GeoEnvironmental Phase III Reports	0%	1 day?	Thu 7/1/21														
81	4.3	ST	4ST1		Finalize Structures Design PS&E	0%	1 day?	Thu 7/1/21														
82	4.4	LS	4LS1		Complete ROW Acquisition Surveys	0%	1 day?	Thu 7/1/21														
83	4.5	HY	4HY1		Complete Any Open Hydraulic Tasks	0%	1 day?	Thu 7/1/21														
84	4.6	RE	4RE1		Finalize Erosion and Sediment Control Contract Package	0%	1 day?	Thu 7/1/21														
85	4.7	EP	4EP1		Complete Construction Consultation	0%	1 day?	Thu 7/1/21														
86	4.8	UT	4UT1		Complete Utility Coordination	0%	1 day?	Thu 7/1/21														
87	4.9	UT	4UT2		Complete Utility Relocation by Owner	0%	1 day?	Thu 7/1/21														
88	4.10	UT	4UT3		Prepare Final Utility Construction Estimates	0%	1 day?	Thu 7/1/21														
89	4.11	TO	4TO1		Complete Transportation Operations Plan-Related Tasks (if a	0%	1 day?	Thu 7/1/21														
90	4.12	VM	4WM1		Complete CR-RAVE and CLEAR Activities	0%	1 day?	Thu 7/1/21														
91	4.13	EN	4EN1		Secure Environmental Permits	0%	1 day?	Thu 7/1/21														
92	4.14	RR	4RR1		Complete Railroad Coordination	0%	1 day?	Thu 7/1/21														
93	4.15	CG	4CG1		Prepare Construction Communication Activities	0%	1 day?	Thu 7/1/21														
94	4.16	PM			Request Construction Funds	0%	1 day?	Thu 7/1/21														
95	4.17	RD	4RD1		Finalize the Final PS&E Package	0%	1 day?	Fri 7/2/21														
96	4.18	CS	4CS1		Complete PS&E Package and Advertise the Project	0%	1 day?	Mon 7/5/21														
97	4.19	MLSN	MLSN	M1008	<b>Let Project</b>	0%	0 days	Mon 7/5/21														
98	4.20	CS	4CS2		Let, Award and Execute	0%	1 day?	Tue 7/6/21														
99	4.21				Post-Letting Activities	0%	1 day?	Wed 7/7/21														

Project: NCDOT PDN 2 Schedu  
Date: Wed 6/9/21

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress	

Page 2
