

ID	WBS	Discipline Code	Task Code	SAP MLSN	Task Name	% Complete	Duration	Start	Jun 13, '21	Jun 20, '21	Jun 27, '21	Jul 4, '21	Jul 11, '21																				
									M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T
1	1				PDN Schedule Template - released 12.2021	0%	1 day?	Mon 6/14/21																									
2	2		1		Project Initiation (Stg 1)	0%	5 days?	Mon 6/14/21																									
3	2.1	MLSN	MLSN		Final STIP	0%	0 days	Mon 6/14/21																									
4	2.2	EN	1EN1		Initiate Environmental Analysis	0%	3 days?	Tue 6/15/21																									
5	2.2.1	EN	1EN1		Comments on Draft Scoping Report	0%	1 day?	Tue 6/15/21																									
6	2.2.2	EN	1EN1		Complete ETRACS and Other Requests	0%	1 day?	Thu 6/17/21																									
7	2.2.3	EN	1EN1		Landowner Letters	0%	1 day?	Thu 6/17/21																									
8	2.2.4	EN	1EN1		Cultural Resources Programmatic Agreement Cultural Resources Screening Checklist for Section 106	0%	1 day?	Thu 6/17/21																									
9	2.2.5	EN	1EN1		Traffic Noise and Air Quality (TNAQ) Notification Scoping Report Recommendations	0%	1 day?	Thu 6/17/21																									
10	2.2.6	EN	1EN1		Community Screening	0%	1 day?	Thu 6/17/21																									
11	2.3	PH	1PH2		Compile Aerial Photography & Mapping	0%	6 days?	Mon 6/14/21																									
12	2.3.1	PH	1PH2		Controlled Aerial Photography	0%	1 day?	Mon 6/14/21																									
13	2.3.2	PH	1PH2		Large Scale Planimetric Mapping	0%	1 day?	Fri 6/18/21																									
14	2.3.3	PH	1PH2		Elevation Data	0%	1 day?	Fri 6/18/21																									
15	2.3.4	PH	1PH2		Digital Mosaic	0%	1 day?	Fri 6/18/21																									
16	2.3.5	PH	1PH2		Airborne Survey Report	0%	1 day?	Mon 6/21/21																									
17	2.4	VM	1VM1		Initiate CR-RAVE, CLEAR and Value Assessment Activities	0%	5 days?	Tue 6/15/21																									
18	2.4.1	VM	1VM1		Constructability Review Checklist	0%	1 day?	Tue 6/15/21																									
19	2.4.2	VM	1VM1		Risk Assessment Worksheet	0%	1 day?	Thu 6/17/21																									
20	2.4.3	VM	1VM1		Risk Assessment Study	0%	1 day?	Fri 6/18/21																									
21	2.4.4	VM	1VM1		Value Engineering (VE) Checklist	0%	1 day?	Fri 6/18/21																									
22	2.4.5	VM	1VM1		Value Engineering (VE) Schedule	0%	1 day?	Mon 6/21/21																									
23	2.4.6	VM	1VM1		CLEAR Database Search	0%	1 day?	Fri 6/18/21																									
24	2.4.7	VM	1VM1		Value Assessment	0%	1 day?	Wed 6/16/21																									
25	2.4.8	VM	1VM1		Value Assessment Worksheet	0%	1 day?	Thu 6/17/21																									
26	2.5	UT	1UT2		Initiate Utility Investigations	0%	3 days?	Tue 6/15/21																									
27	2.5.1	UT	1UT2		Utility Risk Analysis and Inventory Report	0%	1 day?	Tue 6/15/21																									
28	2.5.2	UT	1UT2		Utility Project Outline	0%	1 day?	Wed 6/16/21																									
29	2.5.3	UT	1UT2		Utility Construction Requests	0%	1 day?	Thu 6/17/21																									
30	2.6	PI	1PI1		Initiate Public Engagement Tasks	0%	5 days?	Mon 6/14/21																									
31	2.6.1	PI	1PI1		RPO/MPO CTP/LRTP Outreach Documentation	0%	1 day?	Mon 6/14/21																									
32	2.6.2	PI	1PI1		Public Involvement Plan (PIP)	0%	1 day?	Fri 6/18/21																									
33	2.7	CG	1CG1		Review Project Scoping	0%	1 day?	Tue 6/15/21																									
34	2.7.1	CG	1CG1		Project Scoping Report Review Comments	0%	1 day?	Tue 6/15/21																									
35	2.8	LS	1LS1		Provide Photogrammetric Control & Initiate Survey	0%	3 days?	Tue 6/15/21																									
36	2.8.1	LS	1LS1		Photogrammetric Control for Preliminary/Planning Mapping (NC Grid Datum)	0%	1 day?	Tue 6/15/21																									
37	2.8.2	LS	1LS1		SUE Level D Mapping	0%	1 day?	Wed 6/16/21																									
38	2.8.3	LS	1LS1		Final Mapping Limits Polygon	0%	1 day?	Wed 6/16/21																									
39	2.8.4	LS	1LS1		Photogrammetric Control for Final Survey Mapping (Local Datum)	0%	1 day?	Thu 6/17/21																									
40	2.9	GT	1GT1		Complete Geotechnical & GeoEnvironmental Screening	0%	4 days?	Mon 6/14/21																									
41	2.9.1	GT	1GT1		Geotechnical Input on Express Design	0%	1 day?	Mon 6/14/21																									
42	2.9.2	GT	1GT1		Geotechnical Report for Planning	0%	1 day?	Tue 6/15/21																									
43	2.9.3	GT	1GT1		GeoEnvironmental Scoping Comments Report	0%	1 day?	Thu 6/17/21																									
44	2.10	EP	1EP1		Initiate Environmental Review	0%	5 days?	Tue 6/15/21																									
45	2.10.1	EP	1EP1		Merger Pre-Screening Review	0%	1 day?	Tue 6/15/21																									
46	2.10.2	EP	1EP1		Merger Screening	0%	1 day?	Wed 6/16/21																									
47	2.10.3	EP	1EP1		Merger Plan (if needed)	0%	1 day?	Thu 6/17/21																									

Project: NCDOT PDN 2 Schedu
Date: Mon 4/3/23

Task █ Summary

Split ⋯ Project Summary

Milestone ◆ Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone ◆


Deadline ↓

Critical █


Critical Split ⋯


Progress █

Manual Progress █

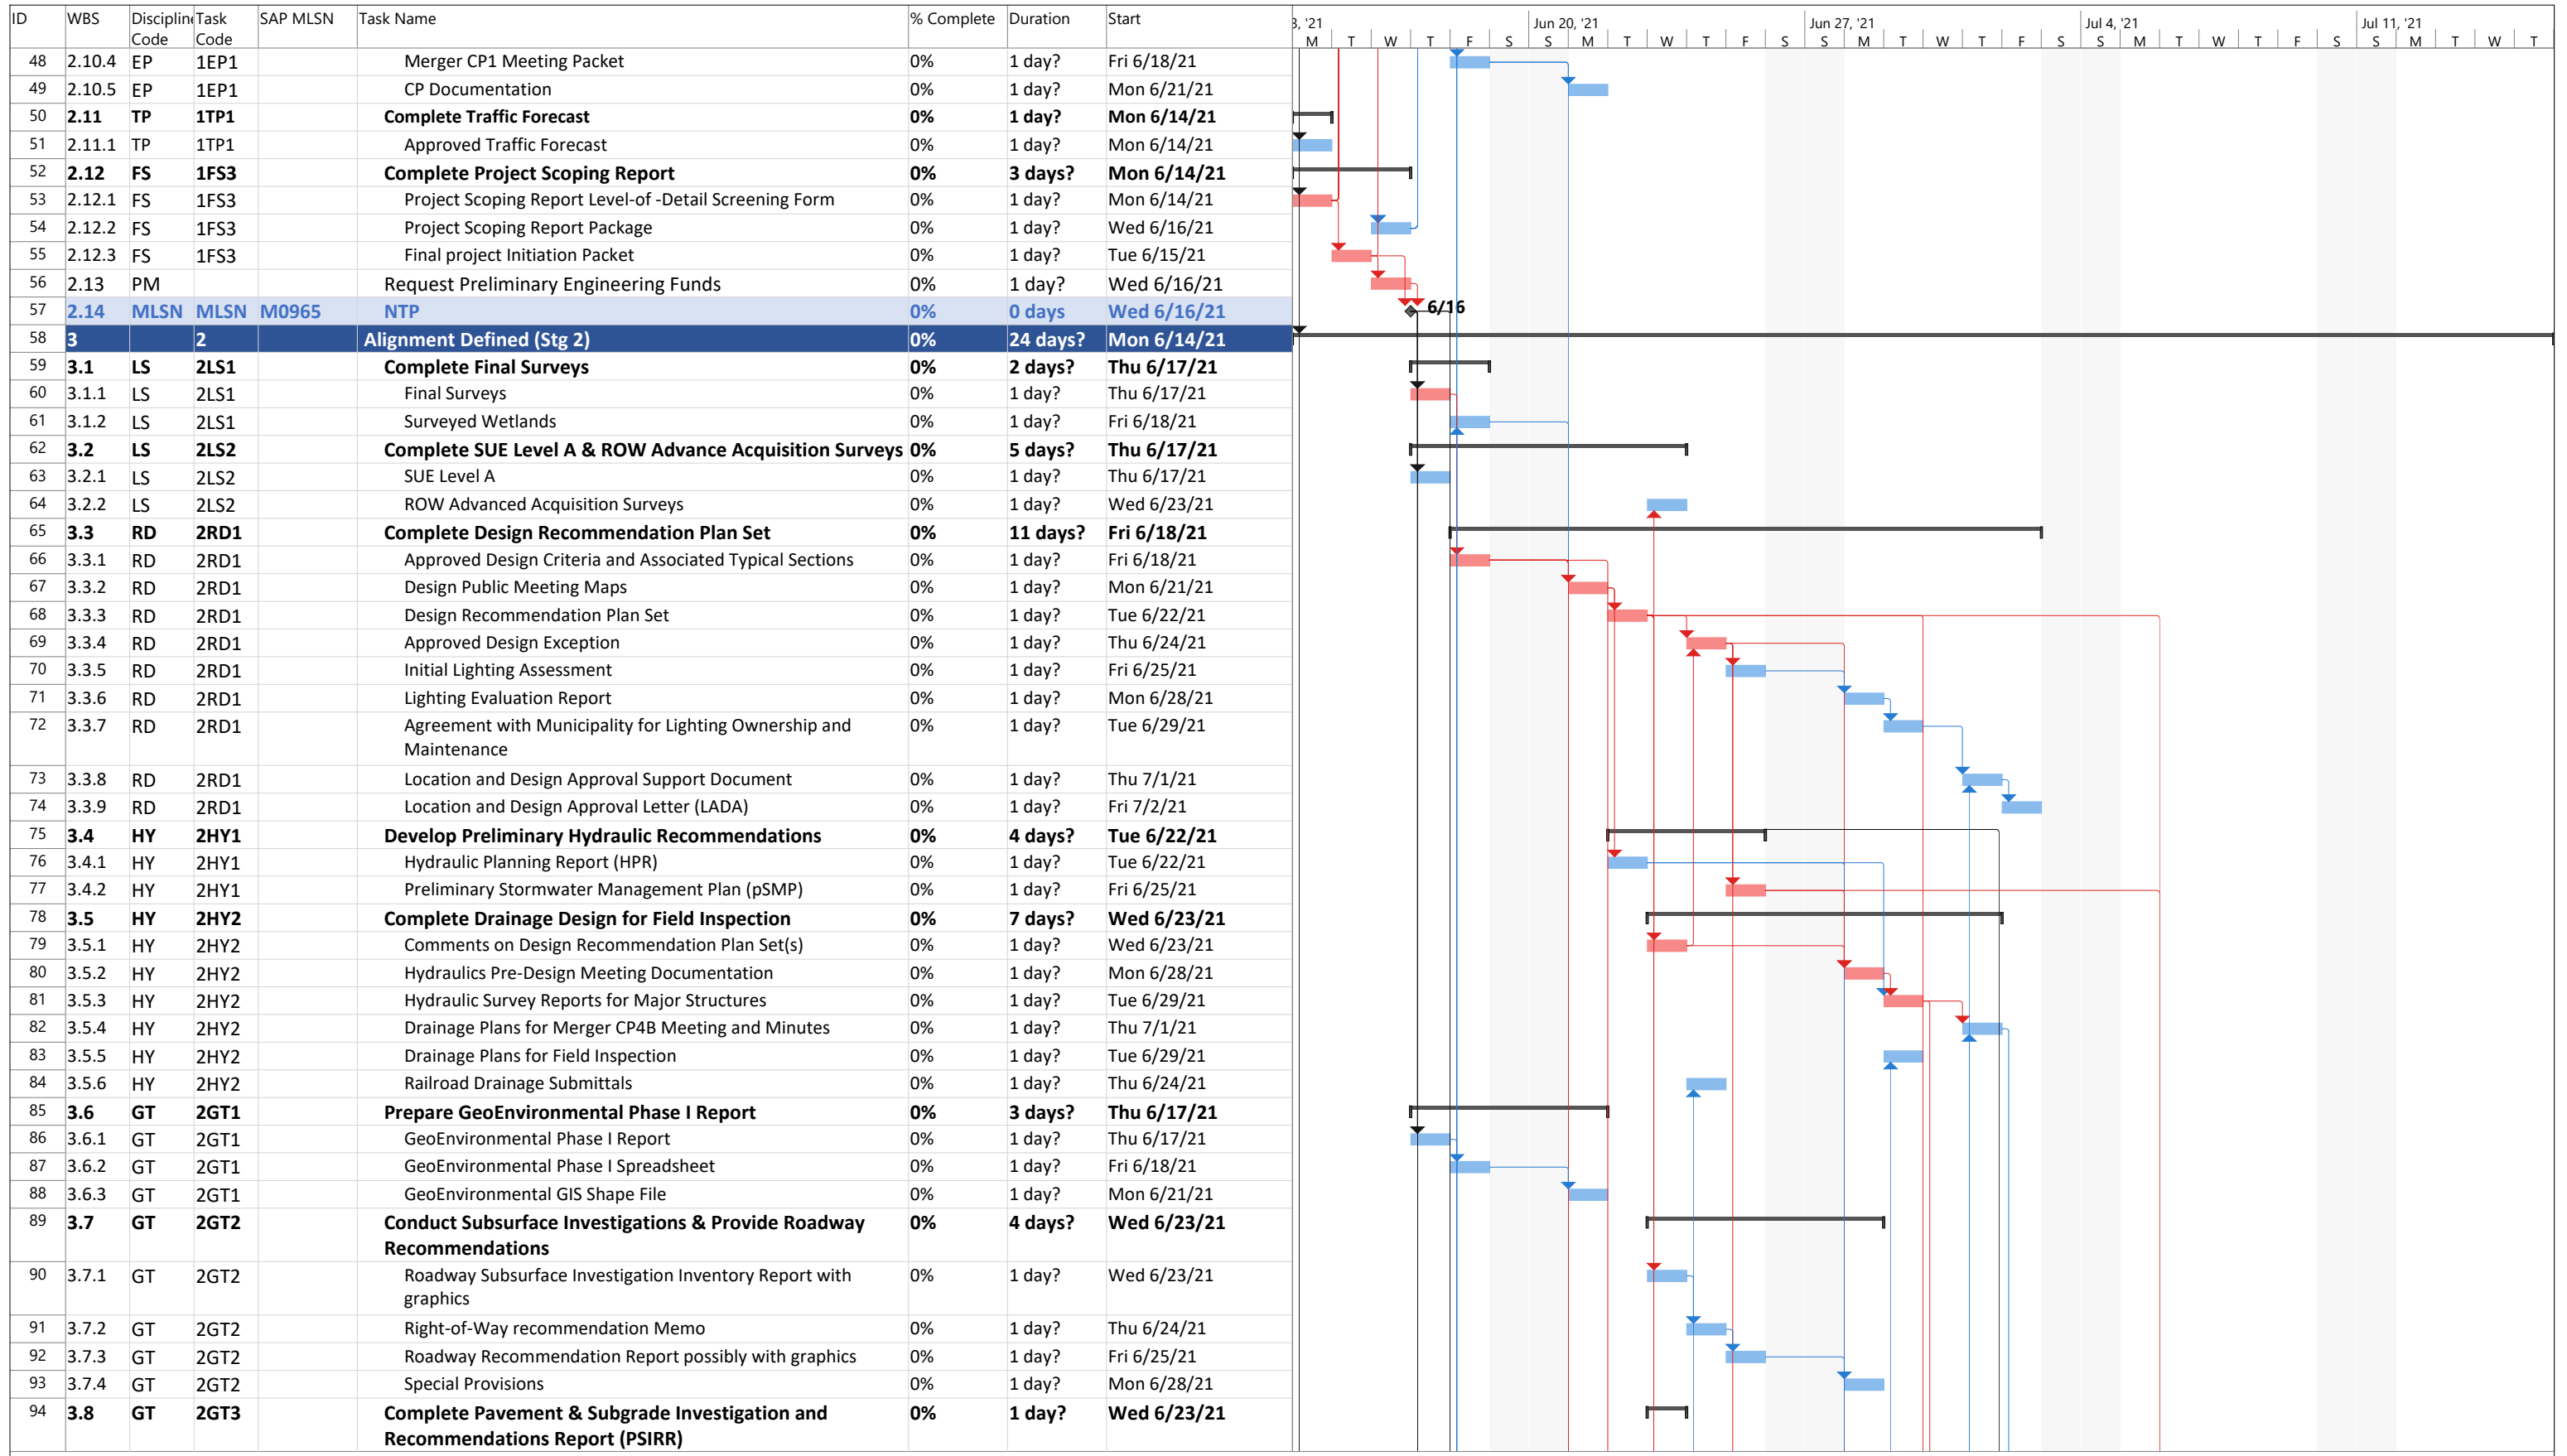

Project: NCDOT PDN 2 Schedu
Date: Mon 4/3/23



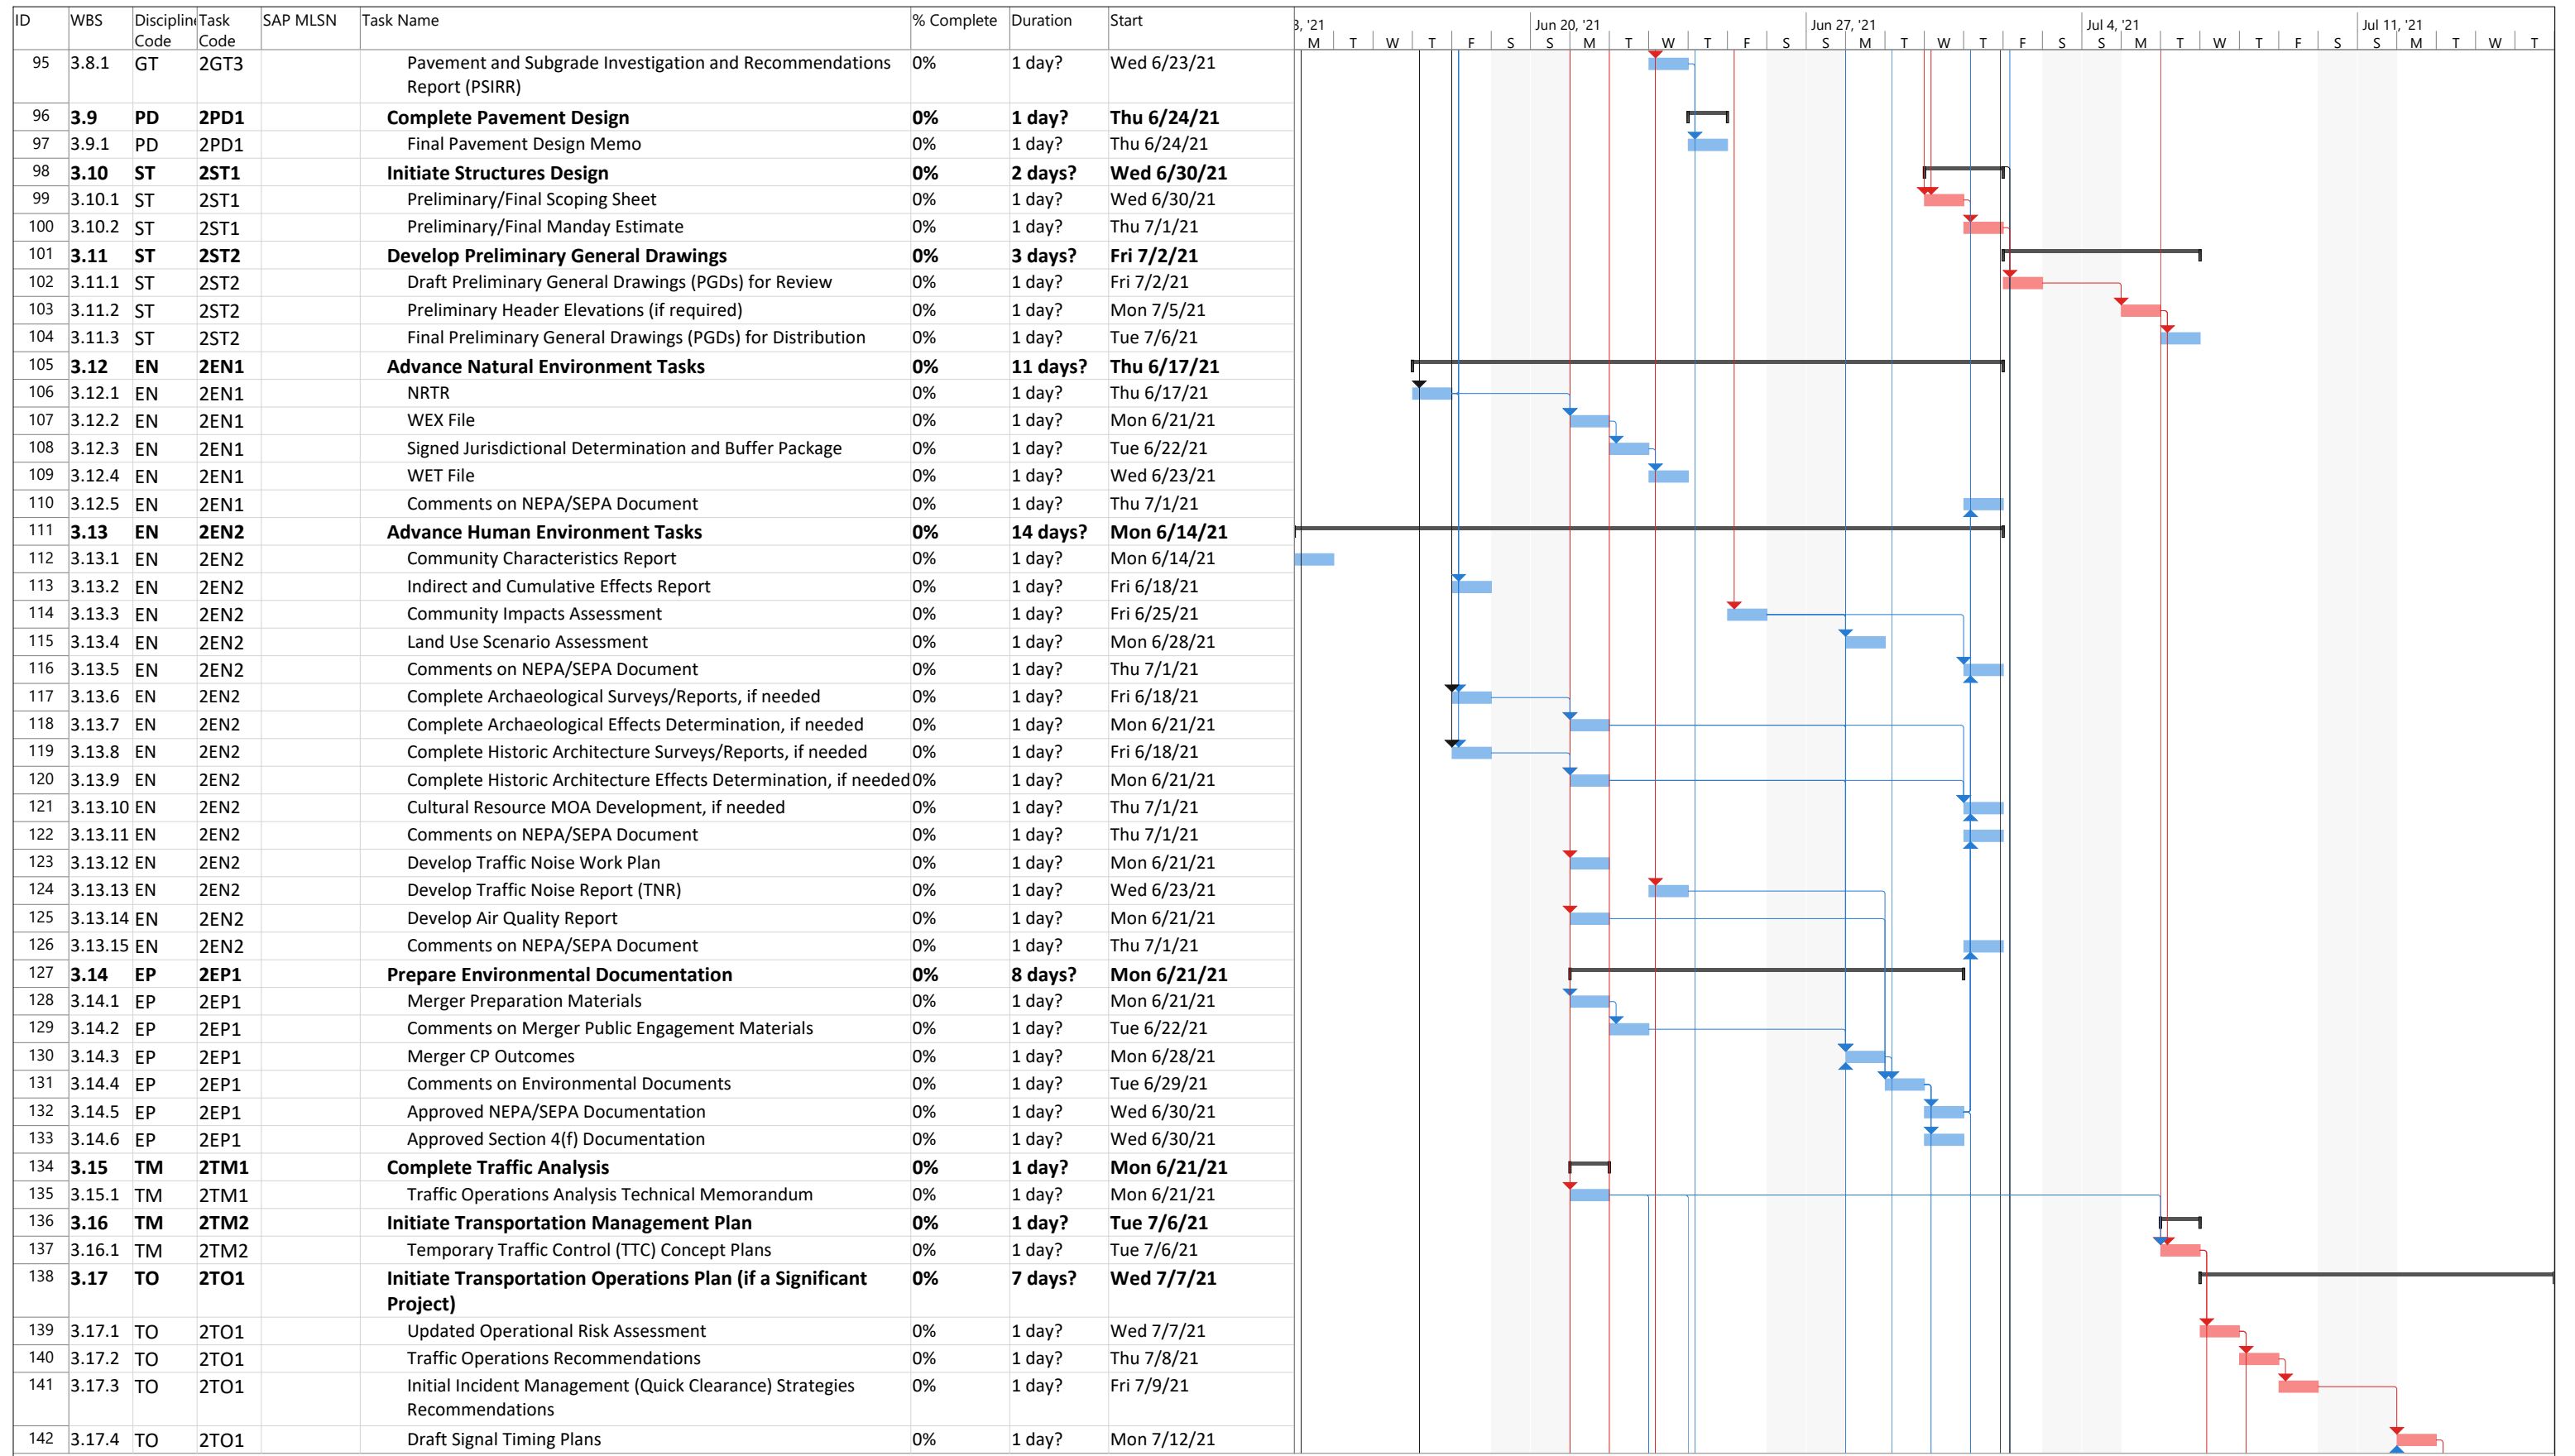

Project: NCDOT PDN 2 Schedu
Date: Mon 4/3/23



ID	WBS	Discipline Code	Task Code	SAP MLSN	Task Name	% Complete	Duration	Start	Jun 18, '21							Jun 20, '21							Jun 27, '21							Jul 4, '21							Jul 11, '21						
									M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T			
143	3.17.5	TO	2TO1		Integrated Corridor Management Decision Matrix	0%	1 day?	Tue 7/13/21																																			
144	3.17.6	TO	2TO1		List of Smart Work zone Equipment	0%	1 day?	Wed 7/14/21																																			
145	3.17.7	TO	2TO1		Updated cost estimate	0%	1 day?	Thu 7/15/21																																			
146	3.17.8	TO	2TO1		Initial Stakeholder Meeting Minutes	0%	1 day?	Thu 7/8/21																																			
147	3.18	RR	2RR1		Initiate Railroad Review	0%	5 days?	Mon 6/21/21																																			
148	3.18.1	RR	2RR1		Railroad Design Line and Grade	0%	1 day?	Mon 6/21/21																																			
149	3.18.2	RR	2RR1		Railroad PE Agreement	0%	1 day?	Fri 6/25/21																																			
150	3.18.3	RR	2RR1		Roadway Plans for Rail Review	0%	1 day?	Wed 6/23/21																																			
151	3.18.4	RR	2RR1		Crossing Scope for Off-Site Detour	0%	1 day?	Thu 6/24/21																																			
152	3.19	RW	2RW1		Initiate Advance Acquisition ROW Tasks	0%	2 days?	Wed 6/23/21																																			
153	3.19.1	RW	2RW1		Advance Acquisition Property Owner Contacts	0%	1 day?	Wed 6/23/21																																			
154	3.19.2	RW	2RW1		Advanced Acquisition ROW Authorization	0%	1 day?	Thu 6/24/21																																			
155	3.20	RW	2RW2		Prepare ROW Cost Estimate	0%	1 day?	Wed 6/23/21																																			
156	3.20.1	RW	2RW2		ROW Cost Estimate (PH 200)	0%	1 day?	Wed 6/23/21																																			
157	3.21	PM			Request ROW Funds	0%	1 day?	Thu 6/24/21																																			
158	3.22	UT	2UT1		Initiate Utility Coordination	0%	7 days?	Wed 6/23/21																																			
159	3.22.1	UT	2UT1		Utility Coordination Kickoff Meeting Minutes	0%	1 day?	Wed 6/23/21																																			
160	3.22.2	UT	2UT1		Routing Plan	0%	1 day?	Thu 6/24/21																																			
161	3.22.3	UT	2UT1		Relocation Schedule	0%	1 day?	Fri 6/25/21																																			
162	3.22.4	UT	2UT1		Preliminary Utility Construction Plans	0%	1 day?	Mon 6/28/21																																			
163	3.22.5	UT	2UT1		Subsurface Utility Engineering (SUE) Level A Request	0%	1 day?	Tue 6/29/21																																			
164	3.22.6	UT	2UT1		Geotechnical Investigation (Trenchless) Request	0%	1 day?	Wed 6/30/21																																			
165	3.22.7	UT	2UT1		Utility Easement Request and Utility Parcel List	0%	1 day?	Thu 7/1/21																																			
166	3.23	UT	2UT2		Prepare Utility Relocation and Construction Estimates	0%	2 days?	Fri 7/2/21																																			
167	3.23.1	UT	2UT2		Utility Relocation (PH 250) Estimate	0%	1 day?	Fri 7/2/21																																			
168	3.23.2	UT	2UT2		Utility Construction (PH 300) Estimate	0%	1 day?	Mon 7/5/21																																			
169	3.24	PM			Request Utility Funds	0%	1 day?	Tue 7/6/21																																			
170	3.25	SG	2SG1		Initiate Signal and ITS Design	0%	1 day?	Tue 6/29/21																																			
171	3.25.1	SG	2SG1		Signal Pole/Cabinet Location Diagrams	0%	1 day?	Tue 6/29/21																																			
172	3.26	TS	2TS1		Complete Safety Analysis & Operational Review	0%	11 days?	Wed 6/23/21																																			
173	3.26.1	TS	2TS1		Traffic Signal Recommendations	0%	1 day?	Wed 6/23/21																																			
174	3.26.2	TS	2TS1		Traffic Safety Alternatives Analysis Report	0%	1 day?	Thu 6/24/21																																			
175	3.26.3	TS	2TS1		Safety Data and Analysis for Environmental Document	0%	1 day?	Fri 6/25/21																																			
176	3.26.4	TS	2TS1		Roadway Plan Comment Memo	0%	1 day?	Mon 6/28/21																																			
177	3.26.5	TS	2TS1		Signing and Delineation Plan Comment Memo	0%	1 day?	Tue 6/29/21																																			
178	3.26.6	TS	2TS1		Comments on the Transportation Management Plan (TMP) and temporary traffic control (TTC) plans	0%	1 day?	Wed 7/7/21																																			
179	3.27	SD	2SD1		Initiate Signing and Delineation Design	0%	3 days?	Wed 6/23/21																																			
180	3.27.1	SD	2SD1		Preliminary Signing and Delineation Strip Map	0%	1 day?	Wed 6/23/21																																			
181	3.27.2	SD	2SD1		Document Conflicts	0%	1 day?	Thu 6/24/21																																			
182	3.27.3	SD	2SD1		Plan Submittals	0%	1 day?	Fri 6/25/21																																			
183	3.28	IM	2IM1		Verify Complete Streets	0%	1 day?	Mon 6/21/21																																			
184	3.28.1	IM	2IM1		Integrated Mobility Division Concurrence Review Memo	0%	1 day?	Mon 6/21/21																																			
185	3.29	RE	2RE1		Initiate Erosion and Sediment Control Plans	0%	9 days?	Wed 6/23/21																																			
186	3.29.1	RE	2RE1		Water Quality Worksheet (Form ESC-1)	0%	1 day?	Wed 6/23/21																																			
187	3.29.2	RE	2RE1		Environmental Document Review (Form ESC-2)	0%	1 day?	Wed 6/30/21																																			
188	3.29.3	RE	2RE1		Pre-Design Meeting Minutes	0%	1 day?	Thu 7/1/21																																			
189	3.29.4	RE	2RE1		E&SC Field Inspection Plans	0%	1 day?	Fri 7/2/21																																			
190	3.29.5	RE	2RE1		ROW/Easement Request File	0%	1 day?	Mon 7/5/21																																			
191	3.30	PI	2PI1		Continue Public Engagement	0%	5 days?	Thu 6/17/21																																			
192	3.30.1	PI	2PI1		Public Involvement plan (PIP)	0%	1 day?	Thu 6/17/21																																			


Project: NCDOT PDN 2 Schedu
Date: Mon 4/3/23

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress

ID	WBS	Discipline Code	Task Code	SAP MLSN	Task Name	% Complete	Duration	Start	3, '21	Jun 20, '21	Jun 27, '21	Jul 4, '21	Jul 11, '21
193	3.30.2	PI	2PI1		Scoping Letter	0%	1 day?	Thu 6/17/21					
194	3.30.3	PI	2PI1		Mailing List	0%	1 day?	Fri 6/18/21					
195	3.30.4	PI	2PI1		Public Outreach Materials	0%	1 day?	Mon 6/21/21					
196	3.30.5	PI	2PI1		Newsletter/Postcard Approval	0%	1 day?	Tue 6/22/21					
197	3.30.8	PI	2PI1		Public Meeting/Public Hearings	0%	1 day?	Tue 6/22/21					
198	3.30.7	PI	2PI1		Environmental Document Comments	0%	1 day?	Wed 6/23/21					
199	3.31	CG	2CG1		Assist with Public Engagement	0%	1 day?	Fri 6/18/21					
200	3.32	CG	2CG1		Various Outreach Materials	0%	1 day?	Mon 6/21/21					
201	3.33	CG	2CG1		Project Special Commitments (Green Sheets) (when applicable)	0%	1 day?	Thu 7/1/21					
202	3.34	VM	2VM1		Complete CR-RAVE Studies/Reviews, CLEAR, and Conduct Value Assessment Activities	0%	10 days?	Thu 6/17/21					
203	3.34.1	VM	2VM1		Constructability Review checklist	0%	1 day?	Thu 6/17/21					
204	3.34.2	VM	2VM1		Constructability Review Minutes/CR Log	0%	1 day?	Fri 6/18/21					
205	3.34.3	VM	2VM1		Risk Assessment Worksheet	0%	1 day?	Mon 6/21/21					
206	3.34.4	VM	2VM1		Risk Assessment Study	0%	1 day?	Tue 6/22/21					
207	3.34.5	VM	2VM1		Value Assessment	0%	1 day?	Tue 6/22/21					
208	3.34.6	VM	2VM1		Value Assessment Worksheet	0%	1 day?	Wed 6/23/21					
209	3.34.7	VM	2VM1		Value Engineering (VE) Study Report	0%	1 day?	Thu 6/24/21					
210	3.34.8	VM	2VM1		Value Engineering (VE) Study Recommendations	0%	1 day?	Fri 6/25/21					
211	3.34.9	VM	2VM1		Final Dispositions (responses to recommendations)	0%	1 day?	Tue 6/29/21					
212	3.34.10	VM	2VM1		CLEAR Database Search	0%	1 day?	Wed 6/30/21					
213	3.35	CS	2CS1		Prepare Initial Design Estimates	0%	2 days?	Wed 6/30/21					
214	3.35.1	CS	2CS1		Construction Cost Estimate	0%	1 day?	Wed 6/30/21					
215	3.35.2	CS	2CS1		Cost Verification Letter	0%	1 day?	Thu 7/1/21					
216	3.36	RD	2RD2		Prepare for Field Inspection	0%	2 days?	Mon 6/28/21					
217	3.36.1	RD	2RD2		Field Inspection Plan Set	0%	1 day?	Mon 6/28/21					
218	3.36.2	RD	2RD2		Quantities for Construction Estimate	0%	1 day?	Tue 6/29/21					
219	3.37	MLSN	MLSN	M1006 & # based on Env Doc Type	Field Inspection & Environ. Document Complete	0%	0 days	Wed 6/30/21					
220	4		3		Plan-in-Hand (Stg 3)	0%	3 days?	Wed 6/30/21					
221	4.1	MLSN	MLSN	M0300	Right of Way Plans Complete (RPC)	0%	0 days	Wed 6/30/21					
222	4.2	RD	3RD1		Complete Roadway Design	0%	1 day?	Thu 7/1/21					
223	4.2.1	RD	3RD1		Right-of-Way Plan Set w/ Noise Wall Locations	0%	1 day?	Thu 7/1/21					
224	4.2.2	RD	3RD1		Quantities for Construction Estimate	0%	1 day?	Thu 7/1/21					
225	4.2.3	RD	3RD1		Roadway Design Plans Set for Permit Application	0%	1 day?	Thu 7/1/21					
226	4.2.4	RD	3RD1		Photometric Layout	0%	1 day?	Thu 7/1/21					
227	4.2.5	RD	3RD1		Lighting Plans Prepared in MicroStation	0%	1 day?	Thu 7/1/21					
228	4.2.6	RD	3RD1		Voltage Drop Calculations	0%	1 day?	Thu 7/1/21					
229	4.2.7	RD	3RD1		Typical Sections for Pavement Design Review	0%	1 day?	Thu 7/1/21					
230	4.3	PD	3PD1		Verify Pavement Design	0%	1 day?	Thu 7/1/21					
231	4.3.1	PD	3PD1		Final Pavement Design Verification Memo	0%	1 day?	Thu 7/1/21					
232	4.3.2	PD	3PD1		Typical section Review Email	0%	1 day?	Thu 7/1/21					
233	4.3.3	PD	3PD1		Shoulder Drain Memo	0%	1 day?	Thu 7/1/21					
234	4.4	LS	3LS1		Complete Additional Surveys and Initiate ROW Acquisition Surveys	0%	1 day?	Thu 7/1/21					
235	4.4.1	LS	3LS1		Additional Surveys	0%	1 day?	Thu 7/1/21					
236	4.5	TM	3TM1		Complete Transportation Management Plan	0%	1 day?	Thu 7/1/21					
237	4.5.1	TM	3TM1		Final Transportation Management Plan (TMP) Submittal	0%	1 day?	Thu 7/1/21					

Project: NCDOT PDN 2 Schedu
Date: Mon 4/3/23


Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress	

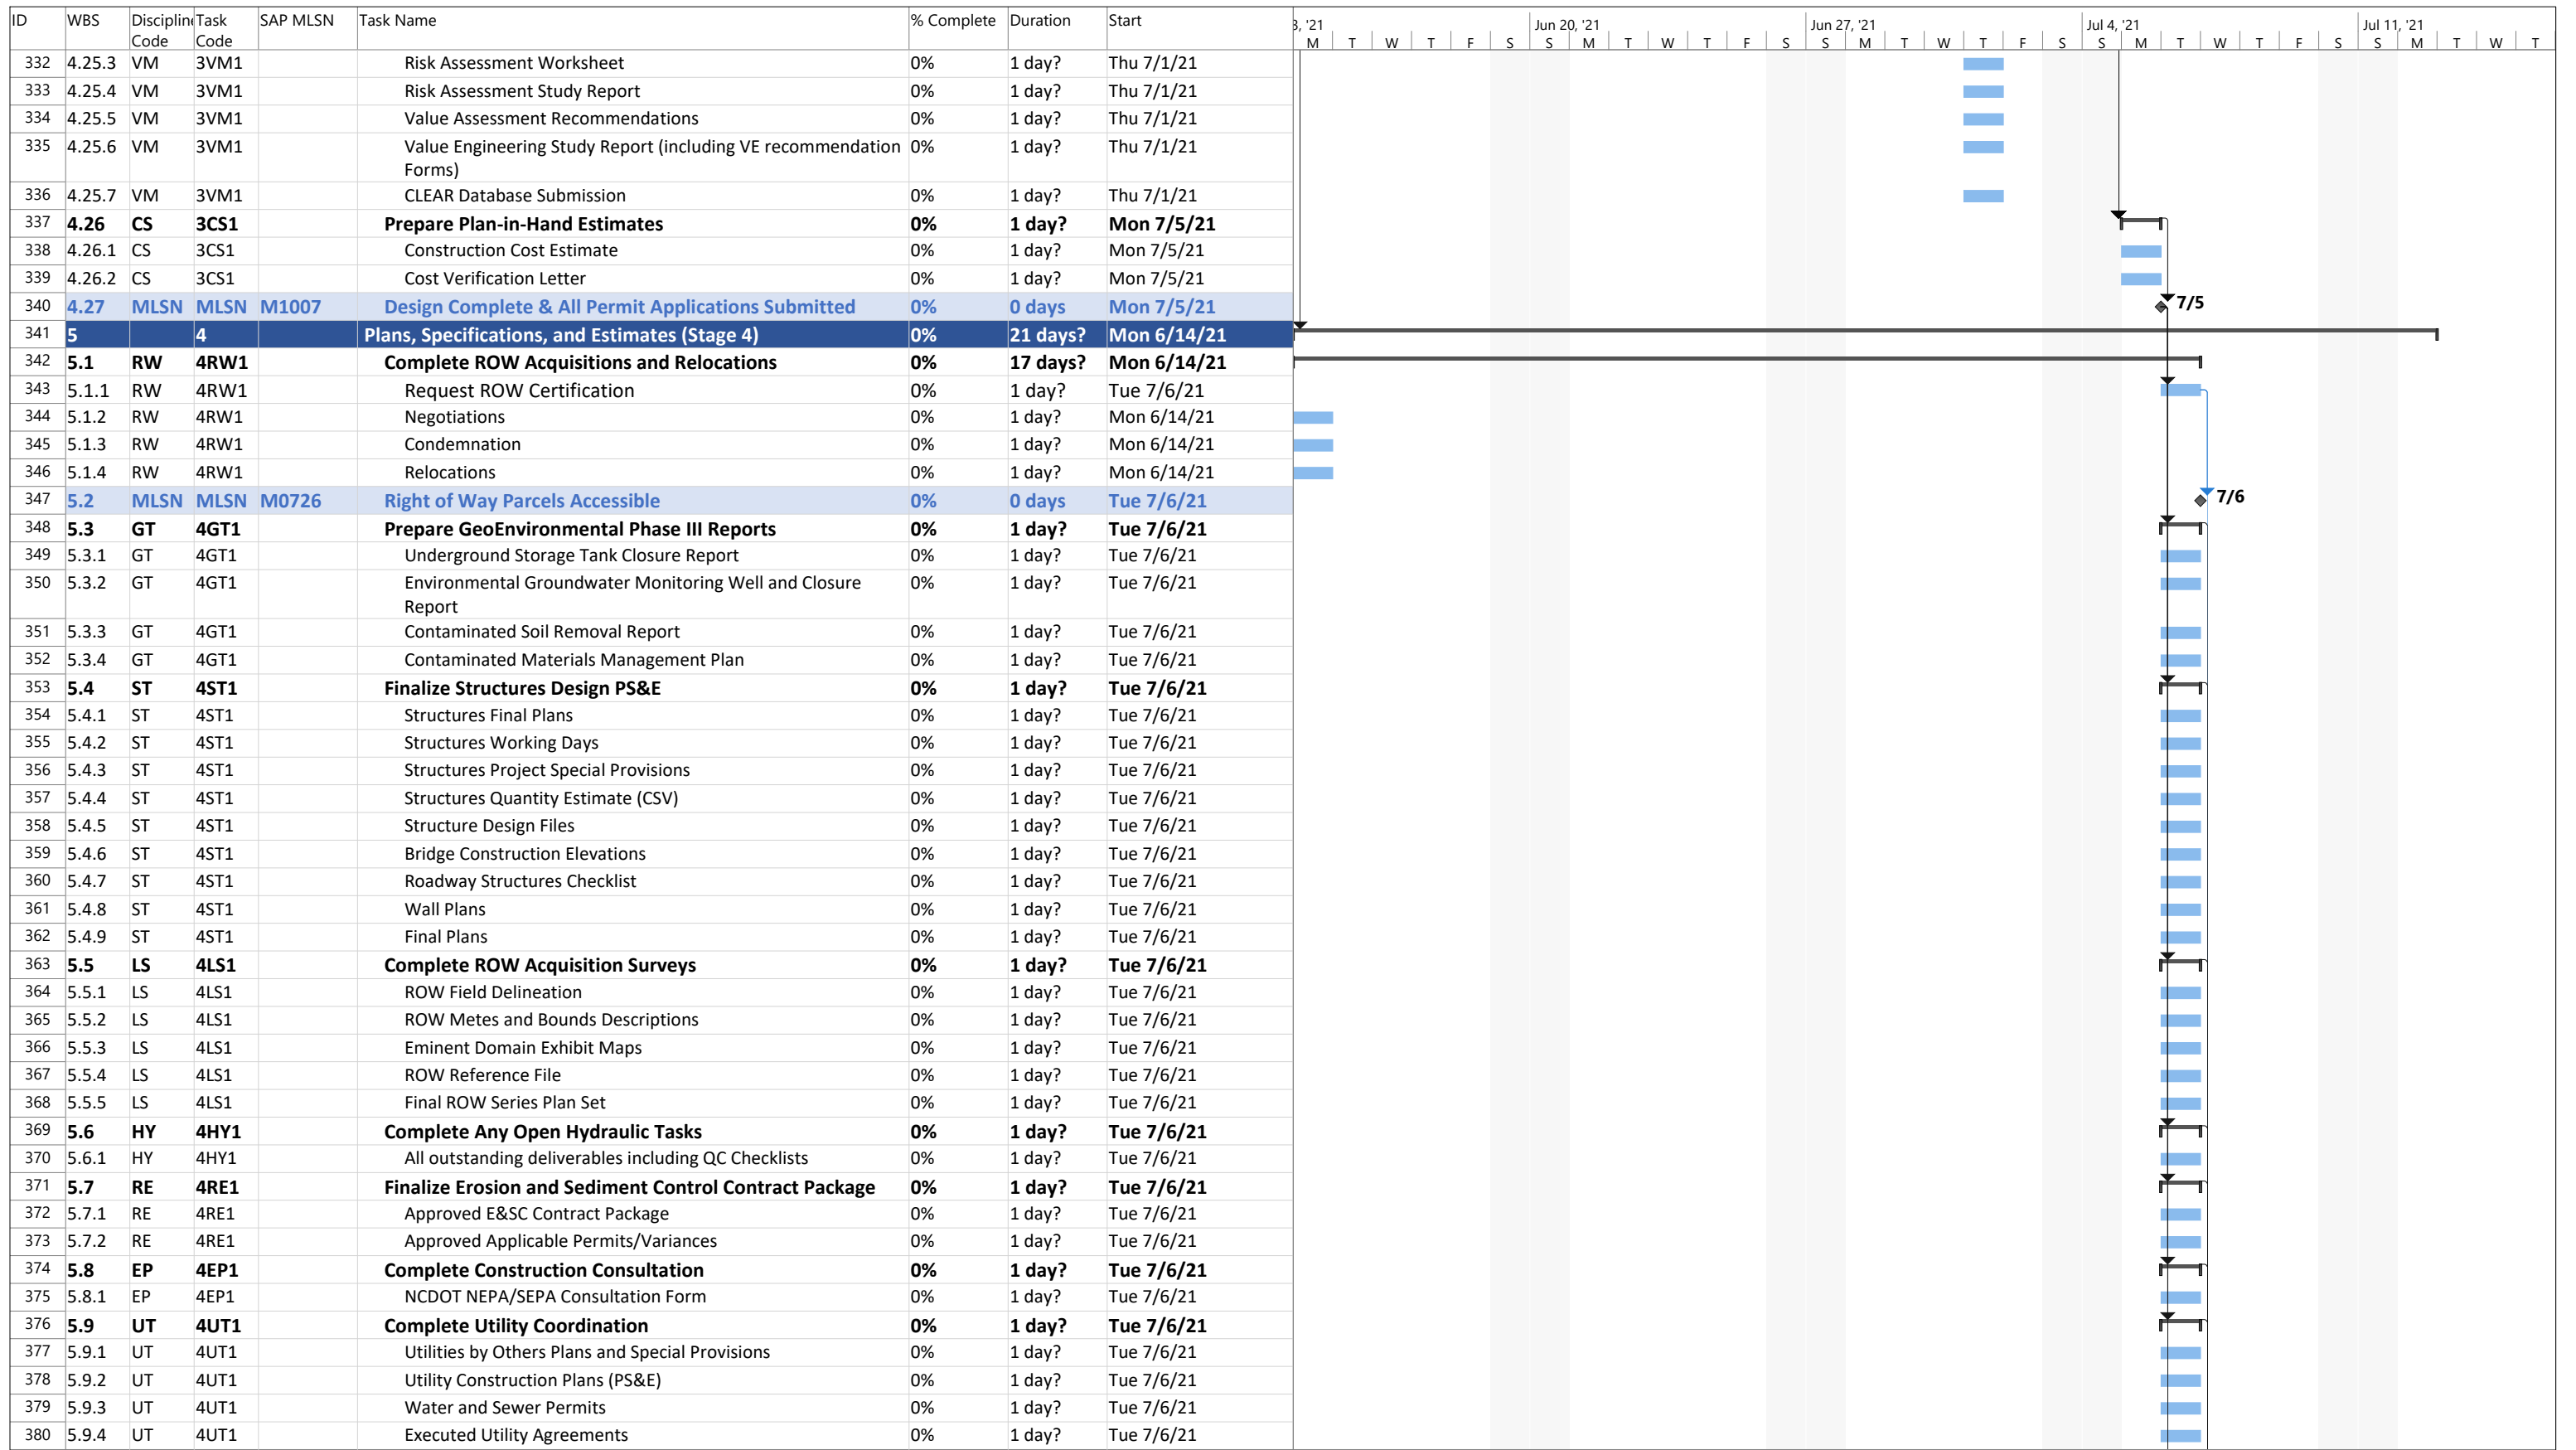

Project: NCDOT PDN 2 Schedu
Date: Mon 4/3/23

Task	Summary	Inactive Milestone	Inactive Summary	Manual Summary Rollup	Manual Summary	External Milestone	Critical Split	Critical
Split	Project Summary	Inactive Task	Manual Task	Finish-only	External Tasks	Deadline	Progress	Manual Progress
Milestone	Inactive Milestone					Critical		

ID	WBS	Discipline Code	Task Code	SAP MLSN	Task Name	% Complete	Duration	Start	Jun 19, '21	Jun 20, '21	Jun 27, '21	Jul 4, '21	Jul 11, '21															
									M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T		
381	5.9.5	UT	4UT1		Utility Authorizations	0%	1 day?	Tue 7/6/21																				
382	5.9.6	UT	4UT1		Utility Certifications	0%	1 day?	Tue 7/6/21																				
383	5.10	UT	4UT2		Complete Utility Relocation by Owner	0%	1 day?	Tue 7/6/21																				
384	5.10.1	UT	4UT2		Relocation Scheduling Conference	0%	1 day?	Tue 7/6/21																				
385	5.10.2	UT	4UT2		Updated Utilities Relocation Schedule	0%	1 day?	Tue 7/6/21																				
386	5.11	UT	4UT3		Prepare Final Utility Construction Estimates	0%	1 day?	Tue 7/6/21																				
387	5.11.1	UT	4UT3		Final Utility Construction (PH 300) Estimate	0%	1 day?	Tue 7/6/21																				
388	5.12	MLSN	MLSN	M0724	Utility Relocation by Others Complete	0%	0 days	Tue 7/6/21																				
389	5.13	TO	4TO1		Complete Transportation Operations Plan-Related Tasks (if a Significant Project)	0%	1 day?	Tue 7/6/21																				
390	5.13.1	TO	4TO1		Final Tow Contract Documents	0%	1 day?	Tue 7/6/21																				
391	5.13.2	TO	4TO1		Final Law Enforcement Memorandum of Understanding (MOUs)	0%	1 day?	Tue 7/6/21																				
392	5.13.3	TO	4TO1		STOC Operators Training	0%	1 day?	Tue 7/6/21																				
393	5.13.4	TO	4TO1		IMAP Procurement Schedule	0%	1 day?	Tue 7/6/21																				
394	5.14	VM	4VM1		Complete CR-AVE, CLEAR, and Value Assessment Activities	0%	1 day?	Tue 7/6/21																				
395	5.14.1	VM	4VM1		Constructability Review Minutes/CR Log	0%	1 day?	Tue 7/6/21																				
396	5.14.2	VM	4VM1		Risk Assessment worksheet	0%	1 day?	Tue 7/6/21																				
397	5.14.3	VM	4VM1		Value Assessment	0%	1 day?	Tue 7/6/21																				
398	5.14.4	VM	4VM1		Value Engineering (VE) Study report	0%	1 day?	Tue 7/6/21																				
399	5.14.5	VM	4VM1		CLEAR Database Submissions	0%	1 day?	Tue 7/6/21																				
400	5.15	EN	4EN1		Secure Environmental Permits	0%	1 day?	Tue 7/6/21																				
401	5.15.1	EN	4EN1		Permit Package	0%	1 day?	Tue 7/6/21																				
402	5.15.2	EN	4EN1		Project Special Commitments (Green Sheets)	0%	1 day?	Tue 7/6/21																				
403	5.16	RR	4RR1		Complete Railroad Coordination	0%	1 day?	Tue 7/6/21																				
404	5.16.1	RR	4RR1		Railroad Agreements	0%	1 day?	Tue 7/6/21																				
405	5.16.2	RR	4RR1		Project Special Provisions	0%	1 day?	Tue 7/6/21																				
406	5.17	CG	4CG1		Prepare Construction Communication Activities	0%	1 day?	Tue 7/6/21																				
407	5.17.1	CG	4CG1		Construction Outreach Material (varies by need)	0%	1 day?	Tue 7/6/21																				
408	5.17.2	CG	4CG1		Construction Public Information Plan	0%	1 day?	Tue 7/6/21																				
409	5.18	PM			Request Construction Funds	0%	1 day?	Tue 7/6/21																				
410	5.19	RD	4RD1		Finalize the Final PS&E Package	0%	1 day?	Wed 7/7/21																				
411	5.19.1	RD	4RD1		Review Set of Final Plans	0%	1 day?	Wed 7/7/21																				
412	5.19.2	RD	4RD1		Final Construction Quantities for Roadway Design Plans	0%	1 day?	Wed 7/7/21																				
413	5.19.3	RD	4RD1		Sealed Contract Roadway Design Plans	0%	1 day?	Wed 7/7/21																				
414	5.20	CS	4CS1		Complete PS&E Package and Advertise the Project	0%	1 day?	Thu 7/8/21																				
415	5.20.1	CS	4CS1		Final Plans	0%	1 day?	Thu 7/8/21																				
416	5.20.2	CS	4CS1		Proposal	0%	1 day?	Thu 7/8/21																				
417	5.20.3	CS	4CS1		Confidential Engineer's Estimate	0%	1 day?	Thu 7/8/21																				
418	5.21	MLSN	MLSN	M1008	Let Project	0%	0 days	Thu 7/8/21																				
419	5.22	CS	4CS2		Let, Award and Execute	0%	1 day?	Fri 7/9/21																				
420	5.22.1	CS	4CS2		Award Letter	0%	1 day?	Fri 7/9/21																				
421	5.22.2	CS	4CS2		Goal Confirmation Letter	0%	1 day?	Fri 7/9/21																				
422	5.22.3	CS	4CS2		Execution Letter	0%	1 day?	Fri 7/9/21																				
423	5.23				Post-Letting Activities	0%	1 day?	Mon 7/12/21																				

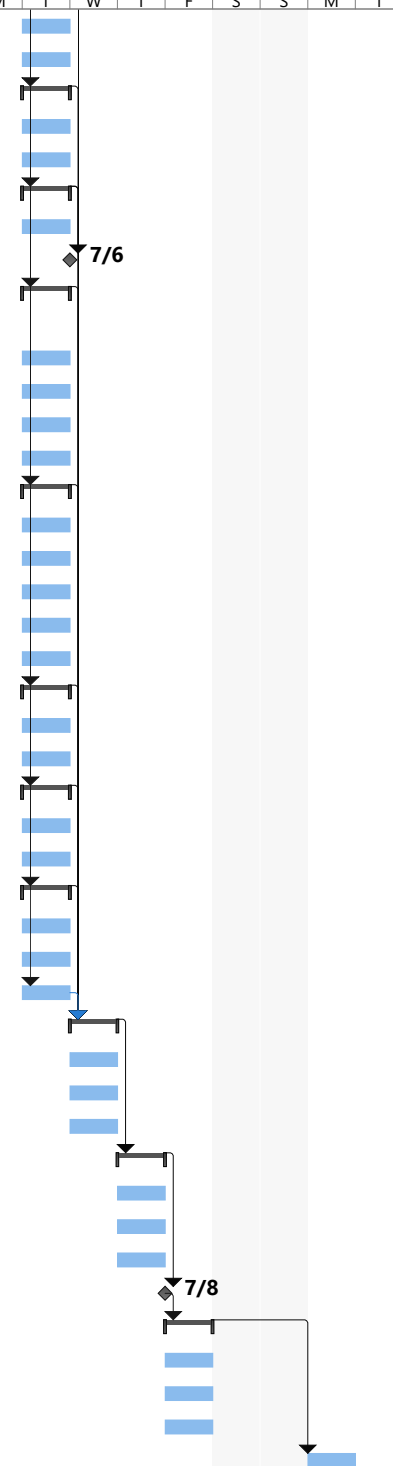

Project: NCDOT PDN 2 Schedu
Date: Mon 4/3/23

Task	Summary	Inactive Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical
Split	Project Summary	Inactive Summary		Manual Summary Rollup	Finish-only	External Milestone	Deadline
		Duration-only	Critical Split	Manual Progress	Progress	Manual Progress	Critical

Page 9
