

ID	Discipline Code	Task Code	SAP MLSN	Responsible Party	Task Name	Predecessors	Successors	Duration	Start	Finish	2024												2025				2026				2027				2028				2029		
WBS# - PROJECT NAME/DESCRIPTION											Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3			
1					WBS# - PROJECT NAME/DESCRIPTION			1050 days	Fri 11/1/24	Mon 3/5/29													WBS# - PROJECT NAME/DESCRIPTION																		
2	SCOPE	SCOPE			Scoping, Fee Estimate, and Notice to Proceed (Stage 1)			40 days	Fri 11/1/24	Mon 1/13/25													Scoping, Fee Estimate, and Notice to Proceed (Stage 1)																		
3	SCOPE	SCOPE		All Parties	Project Scoping Meeting		12,10,11,30,10	10 days	Fri 11/1/24	Fri 11/1/24													Project Scoping Meeting																		
4	SCOPE	SCOPE		PEF	Scope Development	3	5	10 days	Fri 11/1/24	Fri 11/15/24																															
5	SCOPE	SCOPE		NCDOT	Review/Approve Scope	4	6	10 days	Mon 11/18/24	Fri 12/6/24																															
6	SCOPE	SCOPE		PEF	Fee Estimate Development	5	7	10 days	Mon 12/9/24	Fri 12/20/24																															
7	SCOPE	SCOPE		NCDOT	Review/Approve Fee Estimate	6	8	10 days	Mon 12/30/24	Mon 1/13/25																															
8	SCOPE	SCOPE	M0965	NCDOT	Notice To Proceed (Stage 1)	7		38,47,53,34,50 days	Mon 1/13/25	Mon 1/13/25													Notice To Proceed (Stage 1)																		
9		1			Project Initiation (Stage 1)			215 days	Fri 11/1/24	Mon 9/22/25													Project Initiation (Stage 1)																		
10	LS	1LS1		NCDOT	Provide Photogrammetric Control & Initiate Surveys	3		60 days	Fri 11/1/24	Tue 2/11/25																															
11	PH	1PH1		NCDOT	Reviews & Provides Best Available Geospatial Data	3		20 days	Fri 11/1/24	Fri 12/6/24																															
12	PH	1PH2		NCDOT	Compile Aerial Photography & Mapping	3		60 days	Fri 11/1/24	Tue 2/11/25																															
13	RR	1RR1		NCDOT	Identify Railroad Impacts	3		20 days	Fri 11/1/24	Fri 12/6/24																															
14	SG	1SG1			Investigate Existing ITS & Signal Communications			150 days	Fri 11/1/24	Thu 6/19/25													Investigate Existing ITS & Signal Communications																		
15	SG	1SG1		PEF	Initiate Signal System Fiber Owners and Contacts	3		10 days	Fri 11/1/24	Fri 11/15/24																															
16	SG	1SG1		PEF	Conduct Preliminary Signal System Investigation	3		10 days	Fri 11/1/24	Fri 11/15/24																															
17	SG	1SG1		PEF	Prepare & Submit Draft ITS Risk Analysis and Report	15,16		10 days	Mon 11/18/24	Fri 12/6/24																															
18	SG	1SG1		NCDOT	Review of Draft ITS Risk Analysis and Report	17		10 days	Mon 12/9/24	Fri 12/20/24																															
19	SG	1SG1		PEF	Revise & Submit Final ITS Risk Analysis and Report	18		5 days	Mon 12/30/24	Mon 1/6/25																															
20	SG	1SG1		NCDOT	Review of Final ITS Risk Analysis and Report	19		5 days	Tue 1/7/25	Mon 1/13/25																															
21	EN	1EN1		NCDOT	Final ITS Risk Analysis and Report Approved	41		0 days	Thu 6/19/25	Thu 6/19/25													Final ITS Risk Analysis and Report Approved																		
22	SS	1SS1			Determine Affected Coordinated Corridors			10 days	Fri 11/1/24	Fri 11/15/24													Determine Affected Coordinated Corridors																		
23	SS	1SS1		NCDOT	Complete List of Affected Signal Systems	3		10 days	Fri 11/1/24	Fri 11/15/24																															
24	TO	1TO1			Scope Traffic System Operations			20 days	Fri 11/1/24	Fri 12/6/24													Scope Traffic System Operations																		
25	TO	1TO1		NCDOT	Determine Impacted Intelligent Transportation System (ITS) Devices & Coordinating Corridors	3		20 days	Fri 11/1/24	Fri 12/6/24																															
26	TS	1TS1			Assess Safety Planning			20 days	Fri 11/1/24	Fri 12/6/24													Assess Safety Planning																		
27	TS	1TS1		NCDOT	Conduct Traffic Safety Review	3		20 days	Fri 11/1/24	Fri 12/6/24																															
28	GT	1GT1			Geotechnical, Replacement & GeoEnvironmental Planning			10 days	Fri 11/1/24	Fri 11/15/24													Geotechnical, Replacement & GeoEnvironmental Planning																		
29	GT	1GT1		NCDOT	Develop Geotechnical Planning Report	3		10 days	Fri 11/1/24	Fri 11/15/24																															
30	GT	1GT1		NCDOT	Develop GeoEnvironmental Scoping Comments Report	3		10 days	Fri 11/1/24	Fri 11/15/24																															
31	ST	1ST1			Structures Screening			10 days	Fri 11/1/24	Fri 11/15/24													Structures Screening																		
32	ST	1ST1		NCDOT	Structures Cost Estimate for Express Design	3		10 days	Fri 11/1/24	Fri 11/15/24																															
33	CG	1CG1			Review Project Scoping			15 days	Tue 1/14/25	Tue 2/4/25													Review Project Scoping																		
34	CG	1CG1		PEF	Submit ETRACS Request to Initiate Communications Support	8		5 days	Tue 1/14/25	Tue 1/21/25																															
35	CG	1CG1		NCDOT	Review of Communications Support Needs	34		10 days	Wed 1/22/25	Tue 2/4/25																															
36	EN	1EN1			Establish Environmental Needs			115 days	Tue 1/14/25	Thu 6/26/25													Establish Environmental Needs																		
37	EN	1EN1			Data Collection and Mapping			110 days	Tue 1/14/25	Thu 6/19/25													Data Collection and Mapping																		
38	EN	1EN1		PEF	Collect & Review Existing Data	8		5 days	Tue 1/14/25	Tue 1/21/25																															
39	EN	1EN1		PEF	Conduct Site Visit	38,265		0 days	Thu 5/29/25	Thu 5/29/25													Conduct Site Visit																		
40	EN	1EN1		PEF	Update Environmental Features Map & Study Area	39,11		10 days	Fri 5/30/25	Thu 6/12/25																															
41	EN	1EN1		NCDOT	Review of Updated Environmental Features Map & Study Area	40		5 days	Fri 6/13/25	Thu 6/19/25																															
42	EN	1EN1		NCDOT	Environmental Features Map & Study Area Approved	41		0 days	Thu 6/19/25	Thu 6/19/25													Environmental Features Map & Study Area Approved																		
43	EN	1EN1			Requests for Human & Environment Studies			5 days	Fri 6/20/25	Thu 6/26/25													Requests for Human & Environment Studies																		
44	EN	1EN1		PEF	Prepare & Submit ETRACS Request for Historic Architecture	42,21		5 days	Fri 6/20/25	Thu 6/26/25																															
45	EN	1EN1		PEF	Prepare & Submit ETRACS Request for Archaeology	42,21		5 days	Fri 6/20/25	Thu 6/26/25																															
46	EN	1EN1			Land Owner Notification Letters			20 days	Tue 1/14/25	Tue 2/11/25													Land Owner Notification Letters																		

Project: NCDOT PDN Schedule Date: Wed 11/13/24

Task Split
Milestone Summary
Project Summary
Inactive Milestone
Inactive Summary
Manual Task
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

ID	Discipline Code	Task Code	SAP MLSN	Responsible Party	Task Name	Predecessors	Successors	Duration	Start	Finish	2025												2026				2027				2028				2029		
											Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3							
139	HY	2HY1			Develop Preliminary Hydraulic Recommendations			30 days	Mon 8/11/25	Mon 9/22/25	Develop Preliminary Hydraulic Recommendations																										
140	HY	2HY1	PEF		Prepare & Submit Hydraulic Planning Report (HPR)	129	141	10 days	Mon 8/11/25	Fri 8/22/25																											
141	HY	2HY1	NCDOT		Review of HPR	140	142	10 days	Mon 8/25/25	Mon 9/8/25																											
142	HY	2HY1	PEF		Revise & Resubmit HPR	141	143	5 days	Tue 9/9/25	Mon 9/15/25																											
143	HY	2HY1	NCDOT		Review of Revised HPR	142	144	5 days	Tue 9/16/25	Mon 9/22/25																											
144	HY	2HY1	NCDOT		Hydraulic Planning Report Approved	143	162	0 days	Mon 9/22/25	Mon 9/22/25																											
145	RD	2RD2			Complete Design Recommendation Plan Set			40 days	Tue 9/23/25	Tue 11/18/25	Complete Design Recommendation Plan Set																										
146	RD	2RD2	PEF		Prepare & Submit Design Recommendation Plan Set	131,129,89,123,1	148,147FF	20 days	Tue 9/23/25	Mon 10/20/25																											
147	CS	2CS1	PEF		Prepare Initial Design Estimates	146FF	148	20 days	Tue 9/23/25	Mon 10/20/25																											
148	RD	2RD2	NCDOT		Review of Design Recommendation Plan Set	146,147	149	10 days	Tue 10/21/25	Mon 11/3/25																											
149	RD	2RD2	PEF		Revise & Resubmit Design Recommendation Plan Set	148	150	5 days	Tue 11/4/25	Mon 11/10/25																											
150	RD	2RD2	NCDOT		Review of Revised Design Recommendation Plan Set	149	151	5 days	Wed 11/12/25	Tue 11/18/25																											
151	RD	2RD2	NCDOT		Design Recommendation Plan Set Approved	150	204,162,210,20	20 days	Tue 11/18/25	Tue 11/18/25	Design Recommendation Plan Set Approved																										
152	UT	2UT2	UTILITY PEF		Prepare Utility Relocation and Construction Estimates	138,151	171	10 days	Wed 11/19/25	Tue 12/9/25																											
153	RW	2RW2	ROW PEF		Prepare ROW Cost Estimate	151,342SS-140 days		10 days	Fri 2/6/26	Thu 2/19/26																											
154	RR	2RR1			Coordinate Railroad Review			45 days	Wed 11/19/25	Thu 2/5/26	Coordinate Railroad Review																										
155	RR	2RR1	PEF		Prepare & Submit Railroad Design Line and Grade	151,13	156,157	10 days	Wed 11/19/25	Tue 12/9/25																											
156	RR	2RR1	NCDOT		Review of Railroad Line and Grade	155	158	10 days	Wed 12/10/25	Tue 12/30/25																											
157	RR	2RR1	RAILROAD		Rail Review of Railroad Line and Grade	155	158	20 days	Wed 12/10/25	Wed 1/14/26																											
158	RR	2RR1	PEF		Revise & Resubmit Railroad Line and Grade	157,156	159	10 days	Thu 1/15/26	Thu 1/29/26																											
159	RR	2RR1	NCDOT		Review of Revised Railroad Line and Grade	158	160	5 days	Fri 1/30/26	Thu 2/5/26																											
160	RR	2RR1	NCDOT		Railroad Line and Grade Approved	159	320,319	0 days	Thu 2/5/26	Thu 2/5/26																											
161	HY	2HY2			Complete Drainage Design			110 days	Wed 11/19/25	Fri 5/8/26	Complete Drainage Design																										
162	HY	2HY2	PEF		Prepare & Submit Hydraulic Designs & BSR	151,144	163,171,172	20 days	Wed 11/19/25	Tue 12/30/25																											
163	HY	2HY2	NCDOT		Review of Hydraulic Designs & BSR	162	164	10 days	Wed 12/31/25	Wed 1/14/26																											
164	HY	2HY2	PEF		Revise & Resubmit Hydraulic Designs & BSR	163	165	10 days	Thu 1/15/26	Thu 1/29/26																											
165	HY	2HY2	NCDOT		Review of Revised Hydraulic Designs & BSR	164	166	5 days	Fri 1/30/26	Thu 2/5/26																											
166	HY	2HY2	NCDOT		Hydraulic Designs & BSR Approved	165	319,320,194,20	0 days	Thu 2/5/26	Thu 2/5/26																											
167	HY	2HY2	PEF		State Floodplain Compliance (SFC) Package	166	168	5 days	Fri 2/6/26	Thu 2/12/26																											
168	HY	2HY2	AGENCY		NC SFC Review & Approval	167	469,488	60 days	Fri 2/13/26	Fri 5/8/26																											
169	SG	2SG1	PEF		Establish Signal & ITS Locations	151,20	176FF	20 days	Wed 11/19/25	Tue 12/30/25																											
170	UT	2UT3			Advance Utility Coordination and/or Design			115 days	Wed 12/31/25	Mon 6/15/26	Advance Utility Coordination and/or Design																										
171	UT	2UT3	UTILITY PEF		Provide Plans to Utility Owners	162,152	173	5 days	Wed 12/31/25	Wed 1/7/26																											
172	UT	2UT3	UTILITY PEF		Identify Major Utility Conflicts and Relocation Impacts	162	173	5 days	Wed 12/31/25	Wed 1/7/26																											
173	UT	2UT3	UTILITY PEF		Conduct Utility Coordination Meeting (All Utilities)	172,171	174,175,178	0 days	Wed 1/7/26	Wed 1/7/26																											
174	UT	2UT3	UTILITY PEF		Initiate Cost Responsibility Analysis	173	319	5 days	Thu 1/8/26	Wed 1/14/26																											
175	UT	2UT3	UTILITY OWNERS		Utility Owners Develop Routing Plans	173	176	40 days	Thu 1/8/26	Thu 3/5/26																											
176	UT	2UT3	UTILITY PEF		Submit Routing Plan/Preliminary UBO Plans	175,169FF	177,186,185	5 days	Fri 3/6/26	Thu 3/12/26																											
177	UT	2UT3	UTILITY PEF		Create Relocation Schedule	176	320,319	5 days	Fri 3/13/26	Thu 3/19/26																											
178	UT	2UT3	UTILITY PEF		Submit Preliminary Utility Construction Routing Plans (30%)	173	179	20 days	Thu 1/8/26	Thu 2/5/26																											
179	UT	2UT3	NCDOT		Review of 30% UC Plans	178	182,180	10 days	Fri 2/6/26	Thu 2/19/26																											
180	UT	2UT3	UTILITY PEF		Request Subsurface Utility Engineering (SUE) Level A	179	181	5 days	Fri 2/20/26	Thu 2/26/26																											
181	LS	2LS2	NCDOT		Complete SUE Level A	180	182	40 days	Fri 2/27/26	Fri 4/24/26																											
182	UT	2UT3	UTILITY PEF		Submit Preliminary Utility Construction Plans (60%)	179,181	183	20 days	Mon 4/27/26	Fri 5/22/26																											
183	UT	2UT3	NCDOT		Review of 60% UC Plans	182	184,186,185	10 days	Tue 5/26/26	Mon 6/8/26																											
184	UT	2UT3	UTILITY PEF		Request Geotechnical Investigation for Trenchless Construction	183	324	5 days	Tue 6/9/26	Mon 6/15/26																											

Project: NCDOT PDN Schedule Date: Wed 11/13/24

Task Split
Milestone Summary
Project Summary
Inactive Milestone Summary
Manual Task Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline Progress
Manual Progress

ID	Discipline Code	Task Code	SAP MLSN	Responsible Party	Task Name	Predecessors	Successors	Duration	Start	Finish	2024	2025	2026	2027	2028	2029							
											Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
231	PI	2PI1		NCDOT	Review of Revised Website Template	230	232	5 days	Thu 1/8/26	Wed 1/14/26													
232	PI	2PI1		NCDOT	Website Template Approved	231	233	0 days	Wed 1/14/26	Wed 1/14/26													
233	PI	2PI1		NCDOT	Creation of Website	232,226,208	234	10 days	Fri 1/30/26	Thu 2/12/26													
234	PI	2PI1		NCDOT	Website Goes Live	233	2155F,236	0 days	Thu 2/12/26	Thu 2/12/26													
235	PI	2PI1			Public Involvement Comment and Responses			30 days	Fri 2/13/26	Thu 3/26/26													
236	PI	2PI1		NCDOT	Gathering Public Comments	234	237	20 days	Fri 2/13/26	Thu 3/12/26													
237	PI	2PI1		PEF	Response to Public Comments	236	307	10 days	Fri 3/13/26	Thu 3/26/26													
238	GT	2GT1		NCDOT	Prepare GeoEnvironmental Phase I Report	129	319,320,381	20 days	Mon 8/11/25	Mon 9/8/25													
239	GT	2GT2		NCDOT	Roadway Geotechnical & Geopavement Investigations	151	319,320	40 days	Wed 11/19/25	Thu 1/29/26													
240	GT	2GT3		NCDOT	Geotechnical Structure Investigations	166	319,320,382	40 days	Fri 2/6/26	Thu 4/2/26													
241	PD	2PD1			Complete Pavement Design			60 days	Wed 11/19/25	Thu 2/26/26													
242	PD	2PD1		NCDOT	Final Pavement Design Memo	151	319,320,338	60 days	Wed 11/19/25	Thu 2/26/26													
243	TS	2TS1			Complete Safety Analysis and Operational Review			20 days	Wed 11/19/25	Tue 12/30/25													
244	TS	2TS1		NCDOT	Traffic Signal Recommendations	151,27	320,319	20 days	Wed 11/19/25	Tue 12/30/25													
245	EN	2EN1			Initiate Natural Resources Analysis			95 days	Tue 1/14/25	Thu 5/29/25													
246	EN	2EN1			Complete NRTR and WEX File			40 days	Wed 2/12/25	Tue 4/8/25													
247	LS	2LS1		ENVIRON/PEF	Conduct Wetland Delineations and Field Surveys	49	248	10 days	Wed 2/12/25	Tue 2/25/25													
248	EN	2EN1		ENVIRON/PEF	Prepare & Submit Draft NRTR and PJD Package	247	249	10 days	Wed 2/26/25	Tue 3/11/25													
249	EN	2EN1		NCDOT	Review of Draft NRTR and PJD Package	248	250	10 days	Wed 3/12/25	Tue 3/25/25													
250	EN	2EN1		ENVIRON/PEF	Revise & Resubmit Final NRTR and PJD Package	249,260FF	252	5 days	Wed 4/2/25	Tue 4/8/25													
251	EN	2EN1			Signed PJD			35 days	Wed 4/9/25	Thu 5/29/25													
252	EN	2EN1		AGENCY	Review PJD Package	250	253	25 days	Wed 4/9/25	Wed 5/14/25													
253	EN	2EN1		AGENCY	Conduct Agency Field Review	252	254	5 days	Thu 5/15/25	Wed 5/21/25													
254	EN	2EN1		ENVIRON/PEF	Create WET File and Revise PJD Package (If Necessary)	253	255	5 days	Thu 5/22/25	Thu 5/29/25													
255	EN	2EN1		AGENCY	Sign PJD	254	307	0 days	Thu 5/29/25	Thu 5/29/25													
256	EN	2EN1			Threatened & Endangered (T&E) Species Survey			60 days	Tue 1/14/25	Tue 4/8/25													
257	EN	2EN1		ENVIRON/PEF	T&E Survey and Submit Biological Assessment	8	258	10 days	Tue 1/14/25	Tue 1/28/25													
258	EN	2EN1		NCDOT	Initiate Section 7 Consultation	257	259	20 days	Wed 1/29/25	Tue 2/25/25													
259	EN	2EN1		AGENCY	Review Biological Opinion/Commitments	258	260	30 days	Wed 2/26/25	Tue 4/8/25													
260	EN	2EN1		AGENCY	Renders Biological Opinion/Commitments	259	250FF	0 days	Tue 4/8/25	Tue 4/8/25													
261	EN	2EN2			Initiate Human Environment Analysis			250 days	Thu 5/8/25	Fri 5/15/26													
262	EN	2EN2			Complete Community Studies Report			40 days	Thu 5/8/25	Thu 7/3/25													
263	EN	2EN2		PEF	Delineate the Direct Community Impact Area (DCIA) and Demographic Study Area (DSA) Boundary	89,67	264	5 days	Thu 5/8/25	Wed 5/14/25													
264	EN	2EN2		PEF	Submit DCIA & DSA Boundary to Community Studies for Review & Approval	263	265	5 days	Thu 5/15/25	Wed 5/21/25													
265	EN	2EN2		PEF	Compile Demographic information from Community Studies Demographic Tool	264	39,266,91	5 days	Thu 5/22/25	Thu 5/29/25													
266	EN	2EN2		PEF	Community Studies Field Visit	265,38	268	0 days	Thu 5/29/25	Thu 5/29/25													
267	EN	2EN2		PEF	Prepare & Send Out Local Officials Input Forms	89,67	268	10 days	Thu 5/8/25	Wed 5/21/25													
268	EN	2EN2		PEF	Prepare & Submit Draft Community Impact Assessment (CIA)	266,267	269	5 days	Fri 5/30/25	Thu 6/5/25													
269	EN	2EN2		NCDOT	Review of Draft CIA	268	270	10 days	Fri 6/6/25	Thu 6/19/25													
270	EN	2EN2		PEF	Revise & Submit Final CIA	269	271	5 days	Fri 6/20/25	Thu 6/26/25													
271	EN	2EN2		NCDOT	Review of Final CIA	270	272	5 days	Fri 6/27/25	Thu 7/3/25													
272	EN	2EN2		NCDOT	Approve Final CIA	271	204,146FF	0 days	Thu 7/3/25	Thu 7/3/25													
273	EN	2EN2			Complete Cultural Resource Screenings			40 days	Fri 6/27/25	Fri 8/22/25													
274	EN	2EN2		NCDOT	Complete Historic Architecture and Landscapes No Survey Required Form	44	307	40 days	Fri 6/27/25	Fri 8/22/25													
275	EN	2EN2		NCDOT	Complete No Archaeological Survey Required Form	45	307	40 days	Fri 6/27/25	Fri 8/22/25													
276	EN	2EN2			Identify Section 4(f) Resources			140 days	Mon 8/11/25	Thu 3/12/26													

Project: NCDOT PDN Schedule Date: Wed 11/13/24


■ Milestone ◆ Project Summary ▬ Inactive Milestone ◆ Manual Task ▬ Manual Summary Rollup ▬ Start-only ▬ External Tasks ▬ Deadline ▬ Manual Progress
▬ Task Split ▬ Summary ▬ Inactive Task ▬ Inactive Summary ▬ Duration-only ▬ Manual Summary ▬ Finish-only ▬ External Milestone ▬ Progress

ID	Discipline Code	Task Code	SAP MLSN	Responsible Party	Task Name	Predecessors	Successors	Duration	Start	Finish	2024	2025	2026	2027	2028	2029							
											Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
277	EN	2EN2		PEF	Identify Section 4(f) Resource Ownership	129	278	5 days	Mon 8/11/25	Fri 8/15/25													
278	EN	2EN2		PEF	Determine Impacts to Resource	277,166	279	5 days	Fri 2/6/26	Thu 2/12/26													
279	EN	2EN2		AGENCY	Sign de minimis Agreement	278	309	20 days	Fri 2/13/26	Thu 3/12/26													
280	EN	2EN2			Traffic Noise Report (TNR)			185 days	Mon 8/11/25	Fri 5/15/26													
281	EN	2EN2		PEF	Prepare & Submit Workplan	129	282	20 days	Mon 8/11/25	Mon 9/8/25													
282	EN	2EN2		NCDOT	Review of Workplan	281	283	20 days	Tue 9/9/25	Mon 10/6/25													
283	EN	2EN2		PEF	Revise & Resubmit Workplan	282	284	10 days	Tue 10/7/25	Mon 10/20/25													
284	EN	2EN2		NCDOT	Review of Final Workplan	283	285	10 days	Tue 10/21/25	Mon 11/3/25													
285	EN	2EN2		PEF	Field Data Collection & Base Modeling/Validation	284	286	20 days	Tue 11/4/25	Tue 12/9/25													
286	EN	2EN2		NCDOT	Review of Validation	285	287	10 days	Wed 12/10/25	Tue 12/30/25													
287	EN	2EN2		PEF	Revise & Resubmit Validation	286	288	10 days	Wed 12/31/25	Wed 1/14/26													
288	EN	2EN2		NCDOT	Review of Final Validation	287	289,290	10 days	Thu 1/15/26	Thu 1/29/26													
289	EN	2EN2		PEF	Future Year No-Build Modeling	288	291	10 days	Fri 1/30/26	Thu 2/12/26													
290	EN	2EN2		PEF	Future Year Build Modeling	151,288	291	20 days	Fri 1/30/26	Thu 2/26/26													
291	EN	2EN2		PEF	Prepare & Submit Draft TNR	290,289	292	15 days	Fri 2/27/26	Thu 3/19/26													
292	EN	2EN2		NCDOT	Review of Draft TNR	291	293	20 days	Fri 3/20/26	Fri 4/17/26													
293	EN	2EN2		PEF	Revise & Submit Final TNR	292	294	10 days	Mon 4/20/26	Fri 5/1/26													
294	EN	2EN2		NCDOT	Review of Final TNR	293	295	10 days	Mon 5/4/26	Fri 5/15/26													
295	EN	2EN2		NCDOT	Final TNR Approved	294	309	0 days	Fri 5/15/26	Fri 5/15/26													
296	EN	2EN3			Develop Noise Report or Addendum			90 days	Thu 9/24/26	Mon 2/15/27													
297	EN	2EN3		PEF	Future Year No-Build Modeling	328	299	10 days	Thu 9/24/26	Wed 10/7/26													
298	EN	2EN3		PEF	Future Year Build Modeling	328	299	10 days	Thu 9/24/26	Wed 10/7/26													
299	EN	2EN3		PEF	Prepare & Submit Draft DNR	297,298	300	20 days	Thu 10/8/26	Wed 11/4/26													
300	EN	2EN3		NCDOT	Review of Draft DNR	299	301	20 days	Thu 11/5/26	Thu 12/10/26													
301	EN	2EN3		PEF	Revise & Resubmit Draft DNR	300	302	10 days	Fri 12/11/26	Thu 12/31/26													
302	EN	2EN3		NCDOT	Review of Revised Draft DNR	301	303	10 days	Mon 1/4/27	Fri 1/15/27													
303	EN	2EN3		PEF	Revise & Submit Final DNR	302	304	10 days	Tue 1/19/27	Mon 2/1/27													
304	EN	2EN3		NCDOT	Review of Final DNR	303	305	10 days	Tue 2/2/27	Mon 2/15/27													
305	EN	2EN3		NCDOT	Final DNR Approved	304	396	0 days	Mon 2/15/27	Mon 2/15/27													
306	EP	2EP1			Advance NEPA/SEPA Documentation			45 days	Fri 3/27/26	Mon 6/1/26													
307	EP	2EP1		PEF	Prepare & Submit Draft Categorical Exclusion (CE)	274,275,237,151,308	308	10 days	Fri 3/27/26	Fri 4/10/26													
308	EP	2EP1		NCDOT	Review of Draft CE	307	309	10 days	Mon 4/13/26	Fri 4/24/26													
309	EP	2EP1		PEF	Revise & Submit Final CE	308,295,279	310	5 days	Mon 5/18/26	Fri 5/22/26													
310	EP	2EP1		NCDOT	Review of Final CE	309	311	5 days	Tue 5/26/26	Mon 6/1/26													
311	EP	2EP1		NCDOT	Environmental Document Approved	310	319,320,342,40	0 days	Mon 6/1/26	Mon 6/1/26													
312	TM	2TM2			Initiate Transportation Management Plan			20 days	Mon 5/4/26	Tue 6/2/26													
313	TM	2TM2		PEF	Complete Concept Temporary Traffic Control (TTC) Plans	319SF,320SF,151	317,427	20 days	Mon 5/4/26	Tue 6/2/26													
314	SD	SD			Initiate Signing and Delineation Design			20 days	Mon 5/4/26	Tue 6/2/26													
315	SD	2SD1		PEF	Prepare Preliminary Signing and Delineation Strip Map	319SF,320SF,151		20 days	Mon 5/4/26	Tue 6/2/26													
316	VM	2VM1		NCDOT	Complete Value Management Activities	129	320,319,339	60 days	Mon 8/11/25	Mon 11/3/25													
317	SS	2SS1		PEF	Initiate Signal System Timing	313	414	20 days	Tue 6/2/26	Mon 6/29/26													
318	RD	2RD3			Prepare for Field Inspection			40 days	Tue 6/2/26	Tue 7/28/26													
319	CS	2CS2		PEF	Prepare Field Construction Estimate	316,195,239,240,313SF,315SF,320		30 days	Tue 6/2/26	Mon 6/29/26													
320	RD	2RD3		PEF	Prepare Field Inspection Plans Set	195,316,244,239,313SF,315SF,320		30 days	Tue 6/2/26	Mon 6/29/26													
321	RD	2RD3		NCDOT	Review of Field Inspection Plan Set	319,320	322	20 days	Tue 6/30/26	Tue 7/28/26													
322	RD	2RD3		NCDOT	Field Inspection	321	324,338,339,30	0 days	Tue 7/28/26	Tue 7/28/26													

Project: NCDOT PDN Schedule Date: Wed 11/13/24

■ Milestone ◆ Project Summary ▬ Inactive Milestone ◇ Manual Task ▬ Manual Summary Rollup ▬ Start-only ▬ External Tasks ▬ Deadline ▬ Manual Progress
▬ Task Split ▬ Summary ▬ Inactive Task ▬ Inactive Summary ▬ Duration-only ▬ Manual Summary ▬ Finish-only ▬ External Milestone ▬ Progress

ID	Discipline Code	Task Code	SAP MLSN	Responsible Party	Task Name	Predecessors	Successors	Duration	Start	Finish	Q4	2024 Q1	Q2	Q3	Q4	2025 Q1	Q2	Q3	Q4	2026 Q1	Q2	Q3	Q4	2027 Q1	Q2	Q3	Q4	2028 Q1	Q2	Q3	Q4	2029 Q1	Q2	Q3	
323	RD	2RD4			ROW Plans Completed			40 days	Wed 7/29/26	Wed 9/23/26																									
324	RD	2RD4		PEF	Complete & Submit ROW Plan Set	336,322,338FF,33325		20 days	Wed 7/29/26	Tue 8/25/26																									
325	RD	2RD4		NCDOT	Review of ROW Plan Set	324	326	10 days	Wed 8/26/26	Wed 9/9/26																									
326	RD	2RD4		PEF	Revise & Resubmit ROW Plan Set	325	327	5 days	Thu 9/10/26	Wed 9/16/26																									
327	RD	2RD4		NCDOT	Review of Revised ROW Plan Set	326	328	5 days	Thu 9/17/26	Wed 9/23/26																									
328	RD	2RD4			ROW Plans Complete (RPC)	327	344,390,384,30	30 days	Wed 9/23/26	Wed 9/23/26																									
329	RW	2RW3		ROW PEF	Prepare ROW Cost Estimate	322	330	10 days	Wed 7/29/26	Tue 8/11/26																									
330	RW	2RW3		NCDOT	Review of ROW Cost Estimate	329	342	10 days	Wed 8/12/26	Tue 8/25/26																									
331	SCOPE	SCOPE			Scoping, Fee Estimate, and Notice to Proceed (Stage 3 & 4)			40 days	Fri 3/20/26	Fri 5/15/26																									
332	SCOPE	SCOPE		PEF	Scope Development	166,195,201	333	10 days	Fri 3/20/26	Thu 4/2/26																									
333	SCOPE	SCOPE		NCDOT	Review/Approve Scope	332	334	10 days	Mon 4/6/26	Fri 4/17/26																									
334	SCOPE	SCOPE		PEF	Fee Estimate Development	333	335	10 days	Mon 4/20/26	Fri 5/1/26																									
335	SCOPE	SCOPE		NCDOT	Review/Approve Fee Estimate	334	336	10 days	Mon 5/4/26	Fri 5/15/26																									
336	SCOPE	SCOPE			Notice To Proceed (Stage 3 & 4)	335	324,338,339,30	30 days	Fri 5/15/26	Fri 5/15/26																									
337		3			Final Plans (Stage 3)			745 days	Tue 9/9/25	Thu 9/28/28																									
338	PD	3PD1		PEF	Verify and Revise Pavement Design	322,242,336	324FF,351	5 days	Wed 7/29/26	Tue 8/4/26																									
339	VM	3VM1		PEF	Incorporate Value Management Activities	316,322,336	324FF,351	5 days	Wed 7/29/26	Tue 8/4/26																									
340	RW	3RW1			Right of Way Funding			90 days	Tue 6/2/26	Wed 10/7/26																									
341	EP	3EP1		PEF	Complete NEPA/SEPA Documentation	342SS-60 days		10 days	Tue 6/2/26	Mon 6/15/26																									
342	RW	3RW1		NCDOT	Complete ROW Authorization Package	330,311	343,341SS-60 days,153SS-14	30 days	Wed 8/26/26	Wed 10/7/26																									
343	RW	3RW1		NCDOT	ROW Funds Released	342	346	0 days	Wed 10/7/26	Wed 10/7/26																									
344	LS	3LS1		NCDOT	Complete Additional Surveys and ROW Acquisition Surveys	328	346FF	20 days	Thu 9/24/26	Wed 10/21/26																									
345	RW	3RW2		ROW PEF	Complete ROW Acquisitions and Relocations			480 days	Thu 10/8/26	Wed 9/27/28																									
346	RW	3RW2		ROW PEF	Phase 1 - ROW Acquisitions and Relocations (Utility/Priority Parcels)	343,344FF,381,32347,453		160 days	Thu 10/8/26	Wed 6/9/27																									
347	RW	3RW2		ROW PEF	Phase 2 - ROW Acquisitions and Relocations (Utility/Priority Parcels)	346	348,454,351	160 days	Thu 6/10/27	Thu 2/10/28																									
348	RW	3RW2		ROW PEF	Remaining ROW Acquisitions and Relocations	347	349	160 days	Fri 2/11/28	Wed 9/27/28																									
349	RW	3RW2		NCDOT	ROW Certification	348	468,460,475,40	40 days	Wed 9/27/28	Wed 9/27/28																									
350	RD	3RD1			Complete Roadway Design			40 days	Fri 2/11/28	Thu 4/6/28																									
351	RD	3RD1		PEF	Complete & Submit Final Roadway Plan Set	336,328,338,339,352		20 days	Fri 2/11/28	Thu 3/9/28																									
352	RD	3RD1		NCDOT	Review Final Roadway Plan Set	351	353	10 days	Fri 3/10/28	Thu 3/23/28																									
353	RD	3RD1		PEF	Revise & Resubmit Final Roadway Plan Set	352	354	5 days	Fri 3/24/28	Thu 3/30/28																									
354	RD	3RD1		NCDOT	Review Revised Final Roadway Plan Set	353	355	5 days	Fri 3/31/28	Thu 4/6/28																									
355	RD	3RD1		NCDOT	Final Roadway Plan Set Approved	354	441,444	0 days	Thu 4/6/28	Thu 4/6/28																									
356	UT	3UT1			Complete Utility Coordination and/or Design			135 days	Thu 9/24/26	Tue 4/20/27																									
357	UT	3UT1		UTILITY PEF	Prepare & Submit Utilities By Other (UBO) Plans	328	358	20 days	Thu 9/24/26	Wed 10/21/26																									
358	UT	3UT1		NCDOT	Review of UBO Plans	357	359	10 days	Thu 10/22/26	Wed 11/4/26																									
359	UT	3UT1		UTILITY PEF	Revise & Resubmit UBO Plans	358	360	5 days	Thu 11/5/26	Thu 11/12/26																									
360	UT	3UT1		NCDOT	Review of Revised UBO Plans	359	361	5 days	Fri 11/13/26	Thu 11/19/26																									
361	UT	3UT1		NCDOT	UBO Plans Approved	360	390,384,377,40	40 days	Thu 11/19/26	Thu 11/19/26																									
362	UT	3UT1		UTILITY PEF	Prepare & Submit Final Utility Construction (UC) Plans to NCDOT & Utility Owners	328	363,384,390	40 days	Thu 9/24/26	Thu 11/19/26																									
363	UT	3UT1		NCDOT / UO	Review of Final UC Plans	362	364	20 days	Fri 11/20/26	Thu 12/31/26																									
364	UT	3UT1		UTILITY PEF	Revise & Resubmit Final UC Plans to Utility Owners	363	365	10 days	Mon 1/4/27	Fri 1/15/27																									
365	UT	3UT1		UTILITY OWNERS	Utility Owners Review of Revised Final UC Plans	364	366	10 days	Tue 1/19/27	Mon 2/1/27																									
366	UT	3UT1		UTILITY OWNERS	Final UC Plans Approved	365	367,441,444	0 days	Mon 2/1/27	Mon 2/1/27																									
367	UT	3UT1		UTILITY PEF	Finalize Permit Applications (Prepare/Submit/Receive Signatures)	366	368	5 days	Tue 2/2/27	Mon 2/8/27																									
368	UT	3UT1		UTILITY PEF	Submit Final UC Plan Package to NCDEQ Water Supply Section for Review	367	369	0 days	Mon 2/8/27	Mon 2/8/27																									

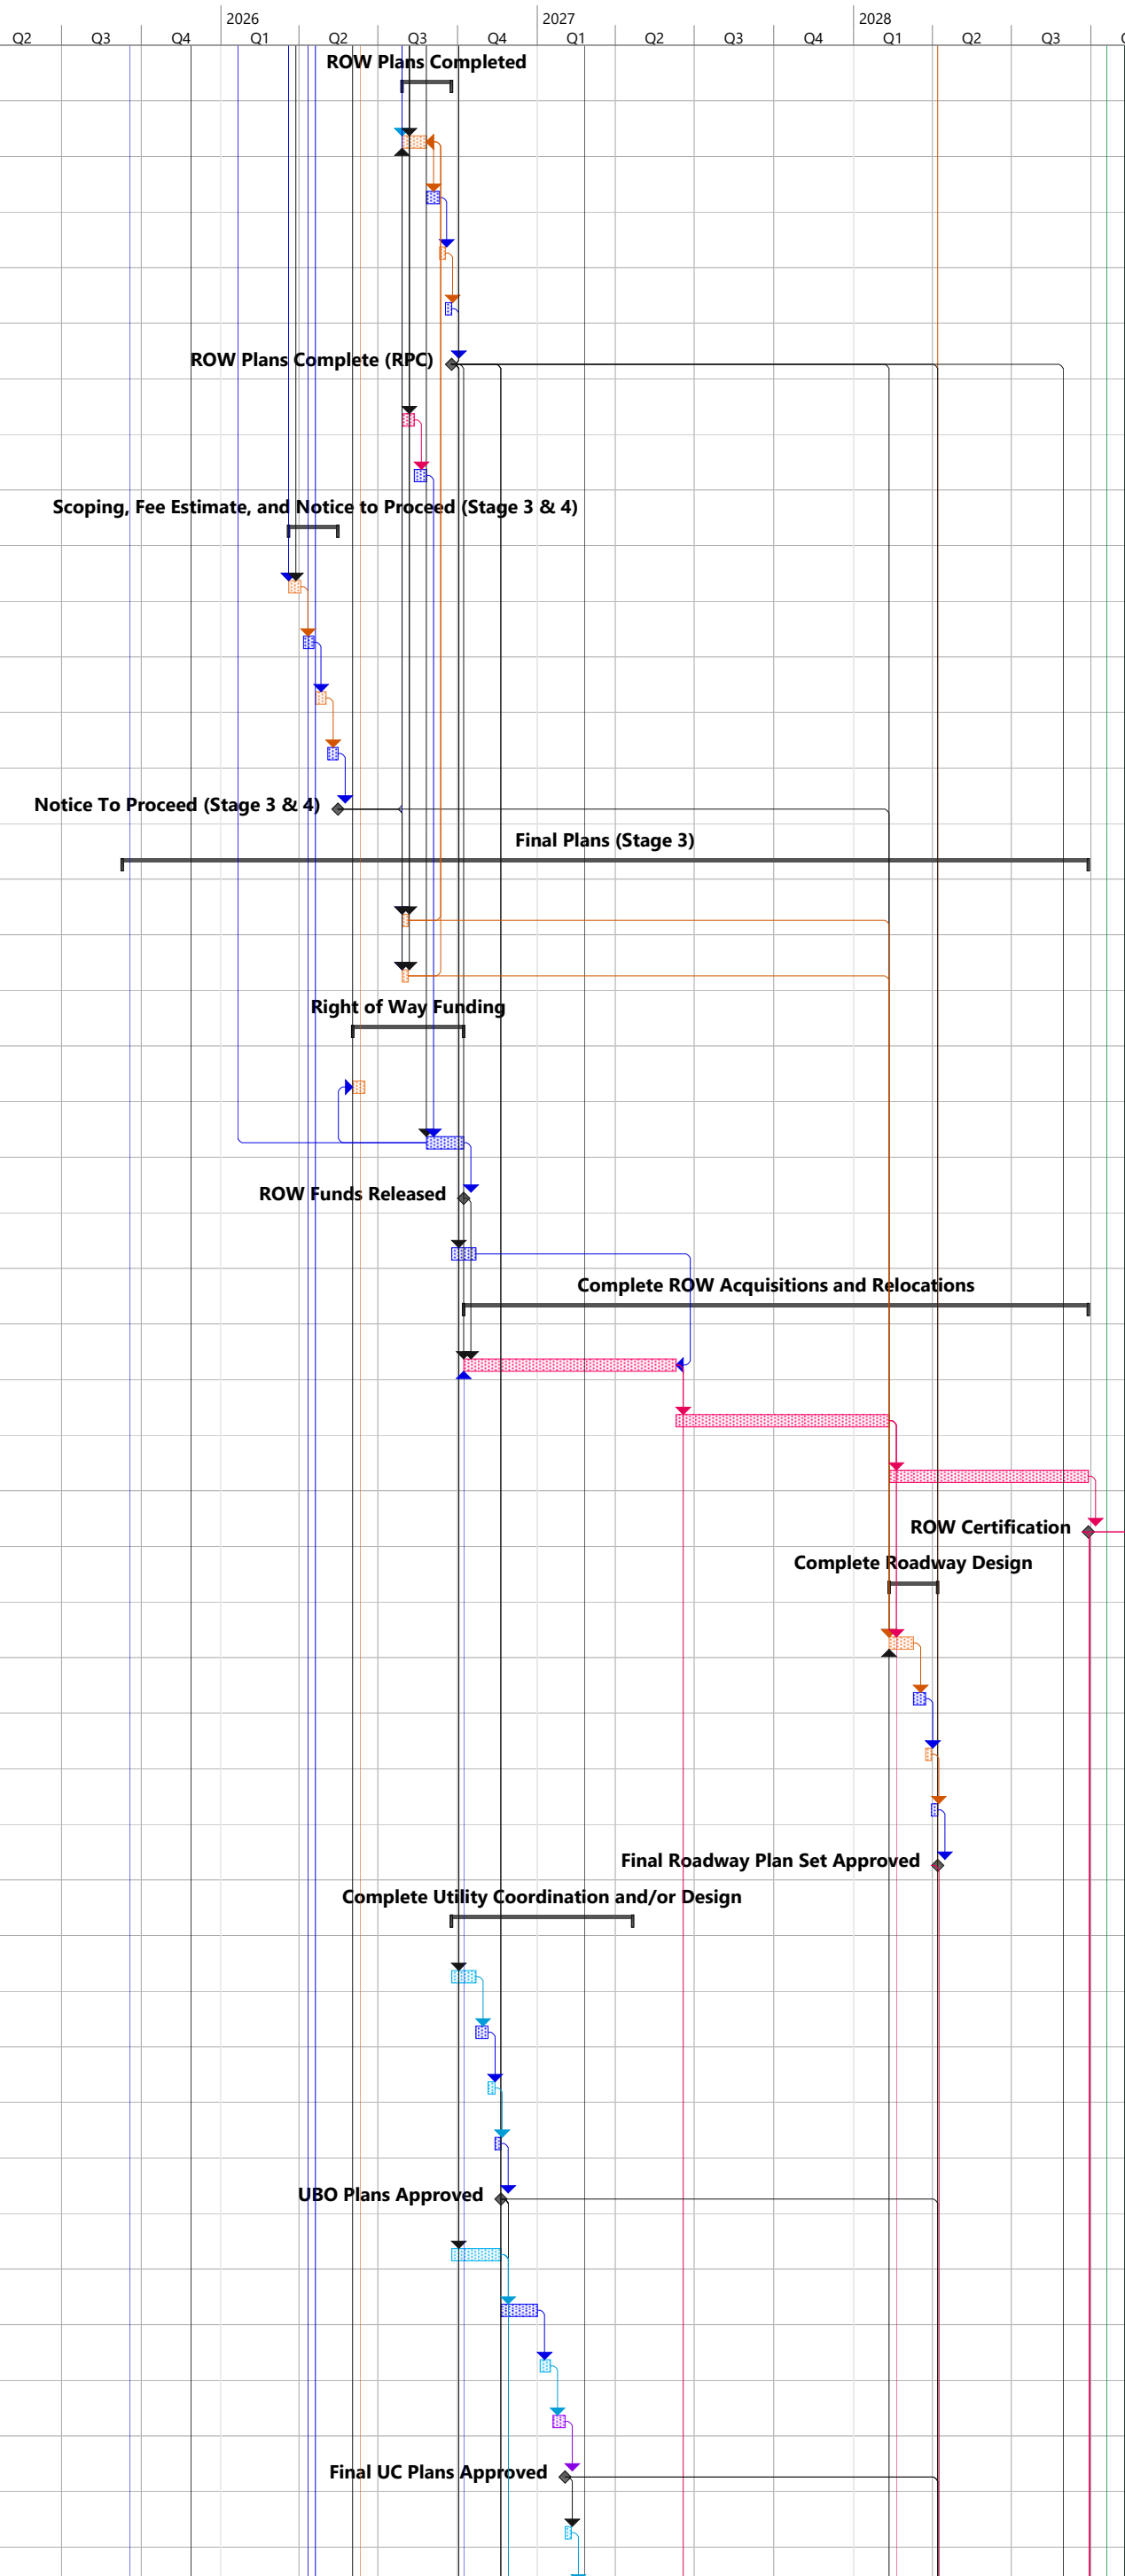

Project: NCDOT PDN Schedule Date: Wed 11/13/24

Task Split

Legend:


- Milestone (Blue diamond)
- Project Summary (Blue bar)
- Inactive Milestone (Grey diamond)
- Inactive Summary (Grey bar)
- Manual Task (Blue bar)
- Manual Summary Rollup (Blue bar)
- Manual Summary (Blue bar)
- Start-only (Blue bar)
- Finish-only (Blue bar)
- External Tasks (Blue bar)
- External Milestone (Blue diamond)
- Deadline (Grey bar)
- Progress (Blue bar)
- Manual Progress (Blue bar)

ID	Discipline Code	Task Code	SAP MLSN	Responsible Party	Task Name	Predecessors	Successors	Duration	Start	Finish	2024	2025	2026	2027	2028	2029							
											Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
369	UT	3UT1		AGENCY	Review of Final UC Plan Package	368	370	40 days	Tue 2/9/27	Tue 4/6/27													
370	UT	3UT1		UTILITY PEF	Revise & Resubmit Final UC Plan Package to Utility Owners	369	371	5 days	Wed 4/7/27	Tue 4/13/27													
371	UT	3UT1		AGENCY	Review of Revised Final UC Plan Package	370	372	5 days	Wed 4/14/27	Tue 4/20/27													
372	UT	3UT1		AGENCY	Issue Authorization to Construct	371	468,481,488	0 days	Tue 4/20/27	Tue 4/20/27													
373	UT	3UT2			Initiate Utility Relocations by Others			10 days	Fri 11/20/26	Thu 12/10/26													
374	UT	3UT2		UTILITY PEF	Update the Utilities Relocation Schedule	361	378,375	10 days	Fri 11/20/26	Thu 12/10/26													
375	UT	3UT2		NCDOT	Hold Relocation Scheduling Conference	374,377	453	0 days	Thu 12/10/26	Thu 12/10/26													
376	UT	3UT3			Prepare Final Utility Relocation and Construction Estimates			40 days	Fri 11/20/26	Mon 2/1/27													
377	UT	3UT3		UTILITY PEF	Prepare Utility Relocation and Construction Estimates	361	378,375	10 days	Fri 11/20/26	Thu 12/10/26													
378	UT	3UT3		NCDOT	Utility Relocation Funding Request	377,374	379	30 days	Fri 12/11/26	Mon 2/1/27													
379	UT	3UT3		NCDOT	Utility Relocation Funds Released	378	453	0 days	Mon 2/1/27	Mon 2/1/27													
380	GT	3GT			GeoEnvironmental and Subsurface Investigation			145 days	Tue 9/9/25	Fri 4/17/26													
381	GT	3GT1		NCDOT	Prepare GeoEnvironmental Phase II Report	238	459,346	40 days	Tue 9/9/25	Mon 11/3/25													
382	GT	3GT2		NCDOT	Verify Geotechnical Deliverables	240	409	10 days	Mon 4/6/26	Fri 4/17/26													
383	RE	3RE1			Complete Erosion and Sediment Control Plans			30 days	Fri 11/20/26	Fri 1/15/27													
384	RE	3RE1		PEF	Prepare & Submit Erosion Control Plan Package	328,361,362	385	10 days	Fri 11/20/26	Thu 12/10/26													
385	RE	3RE1		NCDOT	Review of Erosion Control Package	384	386	10 days	Fri 12/11/26	Thu 12/31/26													
386	RE	3RE1		PEF	Revise & Resubmit Erosion Control Package	385	387	5 days	Mon 1/4/27	Fri 1/8/27													
387	RE	3RE1		NCDOT	Approve Erosion Control Package	386	388	5 days	Mon 1/11/27	Fri 1/15/27													
388	RE	3RE1		NCDOT	Erosion Control Package Approved	387	404,444,462	0 days	Fri 1/15/27	Fri 1/15/27													
389	HY	3HY1			Complete Hydraulic Permitting Tasks and Finalize Plans			30 days	Fri 11/20/26	Fri 1/15/27													
390	HY	3HY1		PEF	Prepare & Submit Permit Drawing Package	328,361,362	391	10 days	Fri 11/20/26	Thu 12/10/26													
391	HY	3HY1		NCDOT	Review of Permit Drawing Package	390	392	10 days	Fri 12/11/26	Thu 12/31/26													
392	HY	3HY1		PEF	Revise & Resubmit Permit Drawing Package	391	393	5 days	Mon 1/4/27	Fri 1/8/27													
393	HY	3HY1		NCDOT	Approve Permit Drawing Package	392	394	5 days	Mon 1/11/27	Fri 1/15/27													
394	HY	3HY1		NCDOT	Permit Drawing Package Approved	393	404,444,461	0 days	Fri 1/15/27	Fri 1/15/27													
395	EN	3EN1			Document Noise Abatement Decision			60 days	Tue 2/16/27	Tue 5/11/27													
396	EN	3EN1		PEF	Prepare & Submit Draft Balloting Figures	305	397	10 days	Tue 2/16/27	Mon 3/1/27													
397	EN	3EN1		NCDOT	Review of Draft Balloting Figures	396	398	10 days	Tue 3/2/27	Mon 3/15/27													
398	EN	3EN1		PEF	Revise & Resubmit Final Balloting Figures	397	399	10 days	Tue 3/16/27	Tue 3/30/27													
399	EN	3EN1		NCDOT	Review of Final Balloting Figures	398	400	10 days	Wed 3/31/27	Tue 4/13/27													
400	EN	3EN1		NCDOT	Final Balloting Figures Approved	399	401	0 days	Tue 4/13/27	Tue 4/13/27													
401	EN	3EN1		NCDOT	Public Input from Final Balloting Figures	400	402	20 days	Wed 4/14/27	Tue 5/11/27													
402	EN	3EN1		NCDOT	Final Noise Wall Determination	401	468,441,351,4	0 days	Tue 5/11/27	Tue 5/11/27													
403	EN	3EN2			Complete Permit Application Package			65 days	Tue 1/19/27	Tue 4/20/27													
404	EN	3EN2		PEF	Prepare & Submit Permit Application Package	388,394	405	10 days	Tue 1/19/27	Mon 2/1/27													
405	EN	3EN2		NCDOT	Review of Permit Application Package	404	406	10 days	Tue 2/2/27	Mon 2/15/27													
406	EN	3EN2		PEF	Revise & Submit Permit Application Package	405	407	5 days	Tue 2/16/27	Mon 2/22/27													
407	EN	3EN2		AGENCY	Review of Permit Application Package	406	448	40 days	Tue 2/23/27	Tue 4/20/27													
408	ST	3ST1			Complete Structures Design			140 days	Mon 4/20/26	Wed 11/4/26													
409	ST	3ST1		PEF	Prepare & Submit Final (Unsealed) Structure Plans	195,382	410	120 days	Mon 4/20/26	Wed 10/7/26													
410	ST	3ST1		NCDOT	Review of Final (Unsealed) Structure Plans	409	456	20 days	Thu 10/8/26	Wed 11/4/26													
411	SG	3SG1			Complete Signal & ITS Design			180 days	Thu 1/13/28	Thu 9/28/28													
412	SG	3SG1		PEF	Prepare & Submit 1st Signal Submittal (Temporary Poles and Geometrics)	413SF	420SS	40 days	Thu 1/13/28	Fri 3/10/28													
413	SG	3SG1		NCDOT	Review of 1st Submittal	414SF	412SF	20 days	Fri 3/10/28	Fri 4/7/28													
414	SG	3SG1		PEF	Revise & Submit 2nd Signal Submittal (Include Wiring)	415SF,317	413SF	40 days	Fri 4/7/28	Tue 6/6/28													


Project: NCDOT PDN Schedule Date: Wed 11/13/24

■ Task Split
■ Milestone Summary
◆ Project Summary
◆ Inactive Task
■ Inactive Milestone Summary
■ Inactive Summary
■ Manual Task
■ Manual Summary Rollup
■ Manual Summary
■ Start-only
■ Finish-only
■ External Tasks
■ External Milestone
■ Deadline
■ Progress
■ Manual Progress

ID	Discipline Code	Task Code	SAP MLSN	Responsible Party	Task Name	Predecessors	Successors	Duration	Start	Finish	Q4	2024 Q1	Q2	Q3	Q4	2025 Q1	Q2	Q3	Q4	2026 Q1	Q2	Q3	Q4	2027 Q1	Q2	Q3	Q4	2028 Q1	Q2	Q3	Q4	2029 Q1	Q2	Q3
415	SG	3SG1		NCDOT	Review of 2nd Submittal	416SF	414SF	20 days	Tue 6/6/28	Wed 7/5/28																								
416	SG	3SG1		PEF	Revise & Submit 3rd Signal Submittal (Final Plans)	417SF	415SF	40 days	Wed 7/5/28	Wed 8/30/28																								
417	SG	3SG1		NCDOT	Review of 3rd Submittal	418SF	416SF	20 days	Wed 8/30/28	Thu 9/28/28																								
418	SG	3SG1		NCDOT	Signal Plans Approved	468SF,481SF	417SF	0 days	Thu 9/28/28	Thu 9/28/28																								
419	SD	3SD1			Complete Signing and Delineation Design			180 days	Thu 1/13/28	Thu 9/28/28																								
420	SD	3SD1		PEF	Prepare 100% Unsealed Signing and Delineation Plans	412SS	421	40 days	Thu 1/13/28	Thu 3/9/28																								
421	SD	3SD1		NCDOT	Review of 100% Unsealed Submittal	420	422	10 days	Fri 3/10/28	Thu 3/23/28																								
422	SD	3SD1		PEF	Prepare 100% Sealed Signing and Delineation Plans	421,468SF,481SF		20 days	Wed 8/30/28	Thu 9/28/28																								
423	RR	3RR1			Finalize Railroad Design & Agreements			435 days	Wed 11/19/25	Thu 9/2/27																								
424	RR	3RR1		NCDOT	Prepare PE Agreement between NCDOT and Railroad	151	425	10 days	Wed 11/19/25	Tue 12/9/25																								
425	RR	3RR1		RAIL	Review of PE Agreement	424	426	60 days	Wed 12/10/25	Thu 3/12/26																								
426	RR	3RR1		NCDOT	PE Agreement between NCDOT and Railroad Signed	425	427	0 days	Thu 3/12/26	Thu 3/12/26																								
427	RR	3RR1		PEF	Hold Field Diagnostics Meeting with NCDOT and Railroad	166,313,426	428	10 days	Tue 6/2/26	Mon 6/15/26																								
428	RR	3RR1		PEF	Prepare & Submit Initial Planimetric for Railroad Signal and Gates	427	429	20 days	Tue 6/16/26	Tue 7/14/26																								
429	RR	3RR1		NCDOT	Review of Initial Planimetric for Railroad Signal and Gates	428	430	20 days	Wed 7/15/26	Tue 8/11/26																								
430	RR	3RR1		PEF	Prepare & Submit Final Planimetric for Railroad Signal and Gates	429	431	10 days	Wed 8/12/26	Tue 8/25/26																								
431	RR	3RR1		NCDOT	Review of Final Planimetric for Railroad Signal and Gates	430	432	10 days	Wed 8/26/26	Wed 9/9/26																								
432	RR	3RR1		RAIL	Review of Planimetric to Include Material Procurement	431	433	240 days	Thu 9/10/26	Thu 9/2/27																								
433	RR	3RR1		NCDOT	Planimetric and Material Procurement Complete	432	476FF,489FF	0 days	Thu 9/2/27	Thu 9/2/27																								
434	RR	3RR2			Complete Railroad Coordination			80 days	Thu 9/24/26	Mon 2/1/27																								
435	RR	3RR2		PEF	Prepare & Submit Railroad Encroachment Agreement	328	436	10 days	Thu 9/24/26	Wed 10/7/26																								
436	RR	3RR2		NCDOT	Review of Railroad Encroachment Agreement	435	437	10 days	Thu 10/8/26	Wed 10/21/26																								
437	RR	3RR2		RAIL	Review of Railroad Encroachment Agreement	436	438	60 days	Thu 10/22/26	Mon 2/1/27																								
438	RR	3RR2		NCDOT	Railroad Encroachment Agreement Signed	437	469,488,439	0 days	Mon 2/1/27	Mon 2/1/27																								
439	RR	3RR2		NCDOT	Railroad Certification	438	475,487	0 days	Mon 2/1/27	Mon 2/1/27																								
440	TM	3TM1		PEF	Complete Transportation Management Plan	468SF,328,481SF		20 days	Wed 8/30/28	Thu 9/28/28																								
441	CS	3CS1		PEF	Prepare Construction Estimate	475SF-260 days,328,366,402		10 days	Fri 4/7/28	Fri 4/21/28																								
442	PM	3PM2		NCDOT	15 Month Let Review Meeting	478FS-300 days,490FS-300		0 days	Tue 12/7/27	Tue 12/7/27																								
443	PM	3PM3			Design Complete Review Meeting			20 days	Fri 4/7/28	Fri 5/5/28																								
444	PM	3PM3		PEF	Finalize Design Completion Review Meeting Materials	355,361,366,388,445		10 days	Fri 4/7/28	Fri 4/21/28																								
445	PM	3PM3		NCDOT	Prepare for Completion Review Meeting	444	446	10 days	Mon 4/24/28	Fri 5/5/28																								
446	PM	3PM3		NCDOT	Conduct Design Complete Review Meeting	445	465	0 days	Fri 5/5/28	Fri 5/5/28																								
447		4			Plans, Specifications, and Estimates (PS&E)/Letting (Stage 4)			550 days	Fri 11/20/26	Mon 3/5/29																								
448	EN	4EN1		PEF	Secure Permits	407	468,453,454,4	0 days	Tue 4/20/27	Tue 4/20/27																								
449	EP	4EP1		NCDOT	Complete NEPA/SEPA Documentation	475FS-60 days,487FS-60		0 days	Thu 10/19/28	Thu 10/19/28																								
450	UT	4UT			Utility Relocation			530 days	Fri 11/20/26	Mon 2/5/29																								
451	UT	4UT1		UTILITY OWNERS	Finalize Utility Coordination and/or Utility Design PS&E	361	453,452	20 days	Fri 11/20/26	Thu 12/31/26																								
452	UT	4UT1		NCDOT	Utility Certification	451	475,487	0 days	Thu 12/31/26	Thu 12/31/26																								
453	UT	4UT2		UTILITY OWNERS	Complete Utility Relocation by Owner [Phase 1]	451,448,379,346,478FF,490FF		240 days	Thu 6/10/27	Mon 6/5/28																								
454	UT	4UT2		UTILITY OWNERS	Complete Utility Relocation by Owner [Phase 2] [Tentative Beyond Let]	448,347	476FF,489FF	240 days	Fri 2/11/28	Mon 2/5/29																								
455	ST	4ST1			Finalize Structures Design PS&E			20 days	Wed 8/30/28	Thu 9/28/28																								
456	ST	4ST1		PEF	Submit Final (Sealed) Structure Plans	457SF,410		10 days	Wed 8/30/28	Thu 9/14/28																								
457	ST	4ST1		NCDOT	Review of Final (Sealed) Structure Plans	458SF	456SF	10 days	Thu 9/14/28	Thu 9/28/28																								
458	ST	4ST1		NCDOT	Structure Plans Approved	468SF,481SF	457SF	0 days	Thu 9/28/28	Thu 9/28/28																								
459	GT	4GT1		NCDOT	Manage GeoEnvironmental Impacts	468SF,381,481SF		20 days	Wed 8/30/28	Thu 9/28/28																								
460	LS	4LS1		NCDOT	Complete ROW Acquisition Surveys	349	471FF,483FF	30 days	Thu 9/28/28	Wed 11/8/28																								

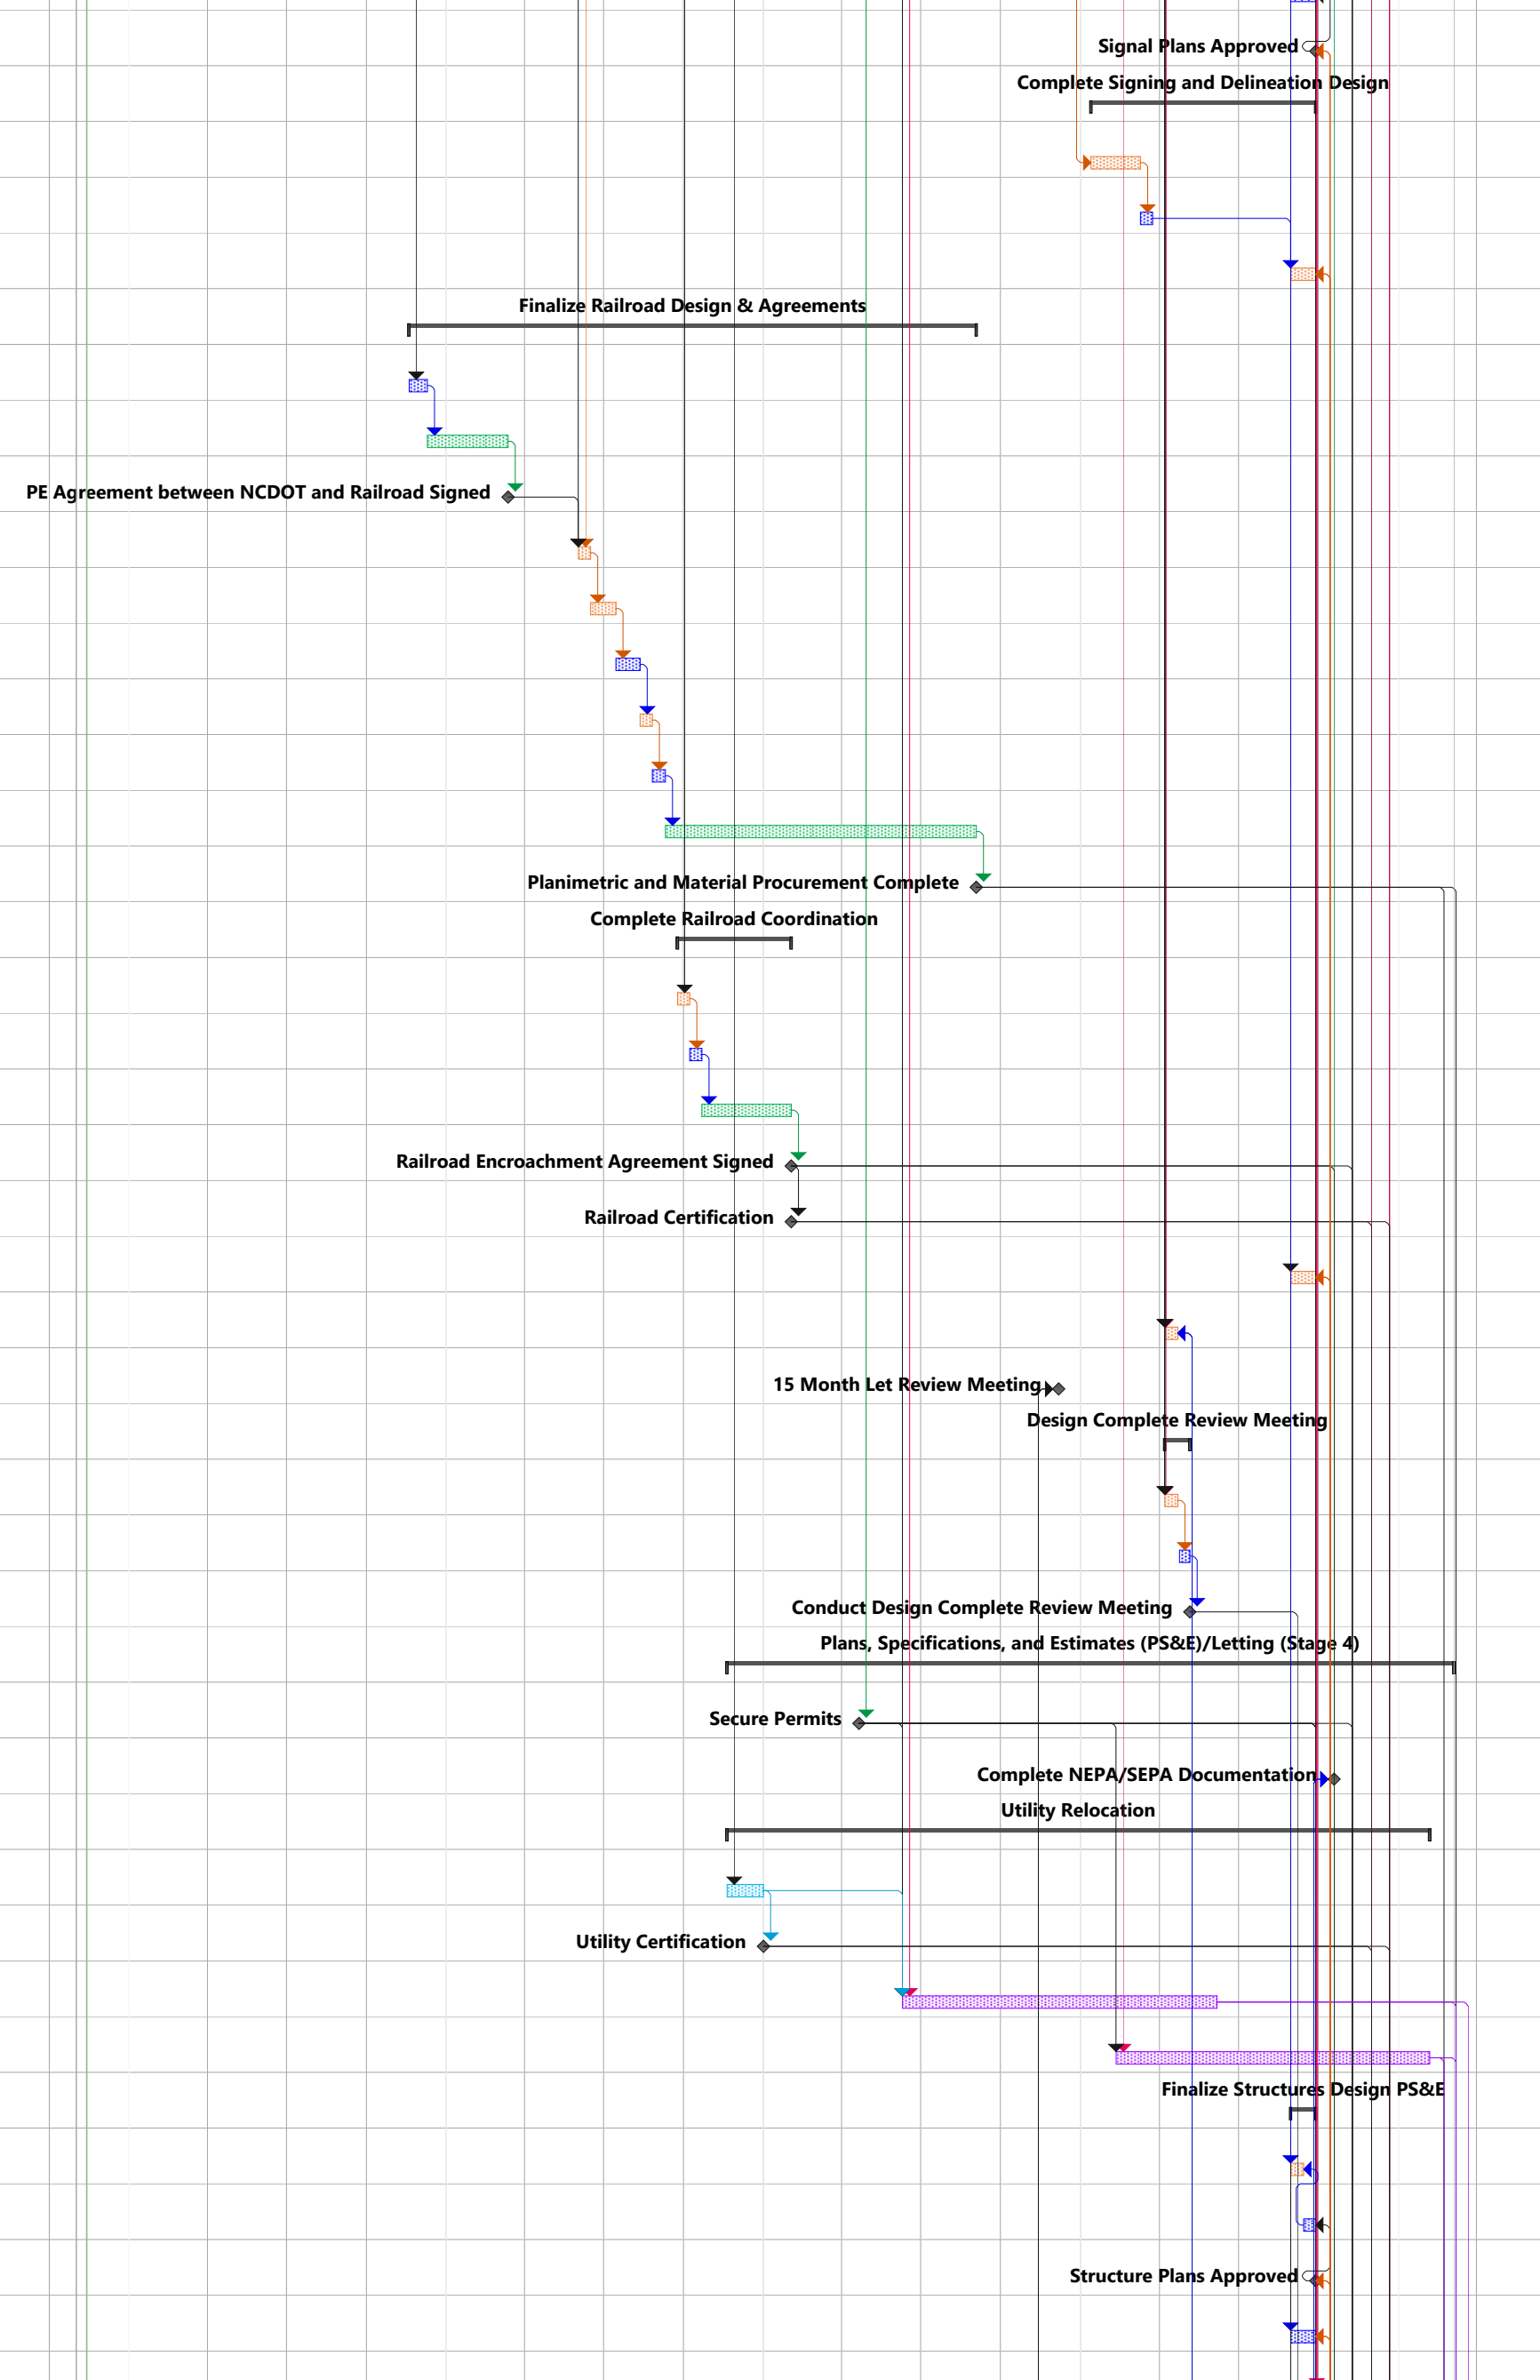

ID	Discipline Code	Task Code	SAP MLSN	Responsible Party	Task Name	Predecessors	Successors	Duration	Start	Finish	2024	2025	2026	2027	2028	2029						
											Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
461	HY	4HY1		PEF	Hydraulic Let Preparation	468SF,394,481SF		20 days	Wed 8/30/28	Thu 9/28/28												
462	RE	4RE1		PEF	Finalize Erosion & Sediment Control Contract Package	468SF,388,481SF		20 days	Wed 8/30/28	Thu 9/28/28												
463	CG	4CG1		NCDOT	Prepare Construction Communication Activities	468SF,481SF		20 days	Wed 8/30/28	Thu 9/28/28												
464	VM	4VM1		NCDOT	Complete Value Management Activities	468SF,481SF		20 days	Wed 8/30/28	Thu 9/28/28												
465	PM	4PM2		NCDOT	PS&E Review Meeting	469FS-30 days,446,482FS-3		0 days	Thu 9/14/28	Thu 9/14/28												
466					Central Let Activities			100 days	Thu 9/28/28	Mon 3/5/29												
467	RD	4RD1			Finalize the PS&E Package			55 days	Thu 9/28/28	Thu 12/21/28												
468	RD	4RD1		PEF	Submit 100% Unsealed Plans, Quantities, and Special Provisions	448,402,372,349	458SF,418SF,4	20 days	Thu 9/28/28	Wed 10/25/28												
469	RD	4RD1	MLSN	PEF	Roadway Plans to Contracts & Proposals (RPCP)	468,168,438	470,465FS-30 days	0 days	Wed 10/25/28	Wed 10/25/28												
470	RD	4RD1		NCDOT	Review of 100% Unsealed Plans, Quantities and Special Provisions	469	471	20 days	Thu 10/26/28	Thu 11/30/28												
471	RD	4RD1		PEF	Revise & Resubmit 100% Unsealed Plans, Quantities and Special Provisions	460FF,470	472	10 days	Fri 12/1/28	Thu 12/14/28												
472	RD	4RD1		NCDOT	Review of Revised 100% Unsealed Plans, Quantities and Special Provisions	471	473	5 days	Fri 12/15/28	Thu 12/21/28												
473	RD	4RD1	MLSN	PEF	Submit 100% Sealed Plans, Quantities, and Special Provisions	472	475	0 days	Thu 12/21/28	Thu 12/21/28												
474	CS	4CS1			Complete PS&E Package and Advertise the Project			45 days	Fri 12/22/28	Mon 3/5/29												
475	CS	4CS1		NCDOT	Construction Funding Request and Project Authorization	473,349,311,439,476,441SF-26	449FS-60	15 days	Fri 12/22/28	Mon 1/22/29												
476	CS	4CS1	MLSN	NCDOT	Advertise Project	475,433FF,454FF	477	0 days	Mon 2/5/29	Mon 2/5/29												
477	CS	4CS1		NCDOT	Project Advertisement	476	478	20 days	Tue 2/6/29	Mon 3/5/29												
478	CS	4CS2	M0550	NCDOT	Central Let	453FF,477	442FS-300 days	0 days	Mon 3/5/29	Mon 3/5/29												
479					Division Let Activities			90 days	Thu 9/28/28	Mon 2/19/29												
480	RD	4RD1			Finalize the PS&E Package			30 days	Thu 9/28/28	Wed 11/8/28												
481	RD	4RD1		PEF	Submit 100% Unsealed Plans, Quantities, and Special Provisions	448,402,372,349	482,458SF,418	10 days	Thu 9/28/28	Wed 10/11/28												
482	RD	4RD1		NCDOT	Review of 100% Unsealed Plans, Quantities and Special Provisions	481	483,465FS-30 days	10 days	Thu 10/12/28	Wed 10/25/28												
483	RD	4RD1		PEF	Revise & Submit 100% Sealed Plans, Quantities and Special Provisions	482,460FF	484	10 days	Thu 10/26/28	Wed 11/8/28												
484	RD	4RD1		PEF	Submit 100% Sealed Plans, Quantities, and Special Provisions	483	486,488	0 days	Wed 11/8/28	Wed 11/8/28												
485	CS	4CS1			Complete PS&E Package and Advertise the Project			60 days	Thu 11/9/28	Mon 2/19/29												
486	CS	4CS1		NCDOT	Update Construction Estimate Pricing	484	487	10 days	Thu 11/9/28	Thu 11/30/28												
487	CS	4CS1		NCDOT	Construction Funding Request and Project Authorization	486,349,311,439,489,441SF-26	449FS-60	35 days	Fri 12/1/28	Mon 1/29/29												
488	CS	4CS1		NCDOT	Complete PS&E Package	168,438,448,484,489		15 days	Thu 11/9/28	Thu 12/7/28												
489	CS	4CS1		NCDOT	Project Advertisement	487,488,433FF,45490		15 days	Tue 1/30/29	Mon 2/19/29												
490	CS	4CS2		NCDOT	Division POC Let (DPOC)	489,453FF	442FS-300 days	0 days	Mon 2/19/29	Mon 2/19/29												

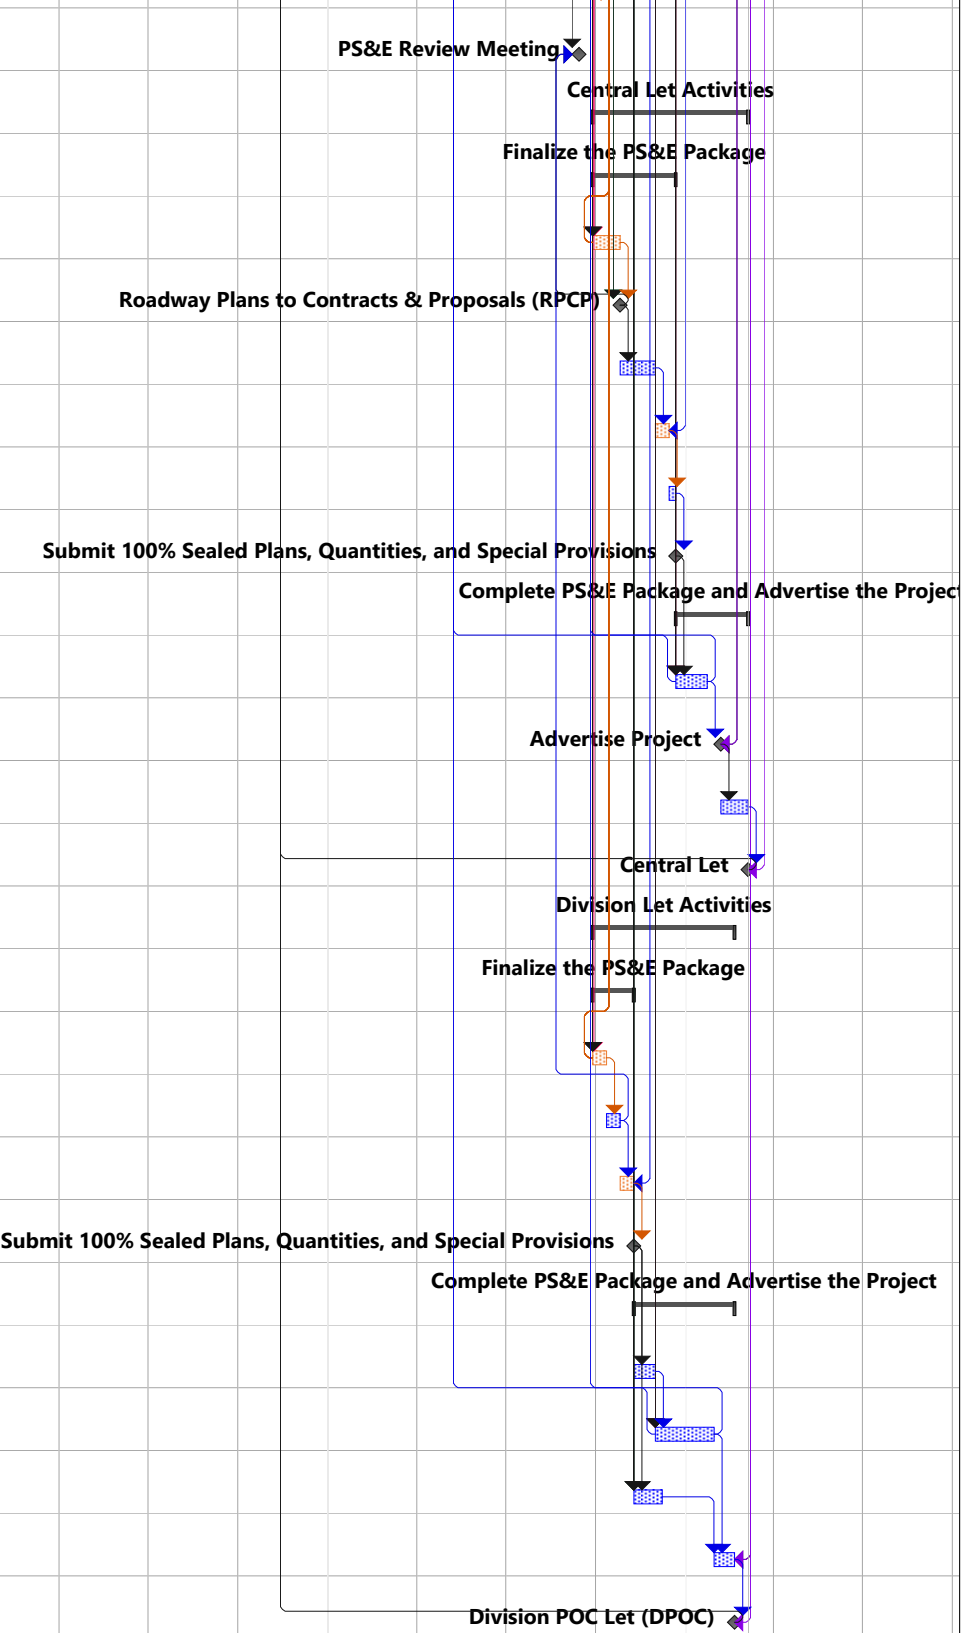

Project: NCDOT PDN Schedule Date: Wed 11/13/24

Task Split	Milestone	Project Summary	Inactive Milestone	Manual Task	Manual Summary Rollup	Start-only	External Tasks	Deadline	Manual Progress
	Summary	Inactive Task	Inactive Summary	Duration-only	Manual Summary	Finish-only	External Milestone	Progress	
