


# Candidate Project: Systems Planning to Programming



DATE: August 31, 2021

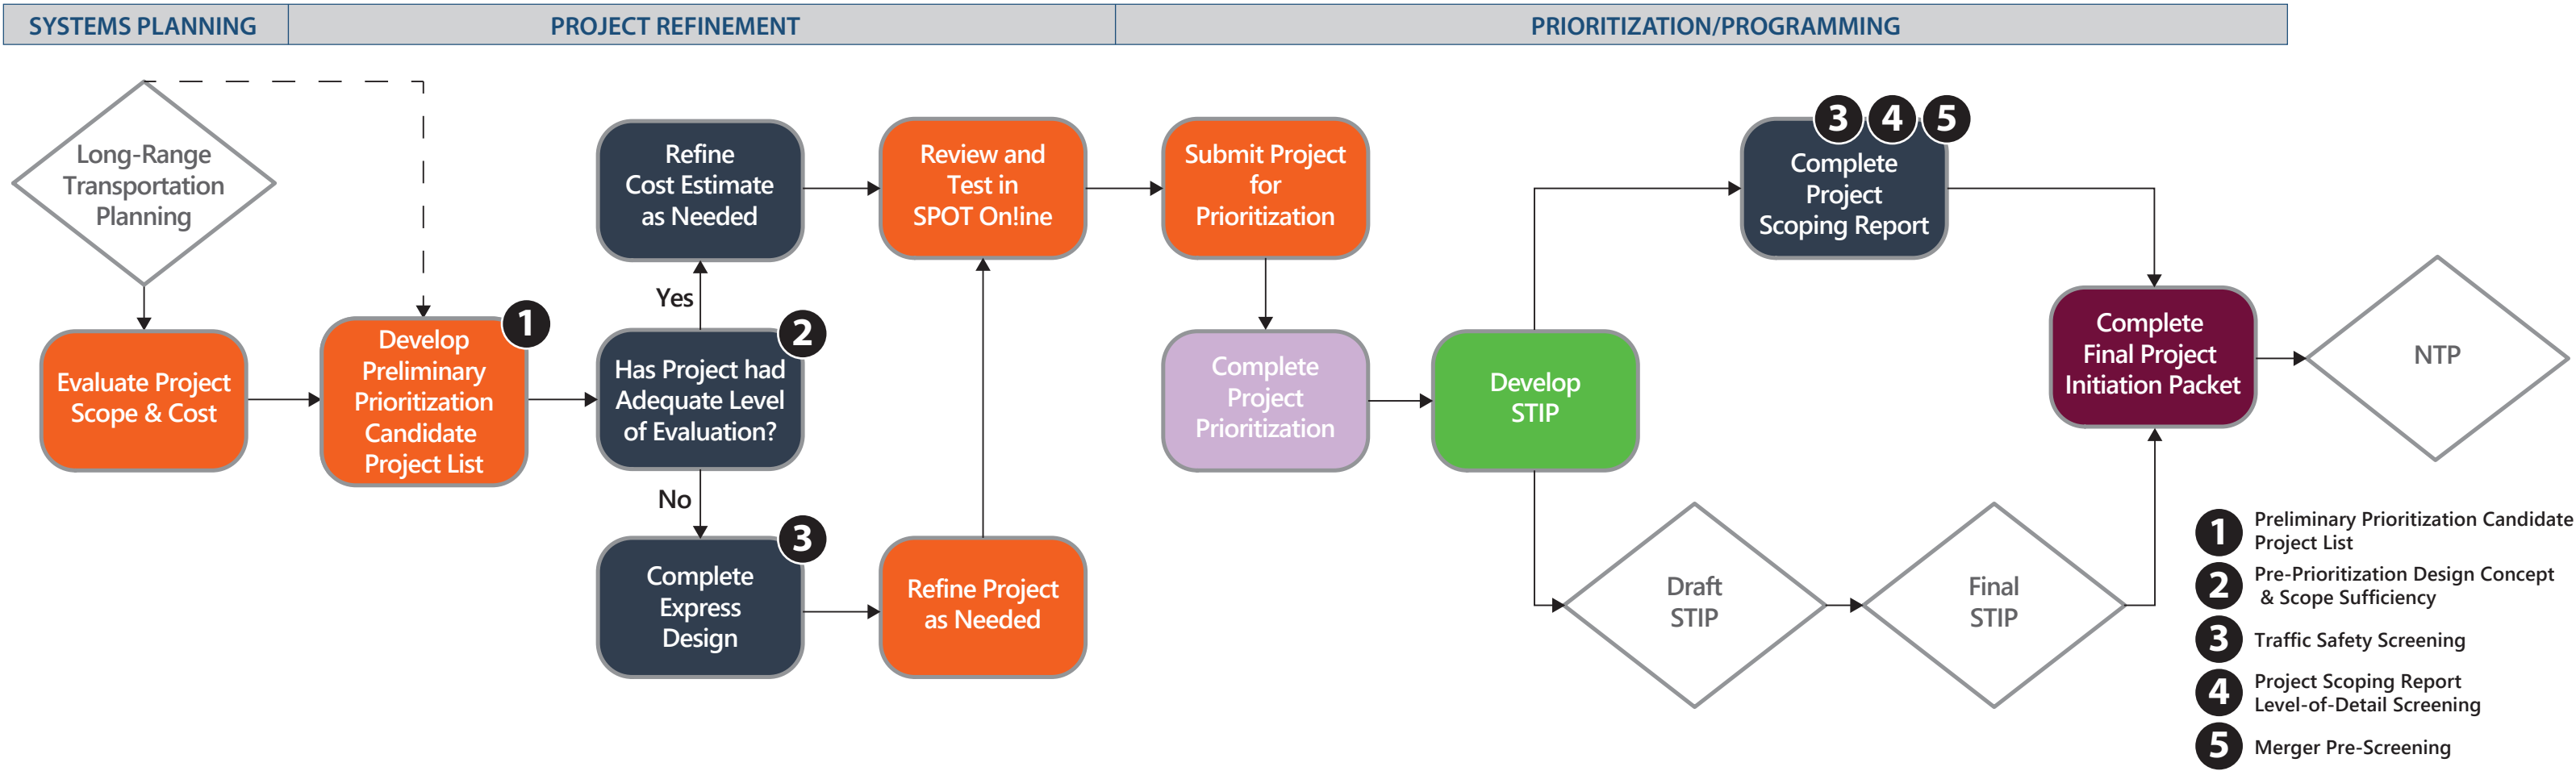

- 1** Preliminary Prioritization Candidate Project List
- 2** Pre-Prioritization Design Concept & Scope Sufficiency
- 3** Traffic Safety Screening
- 4** Project Scoping Report Level-of-Detail Screening
- 5** Merger Pre-Screening

	Evaluate Project Scope & Cost	Develop Preliminary Prioritization Candidate Project List	Has Project had Adequate Level of Evaluation?	Complete Express Design	Refine Cost Estimate as Needed	Refine Project as Needed	Review and Test in SPOT Online	Submit Project for Prioritization	Complete Project Prioritization	Develop STIP	Complete Project Scoping Report	Complete Final Project Initiation Packet
Division Corridor Development Engineer	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	LEAD
Division Planning Engineer	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT
Corridor Development/Feasibility Studies Unit	SUPPORT	SUPPORT	LEAD	LEAD	LEAD	SUPPORT			SUPPORT	SUPPORT	LEAD	SUPPORT
Project Manager											SUPPORT	SUPPORT
Project Sponsor (MPO, RPO, Division - DPE)	LEAD	LEAD	SUPPORT	SUPPORT	SUPPORT	LEAD	LEAD	LEAD	SUPPORT		SUPPORT	SUPPORT
State Transportation Improvement Program Unit		SUPPORT								LEAD		
Strategic Prioritization Office of Transportation		SUPPORT					SUPPORT	SUPPORT	LEAD	SUPPORT		
Transportation Planning Division	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT	SUPPORT			SUPPORT	SUPPORT
