


Project: NCDOT PDN 2 Schedu Date: Mon 10/5/20	Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split	
	Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
	Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress	

ID	WBS	Discipline Code	Task Code	SAP MLSN	Task Name	Predecessor	% Complete	Duration	Oct 11, '20							Oct 18, '20							Oct 25, '20														
									T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F						
52	4.17	EN	3EN1		Complete Permit, Commitments, and Design Noise Report	34	0%	1 day																													
53	4.18	EN	3EN2		Determine Final Noise Abatement	52	0%	1 day																													
54	4.19	VM	3VM1		Complete Value Engineering	34	0%	1 day																													
55	4.20	VM	3VM2		Conduct Risk Management	34	0%	1 day																													
56	4.21	CS	3CS1		Prepare Plan-in-Hand Estimates	38,40,41	0%	1 day																													
57	5	MLSN	MLSN	M1007	Design Complete & All Permit Applications Submitted	56	0%	0 days																													
58	6		4		Plans, Specifications, and Estimates (Stage 4)		0%	4 days																													
59	6.1	RW	4RW1		Complete ROW Acquisitions and Relocations	57	0%	1 day																													
60	6.2	GT	4GT1		Prepare GeoEnvironmental Phase III Reports	57	0%	1 day																													
61	6.3	ST	4ST1		Finalize Structures Design PS&E	57	0%	1 day																													
62	6.4	LS	4LS1		Complete ROW Acquisition Surveys	57	0%	1 day																													
63	6.5	HY	4HY1		Complete Any Open Hydraulic Tasks	57	0%	1 day																													
64	6.6	UT	4UT1		Complete Utility Coordination	57	0%	1 day																													
65	6.7	UT	4UT2		Complete Utility Relocation by Owner	57	0%	1 day																													
66	6.8	TO	4TO1		Complete Transportation Operations Plan-Related Tasks (if a	57	0%	1 day																													
67	6.9	SS	4SS1		Signal Timing Implementation (if not a Significant Project)	57	0%	1 day																													
68	6.10	EN	4EN1		Secure Environmental Permits	57	0%	1 day																													
69	6.11	RR	4RR1		Complete Railroad Coordination	57	0%	1 day																													
70	6.12	CG	4CG1		Prepare Construction Communication Activities	57	0%	1 day																													
71	6.13	RD	4RD1		Finalize Contract Package	59,60,61	0%	1 day																													
72	6.14	MLSN	MLSN	M1008	PS&E Submittal	71	0%	0 days																													
73	6.15	CS	4CS1		Complete CS&D Project Review	72	0%	1 day																													
74	6.16				Post-Letting Activities	73	0%	1 day																													

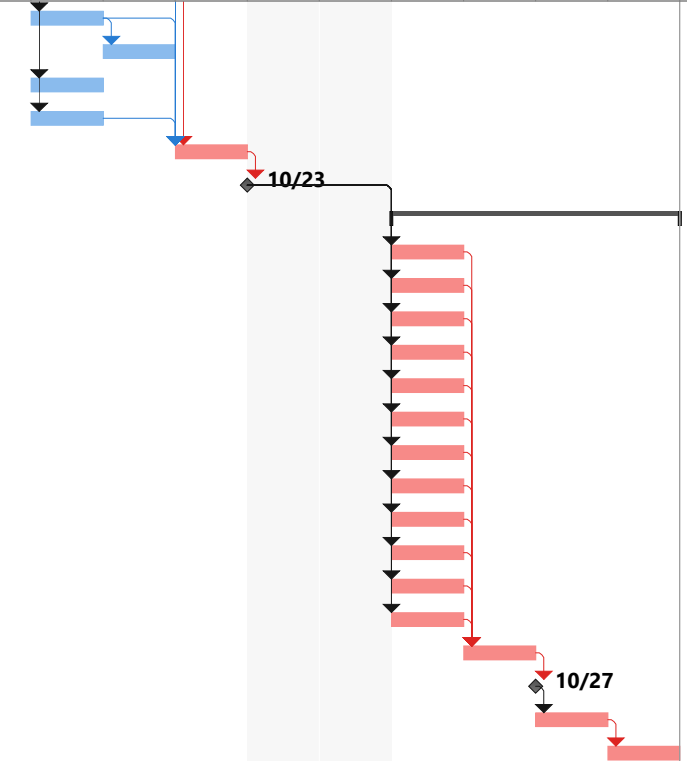

Project: NCDOT PDN 2 Schedu Date: Mon 10/5/20	Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split	
	Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
	Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress	
